


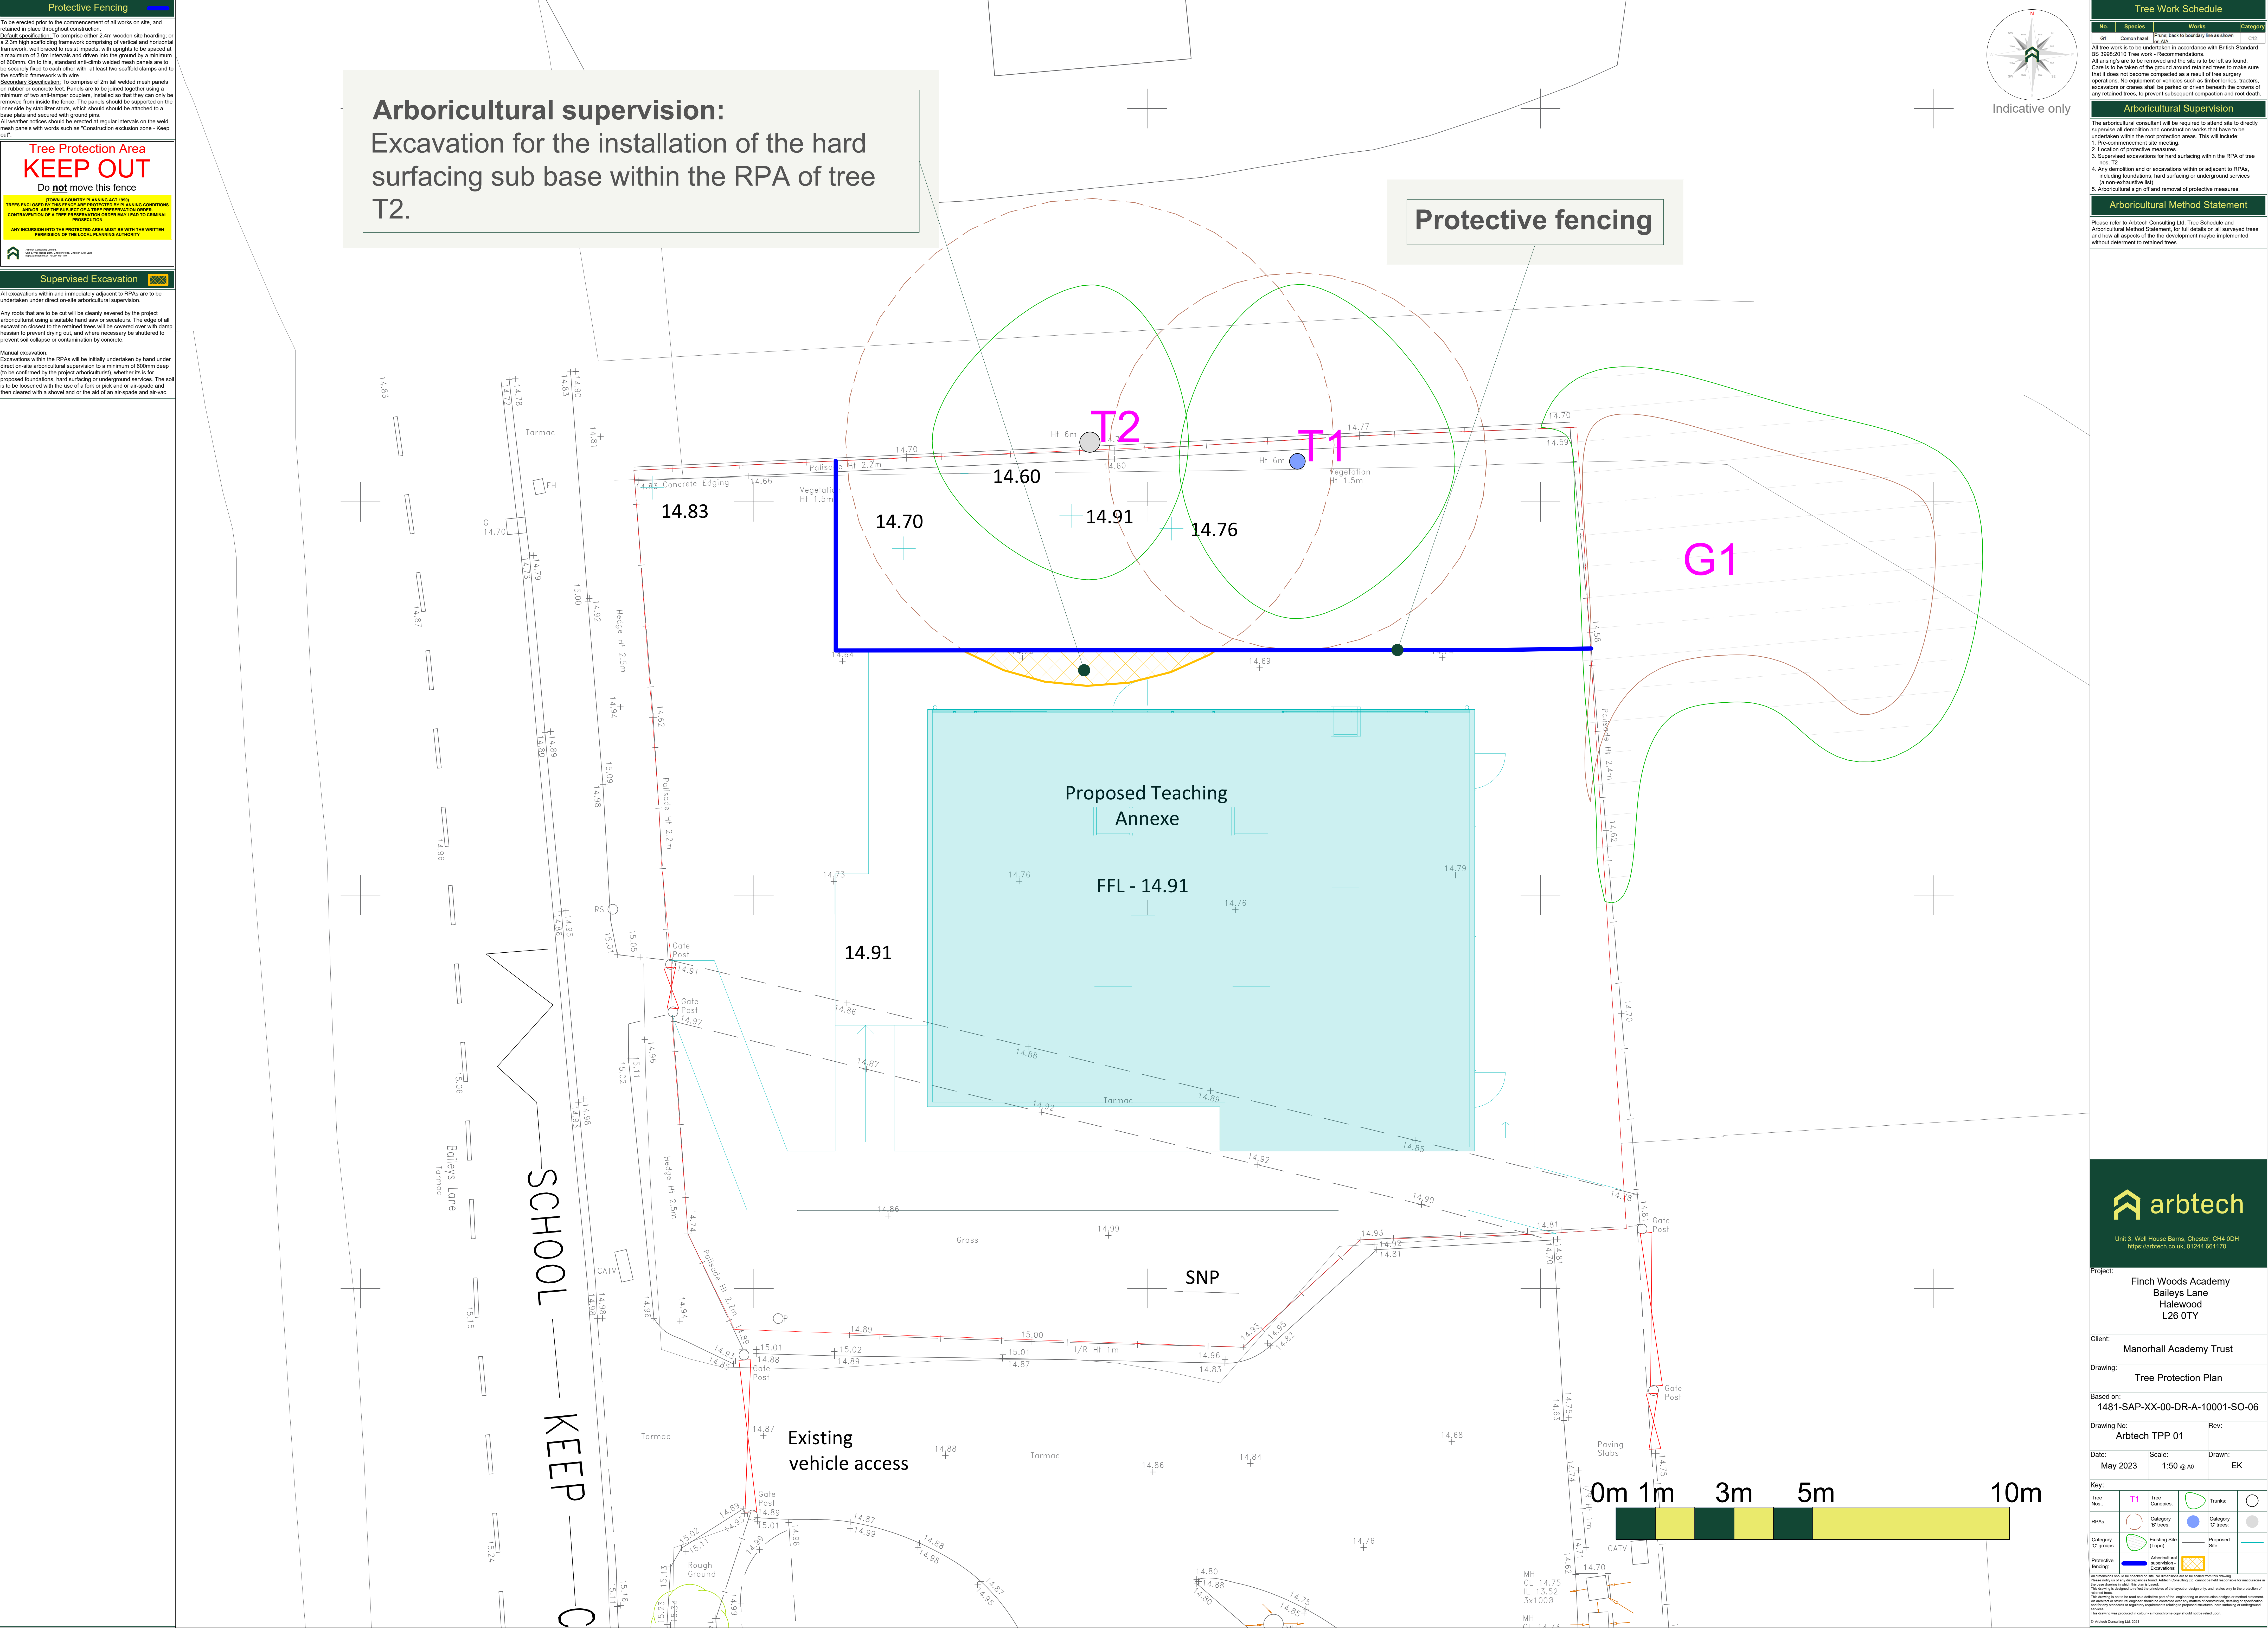

Tree Work Schedule			
No.	Species	Works	Category
G1	Common hazel	Prune back to boundary line as shown	C12
All tree work is to be undertaken in accordance with British Standard BS 3998:2010 Tree work - Recommendations.			
All stumps are to be removed and the site is to be left as found. Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of tree surgery operations. No equipment or vehicles such as timber lorries, tractors, excavators or cranes shall be parked or driven beneath the crowns of any retained trees, to prevent subsequent compaction and root death.			
Arboricultural Supervision			
The arboricultural consultant will be required to attend site to directly supervise all demolition and construction works that have to be undertaken within the root protection areas. This will include: 1. Pre-commencement site meeting. 2. Location of protective measures. 3. Supervised excavations for hard surfacing within the RPA of tree zone T2. 4. Any demolition and or excavations within or adjacent to RPAs, including foundations, hard surfacing or underground services (as non-exhaustive list). 5. Arboricultural sign off and removal of protective measures.			
Arboricultural Method Statement			
Please refer to Arbtch Consulting Ltd. Tree Schedule and Arboricultural Method Statement, for full details on all surveyed trees and how all aspects of the site development maybe implemented without detriment to retained trees.			

Protective Fencing
To be erected prior to the commencement of all works on site, and retained in place throughout construction.
Default specification: To comprise either 2.4m wooden site boarding or a 2.5m high scaffolding framework comprising of vertical and horizontal framework, well braced to resist impacts, with uprights to be spaced at a maximum of 3.0m intervals and driven into the ground to a minimum of 600mm. On to this, standard anti-climb welded mesh panels are to be securely fixed to each other with at least two scaffold clamps and to the scaffold framework with wire.
Secondary Specification: To comprise of 2m tall welded mesh panels on rubber or concrete feet. Panels are to be joined together using a minimum of two anti-tamper couplers, installed so that they can only be removed from inside the fence. The panels should be supported on the inner side by stabilizer struts, which should be attached to a base plate and secured with ground pins.
All weather notices should be erected at regular intervals on the weld mesh panels with words such as "Construction exclusion zone - Keep out".

Tree Protection Area
KEEP OUT
Do not move this fence
(TOWN & COUNTRY PLANNING ACT 1990)
TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY PLANNING CONDITIONS AND ARE THE SUBJECT OF A TREE PRESERVATION ORDER.
ANY INCURSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN PERMISSION OF THE LOCAL PLANNING AUTHORITY

Supervised Excavation
All excavations within and immediately adjacent to RPAs are to be undertaken under direct on-site arboricultural supervision.
Any roots that are to be cut will be clearly severed by the project arboricultural using a suitable hand saw or secateurs. The edge of all excavation closest to the retained trees will be covered over with damp hessian to prevent drying out, and where necessary be shored to prevent soil collapse or contamination by concrete.
Manual excavation: Excavations within the RPAs will be initially undertaken by hand under direct on-site arboricultural supervision to a minimum of 600mm deep (to be confirmed by the project arboricultural), whether its for proposed foundations, hard surfacing or underground services. The soil is to be loosened with the use of a fork or pick and/or air-spade and then cleared with a shovel and/or the aid of an air-spade and air-vac.
