



Remediation and Enabling Works Strategy
Land South of Lickers Lane, Whiston

Reference: 15-065-R3-1
Date: August 2022



REMEDIATION AND ENABLING WORKS STRATEGY

Land south of Lickers Lane
Whiston
Prescot
L35 3JE

Prepared for:



Report Ref: 15-065-R3-1
Date Issued: August 2022



E3P

Taylor Road
Trafford Park
Urmston
Manchester
M41 7JQ

+ 44 (0) 161 707 9612
<https://e3p.co.uk>

Registered in England
CRN: 08725262

QUALITY ASSURANCE

PROJECT NUMBER	15-065		
VERSION	Version 1		
REMARKS	Issue 1		
DATE	August 2022		
PREPARED BY	N. Sellars		
QUALIFICATIONS	MSci (Hons), FGS, MIEnvSc		
CHECKED BY	R. Horseman		
QUALIFICATIONS	BSc (Hons), CEnv, FGS		
AUTHORISED BY	M. Dyer		
QUALIFICATIONS	BSc, FGS, AIEMA, AMI CEnv		

EXECUTIVE SUMMARY

Site Address	Land south of Lickers Lane, Whiston, Prescot, L35 3JE
National Grid Reference	E 347490, N 390400
Site Area	2.55 Ha.
Background	E3P has been instructed by Vistry Partnerships to develop a remediation and enabling works strategy for the proposed residential development at the site located to the south of Lickers Lane in Whiston. The E3P Remediation and Enabling Earthworks Strategy has been produced in due consideration of the geoenvironmental site investigation and contaminated land assessments previously undertaken by E3P.

CONTAMINATED LAND RISK ASSESSMENT

Human Health Risk Assessment	A Tier I human health risk assessment has been undertaken using the chemical analysis results of the soils and comparing them to the relevant Tier I criteria. This assessment has identified the presence of elevated benzo(a)anthracene, benzo(b)fluoranthene, benzo(a)pyrene and dibenzo(a,h)anthracene. All of the exceedances have been identified within TP115. All the identified elevated concentrations have primary exposure pathways related to dermal contact and ingestion, soil ingestion and consumption of homegrown produce. As all of the exceedance has been identified within one exploratory location they are considered to be an isolated hotspot, therefore during the enabling works, it is recommended the impacted Made Ground is excavated and placed within an area of low sensitivity. The Made Ground identified within TP115 is not considered suitable for use within the upper 300 mm of a residential garden given the presence of deleterious elements. It will therefore be necessary to place a minimum of 150 mm of sub-soil and 150 mm topsoil to constitute a 300 mm clean soil matrix within all areas of private gardens where Made Ground remains. Chemical analysis of topsoil and subsoil confirms the material is suitable for re-use within proposed gardens and public open spaces areas. It should be noted that further chemical analysis will be required to confirm soils are chemically suitable in line with intended re-use volumes. It should be noted that further investigation is required within the additional southern and eastern parcels to confirm no unacceptable risk to human health and controlled waters.
Controlled Waters Risk Assessment	The Tier 1 Controlled Waters Risk Assessment has not identified any significant source of potential contamination or dissolved phase impact/leachate within the groundwater samples. The developed conceptual site model did not identify a potentially complete pollutant linkage and, as such, the site is deemed to pose no significant risk to controlled waters or the wider environ.
Ground Gas	Ground gas monitoring suggests that the site can be classified as CS1/Green, and it is considered that gas protection measures will not be required. Further assessment is required within the southern and eastern parcels.



Coal Mining and Historical Workings	In accordance with industry best practice as detailed within CIRIA 32, E3P has concluded that shallow mine workings are not present in the southwestern sector of the site. No evidence of workings or broken ground was identified as part of the intrusive investigation. Thus, the assessment has concluded that there is sufficient rock cover to provide the required degree of stability in the event of successive collapses (cavitation's) within potential workings beneath the site. It should be noted that further investigation may be required within the additional southern parcel of the site which is yet to be investigated.
Invasive Plants	A full invasive plant species survey should be instigated prior to the commencement of any enabling earthworks.
Potable Water Supply	This will need to be confirmed following the completion of a UKWIR risk assessment. Post-remediation and enabling works ground conditions may be different from those identified during this site investigation.

GEOTECHNICAL ASSESSMENT

Relict Sub-Structures	Due to the undeveloped nature of the site, there is not expected to be substantial underground obstructions present across the site.
Adverse Ground Conditions	All potentially infilled ponds and historical features where deleterious/putrescible material is identified should be located and subject to the necessary remediation works.
Proposed Foundations	At the time of writing, development levels are unknown, It is considered likely that the proposed structures will be founded on a combination of strip / trench fill type foundations where medium dense of firm clays are present at 1.00m bgl or found upon the sandstone bedrock present at the near-surface (<1.5 to 2.0m). Foundation depths within the conjectured influence of former, existing or proposed trees will need to be deepened to ensure that structural loading bears within the underlying target founding stratum, which cannot be subject to volumetric instability associated with fluctuation in moisture content within areas where clay deposits have been identified. Consideration must be given to the varying soil matrices and differing settlement characteristics and where a foundation spans two varying matrices the sub-structure should be designed accordingly.
Highways and Infrastructure	All proposed adopted roads will be constructed in accordance with the geotechnical engineering requirements as defined within the MCHW Series 600. Specific engineering and compaction of materials will be completed in strict accordance with the geotechnical specification contained within this report. All materials outside of structural/infrastructure development will be engineered and compacted to ensure consolidation associated with self-weight settlement is limited to < 50 mm in accordance with the E3P specification.

REMEDIATION AND ENABLING WORKS

Objectives	The remediation and enabling works will be delivered in a manner that will seek to ensure that the site is prepared to deliver the optimum foundation solution for the proposed structures, infrastructure and highways. The site remediation and enabling works strategy provides a comprehensive specification for the regeneration of the land to negate identified pollutant linkages and construct a development platform that will be geotechnically suitable for the proposed end use.
-------------------	---



Remediation and Enabling Works	The salient features of the remediation and enabling works strategy are summarised as follows: - Implementing of all works in strict accordance with UK Environmental Permitting and local planning authority requirements. - Controlled removal of all trees and vegetation. - Removal and treatment of all invasive plant species (as required) in accordance with specialist contractor method statement, validation and independent certification. - Recovery of natural topsoil. - Further site investigation to additional southern and eastern parcels. - Segregation of organic topsoil deemed unsuitable for use within a residential garden and placement in an area of no sensitivity or removal from site in accordance with UK waste management legislation. - Management of all anthropogenic material impacted by trace asbestos fibre in a controlled and legislatively compliant manner. - Removal of all materials considered geotechnically deleterious. - Excavation and processing of Made Ground in a controlled manner with the sorting, processing and segregation of identified deleterious materials to geotechnical specification. - Validation sampling and leachate testing to confirm material retained on site poses no unacceptable risk to the residential end users, controlled waters or wider environ. - Importation of suitable material (if required) to achieve the required development levels. - Replacement of material in accordance with the E3P enabling specification and engineering requirements.
---------------------------------------	--

BUILD PHASE REQUIREMENTS

Summary of Build-Phase Mitigation Requirements	The developer's works will also include the completion of the following additional elements: - Provision of a 300 mm growing medium using certified material with appropriate validation within proposed gardens, areas of public open space and soft landscaping. - Construction of appropriate potable water supply infrastructure.
---	--



TABLE OF CONTENTS

Land south of Lickers Lane	2
Whiston.....	2
Prescot.....	2
EXECUTIVE SUMMARY	1
1. INTRODUCTION	6
1.1. Background	6
1.2. Report Objectives	6
1.3. Scope of Works.....	6
1.4. Previous Works	6
1.5. Redevelopment Plan	7
1.6. Summary of Parties Involved.....	7
1.7. Regulatory Correspondence	8
1.8. Site Details	9
1.9. Site Summary.....	9
1.10. Summary of Reported Ground Conditions	10
2. E3P CONTAMINATION RISK ASSESSMENT	11
2.1. Background	11
2.2. Human Health Risk Summary	11
2.3. Controlled Waters Contamination Risk Summary	13
2.4. Ground Gas	13
2.5. Potable Water Supply Infrastructure	14
3. SITE REMEDIATION AND ENABLING WORKS	15
3.1. REMEDIATION OPTIONS APPRAISAL	15
3.2. Contaminants of Concern (CoC)	15
3.2.1. Metals, PAH, Non-Volatile Hydrocarbon (Petroleum Range) Compounds	15
3.2.2. Asbestos.....	15
3.3. Summary of Preferred Remediation Options.....	17
3.4. Overview of Works.....	17
3.5. Validation Sampling Protocol	25
3.6. Remediation Contractors Site Management and Responsibility	26
4. MATERIALS MANAGEMENT AND LEGISLATIVE COMPLIANCE	27
5. ENVIRONMENTAL MONITORING AND VALIDATION	28
5.1. Site Management	28
5.2. Completion.....	28
5.3. Mitigation of Risk from Soils with Asbestos Fibres	29
5.3.1. Pre-Commencement Works	29
5.3.2. Control, Monitoring and Reporting of General Aerial Emissions from Dusts and Particulates	29
6. GEOTECHNICAL ENGINEERING SPECIFICATION	32
6.1. E3P Geotechnical Engineering Specification.....	32
6.2. Locally-Won Fill Material	32
6.3. Classification of Fill Material	33
6.3.1. General Classification.....	33
6.3.2. Pre-Commencement Earthworks Testing Frequency / Performance.....	33
6.3.3. Use of Fill Materials	35
6.4. General Requirements.....	35
6.4.1. Construction of Fills – Highways.....	38
6.4.2. Construction of Fills – Adopted Highways, Estate Roads and Car Park	39
6.4.3. Unacceptable Material	39



6.5.	Earthworks Material Tests	41
6.6.	Specification for Ground Improvement by Vibro-Stone Column	41
6.7.	Current and Proposed Site Topography and Slope Interaction	43
7.	RECORD-KEEPING AND VERIFICATION.....	44
7.1.	Record-Keeping	44
7.2.	Verification.....	44
8.	CONTINGENCY PLAN	45
8.1.	Previously Unidentified Contaminants	45
9.	SECOND PHASE MITIGATION AND MANAGEMENT – BUILD PHASE.....	46
9.1.	Placement Of GROWING MEDIUM	46
9.1.1.	Procedure for Placement of Chemically Suitable Cover System	47
9.2.	Potable Water Supply – Contaminant Assessment Criteria	49
	APPENDIX I LIMITATIONS.....	50
	APPENDIX II GLOSSARY	52
	APPENDIX III DRAWINGS	55
	APPENDIX IV E3P REMEDIATION/ VALIDATION CRITERIA.....	57
	APPENDIX V E3P MATERIAL IMPORT CRITERIA	62
	APPENDIX VI CONTRACTOR PRE-COMMENCEMENT CHECK SHEET	64
	APPENDIX VII CONTRACTOR COMPLETION CHECK SHEET	67

DRAWING LIST

15-065-001 - Site Location Plan
15-065-002 - Proposed Development Plan
15-065-003 - Historical Features Plan
15-065-004 - Site Features Plan
15-065-005 - Exploratory Hole Location Plan
15-065-006 - Depth of Made Ground Plan
15-065-007 - Depth to Topsoil Plan
15-065-008 - Depth to Founding Strata Plan
15-065-010 - Conceptual Site Model
15-065-012 - Depth to Bedrock Plan
15-065-018 - Contamination Issue Plan



1. INTRODUCTION

1.1. BACKGROUND

E3P has been instructed by Vistry Partnerships to develop a remediation and enabling works strategy for the proposed residential development at the site located to the south of Lickers Lane, Prescott.

1.2. REPORT OBJECTIVES

The objectives of this report are to:

- ✿ Prepare overview of contaminated land remediation requirements;
- ✿ Evaluate feasible remedial technologies;
- ✿ Assess the most-appropriate earthworks solution to ensure the delivery of the optimum development platform;
- ✿ Define validation criteria to demonstrate the successful implementation of a site remediation and enabling works plan;
- ✿ Specify geotechnical engineering performance requirements; and
- ✿ Ensure the safe, cost effective and regulatory compliant redevelopment of the site.

1.3. SCOPE OF WORKS

The development of the risk management strategy for the subject site includes the following tasks:

- ✿ Identification of the relevant pollutant linkages;
- ✿ Review of site characteristics;
- ✿ Identification of geotechnical constraints;
- ✿ Development of remedial objectives;
- ✿ Selection of appropriate remedial technology; and
- ✿ Development of remedial strategy.

1.4. PREVIOUS WORKS

The following phases of geoenvironmental investigations have previously been carried out at the site:

- ✿ **E3P** – *Geo-Environmental Site Assessment*. Ref: Report No. 15-065-R2-1, dated November 2021, Prepared for Vistry Partnerships.

To inform the assessment of the potential risk to contaminated land within the context of the proposed residential development and to inform the preparation of the remediation strategy, the pertinent points from the above report are summarised within Section 2.


For the avoidance of any doubt, the E3P Geo-Environmental Site Investigation Report should be read both as a precursor to and in conjunction with this document.



1.5. REDEVELOPMENT PLAN

E3P understands that Vistry Partnerships are considering the proposed acquisition and future redevelopment of a parcel of land to the south of Lickers Lane, Whiston for low rise residential housing with associated adopted estate roads and utility infrastructure. The draft development layout is included as Drawing 15-065-002 (Appendix III) and a snapshot is shown as Figure 1.1. It should be noted that this remediation strategy is inclusive of the additional parcels to the south and east of the original site's boundary.

FIGURE 1.1 SNAPSHOT OF PROPOSED DEVELOPMENT

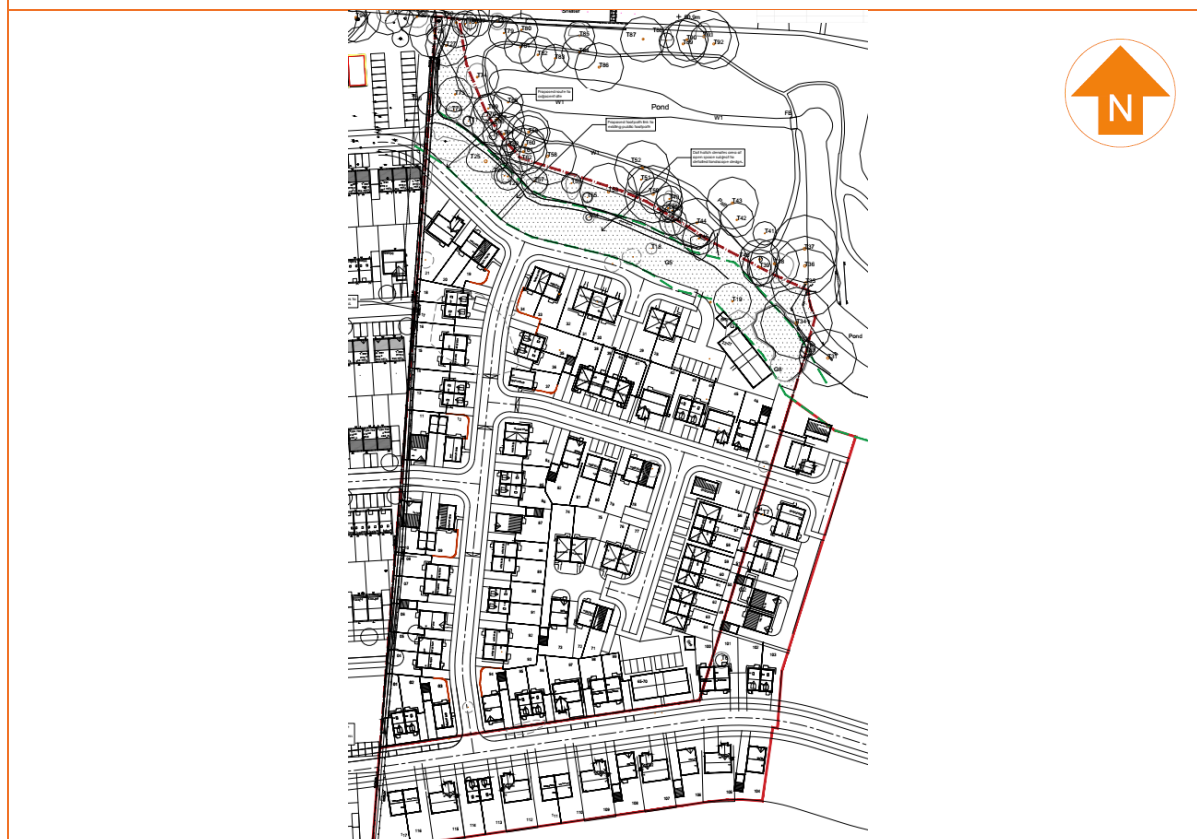

1.6. SUMMARY OF PARTIES INVOLVED

Function/interest	Name of Party
Local Planning Authority	Knowsley Council
Developer	Vistry Partnerships
Geoenvironmental Consultant	E3P
Main Contractor	Vistry Partnerships
Remediation/Enabling Works Contractor	TBC
Human Health Regulator	Knowsley Council
Controlled Waters and Waste Regulator	Environment Agency
Highways Adoption Authority	Knowsley Council



1.7. REGULATORY CORRESPONDENCE

Vistry Partnerships are in the process of submitting a detailed planning application to the local planning authority for the proposed redevelopment of the site for low-rise residential housing with associated adopted estate roads and infrastructure.

It is presumed that as part of the planning approval process, the planning authority will undertake consultation with the pertinent statutory consultees, which will include:

- ✳ Environmental health/contaminated land officer at the local authority (or external adviser);
- ✳ Environment Agency planning liaison; and
- ✳ The Coal Authority.



1.8. SITE DETAILS

Site Address	Land south of Lickers Lane, Whiston, Prescott, L35 3JE
National Grid Reference	E 347490, N 390400
Site Area	2.55 Ha.

All acronyms used within this report are defined in the glossary presented in Appendix II.

A site location plan is presented in Appendix III as Drawing 15-065-001.

1.9. SITE SUMMARY

TABLE 1.1 SITE DESCRIPTION AND SETTING

Occupancy/Use	The site is roughly rectangular in shape and is located to the south of Lickers Lane, Prescott. Two connected bodies of water border the site on the northern boundary. The general topography of the site is uniform with a gradual slope to the south of the site. There are frequent ruts and ditches caused by off-road vehicles across the site. Access is most effectively gained from the northern entrance of the site off Lickers Lane.	
	Upton entering site, the northern third of the site is overgrown with a mix of mature and semi mature trees and shrubbery. The areas south of the mature and semi-mature trees consist of waist-high vegetation. Historical mapping does not indicate the presence of any building or structures having been erected on the site. The site is currently open to the public, during the site walkover people were seen using the site for dog walking and other recreational activities.	
Environmental Setting	Drift Geology	Glacial Till – SAND, CLAY, GRAVEL
	Bedrock Geology	Kinnerton Sandstone Formation – SANDSTONE Pennine Middle Coal Measures Formation – MUDSTONE, SILTSTONE, SANDSTONE
	Hydrogeology	Secondary Undifferentiated aquifer (drift) overlying a Principal and Secondary A aquifer (solid). Two groundwater abstractions have been identified within a 1 km radius.
	Hydrology	Unnamed water features 7 m to the North East of the site.
	Flood Risk	The site is primarily located in an area that has limited potential for groundwater flooding to occur. The South West corner of the site is regarded as having potential for groundwater flooding of properties located below ground level.
	Subsidence Hazard	No hazard identified in data searches.



Site History	A review of the pertinent Ordnance Survey mapping dating from circa 1850 to the present day confirmed the site has remained undeveloped agricultural land. Mapping indicates that Pre 1937 the site has several of trees with a field boundary traversing from north-west to southeast. 1975 mapping illustrates the field boundary has been removed and replaced with another boundary running from east to west within the northern central sector of the site. The site also forms part of the Halsnead Park.
Landfill Sites and Ground Gases	The Envirocheck report has not identified any landfills, historic or present within 250 m of the site. The closest recorded Landfill is located 794 m to the North West of the site.
Radon	Unaffected – no special precautions required.

1.10. SUMMARY OF REPORTED GROUND CONDITIONS

E3P has prepared a detailed Site Investigation Report (Ref: 15-065-R2, dated November 2021). The summary of reported ground conditions is given in Table 1.2.

TABLE 1.2 SUMMARY OF GROUND CONDITIONS

MADE GROUND	Made Ground has been identified within one location (TP115). Made Ground consisted of Black sandy gravelly clay, gravels included angular to subrounded fragments of brick, mudstone, sandstone and ceramics.
Topsoil	Topsoil deposits were encountered within all exploratory hole locations apart from TP115 in which reworked Made Ground was identified. Topsoil deposits were encountered between 0.00 m and 0.60 m bgl. Topsoil deposits were formed from dark grey to black slightly clayey, gravelly SAND with frequent rootlets. Gravels were made up of fine to medium subrounded to rounded of mudstone and sandstone.
Drift	Drift deposits were encountered within all of the exploratory locations to a maximum depth of 2.60 m bgl. Ground conditions consisted of granular medium dense gravelly SAND becoming dense at depth within weathered sandstone. Clay deposits were identified within the central northern sector of the site which comprised of firm to very stiff medium to very high strength gravelly clays.
Bedrock	The solid bedrock geology was encountered between 1.00 m and 40.00 m bgl. The bedrock was consistent across the site being formed of yellow brown SANDSTONE.
Groundwater	No significant groundwater ingress was identified during the excavation of the exploratory locations. Monitoring recorded groundwater between 0.50 – 2.20 m bgl.



2. E3P CONTAMINATION RISK ASSESSMENT

2.1. BACKGROUND

E3P has completed a Tier 1 Qualitative Contaminated Land Risk Assessment to determine the potential risk to human health, controlled waters and the wider environ. This assessment is documented in full within the E3P Geoenvironmental Site Assessment report and, for clarity, is summarised in the following sections of this document.

2.2. HUMAN HEALTH RISK SUMMARY

The E3P Tier 1 Qualitative Human Health Risk Assessment identified concentrations of the following determinants at or above the screening criteria for the assessment of no unacceptable degree of risk to human health:

- ✿ Benzo(a)Anthracene;
- ✿ Benzo(b)Fluoranthene;
- ✿ Benzo(a)Pyrene; and
- ✿ Dibenzo(a,h)Anthracene.

No asbestos was identified within any of the soils submitted for analysis and there were no visual signs of ACM within the soils during the site investigation.

No significant concentrations of hydrocarbon compounds or heavy metals were identified in the soils submitted for chemical analysis.

The exceedances for all determinants are associated with shallow Made Ground deposits with TP115 at 0.30 m bgl.

All the identified elevated concentrations have primary exposure pathways related to dermal contact and ingestion, soil ingestion and consumption of homegrown produce. As all of the exceedances are identified within one exploratory location they are considered to be an isolated hotspot, therefore during the enabling works, it is recommended the impacted Made Ground is excavated and placed within an area of low sensitivity.

The Made Ground identified within TP115 is not considered suitable for use within the upper 300 mm of a residential garden given the presence of deleterious elements. It will therefore be necessary to place a minimum of 150 mm of sub-soil and 150 mm topsoil to constitute a 300mm clean soil matrix within all areas of private gardens where Made Ground remains.

Chemical analysis of topsoil and subsoil confirms the material is suitable for re-use within proposed gardens and public open spaces areas. It should be noted that further chemical analysis will be required to confirm soils are chemically suitable in line with intended re-use volumes.

It is concluded that the site will be suitable for the proposed residential end use subject to the completion of the supplementary assessments and the following build-phase mitigation items:



Land South of Lickers Lane

Remediation and Enabling Works Strategy

August 2022

-  Use of potable water supply infrastructure that will be compliant with United Kingdom Water Infrastructure Risk (UKWIR) assessment criteria.
-  Construction of a 300 mm growing medium to all areas of private garden in accordance with the detailed methodologies herein.
-  Further investigation within the additional southern and eastern parcels.



2.3. CONTROLLED WATERS CONTAMINATION RISK SUMMARY

A Tier 1 Controlled Water Risk Assessment was completed by E3P as part of the E3P Geo-Environmental Site Assessment, the findings of which are summarised as follows:

- ✳ The primary receptor has been identified as the underlying Principal bedrock aquifer and the unnamed watercourse (pond);
- ✳ It is unlikely that significant contaminant impact to the aquifer or the watercourse will occur due to there being no identified soil sources of contamination and a lack of groundwater to mobilise any such contaminants;
- ✳ The Tier 1 assessment has identified that there is considered to be no unacceptable risk to the underlying principal aquifer.

2.4. GROUND GAS

Ground gas has been assessed by E3P as part of the E3P Geoenvironmental Site Assessment. The assessment was completed in accordance with the methodology outlined with the CIRIA publication C665, utilising the results of the ground gas monitoring surveys to calculate a tentative gas screening value (GSV). The GSVs for the monitoring positions are summarised in Table 2.1.

TABLE 2.1 GAS RISK PROFILE AND LOCATION

WELL	DATE	DEPTH TO WATER (m bgl)	MAX FLOW (l/hr)	MAX CH ₄ (%V/V)	MAX CH ₄ Q _{hg} (l/hr)	MAX CO ₂ (%V/V)	MAX CO ₂ Q _{hg} (l/hr)	CHARACTERISTIC SITUATION	NHBC TRAFFIC LIGHT
WS101	04/11/2021	-	0.1	0.1	0.0001	1.4	0.0014	CS1	Green
	15/11/2021	1.2	0.1	0.1	0.0001	1.9	0.0021	CS1	Green
	10/12/2021	0.9	0.1	0.1	0.0001	2.6	0.0026	CS1	Green
	31/12/2021	1.2	0.1	0.1	0.0001	1.4	0.0023	CS1	Green
	20/01/2022	2	0.1	-0.1	-0.0001	0.1	0.0001	CS1	Green
	28/01/2022	2	0.1	0.1	0.0001	0.1	0.0001	CS1	Green
WS102	04/11/2021	-	0.1	0.1	0.0001	4.1	0.0041	CS1	Green
	15/11/2021	-	0.1	0.1	0.0001	4.1	0.0041	CS1	Green
	10/12/2021	0.5	0.1	0.1	0.0001	3.6	0.0037	CS1	Green
	31/12/2021	0.5	0.1	0.1	0.0001	3.5	0.0035	CS1	Green
	20/01/2022	-	0.1	-0.1	0.0001	0.1	0.0001	CS1	Green
	28/01/2022	-	0.1	0.1	0.0001	0.1	0.0001	CS1	Green
WS103	04/11/2021	-	0.1	0.1	0.0001	0.8	0.0016	CS1	Green
	15/11/2021	-	0.1	0.1	0.0001	5.1	0.0056	CS2	Amber 1
	10/12/2021	-	0.1	0.1	0.0001	4.2	0.0047	CS1	Green
	31/12/2021	-	0.1	0.1	0.0001	4.3	0.0043	CS1	Green
	20/01/2022	-	-0.1	-0.1	-0.0001	0.1	0.0001	CS1	Green
	28/01/2022	-	0.1	0.1	0.0001	0.1	0.0001	CS1	Green



WELL	DATE	DEPTH TO WATER (m bgl)	MAX FLOW (l/hr)	MAX CH ₄ (%V/V)	MAX CH ₄ Q _{hg} (l/hr)	MAX CO ₂ (%V/V)	MAX CO ₂ Q _{hg} (l/hr)	CHARACTERISTIC SITUATION	NHBC TRAFFIC LIGHT
WS104	04/11/2021	1.46	0.1	0.1	0.0001	1.4	0.0014	CS1	Green
	15/11/2021	1.54	0.1	0.1	0.0001	4.3	0.0043	CS1	Green
	10/12/2021	1.65	0.1	0.1	0.0001	3.8	0.0038	CS1	Green
	31/12/2021	1.6	0.1	0.1	0.0001	3.8	0.0038	CS1	Green
	20/01/2022	1.7	0.1	-0.1	-0.0001	0.1	0.0001	CS1	Green
	28/01/2022	1.6	0.1	0.1	0.0001	0.1	0.0001	CS1	Green
WS106	04/11/2021	2.2	0.1	0.1	0.0001	3.3	0.0033	CS1	Green
	15/11/2021	-	0.1	0.1	0.0001	2.6	0.0028	CS1	Green
	10/12/2021	1.8	0.1	0.1	0.0001	1.8	0.0025	CS1	Green
	28/01/2022	-	0.1	0.1	0.0001	0.1	0.0001	CS1	Green

E3P has assessed the previous variables and come to the following conclusions:

- ✳ Ground gas monitoring suggests that the site can be predominantly classified as CS1, and in these areas, it is considered that gas protection measures will not be required.
- ✳ In the vicinity of WS103, carbon dioxide has been identified above the 5% v/v threshold, however as this was an isolated occurrence and the GSV is noted to be within a CS1 classification for the remainder of the monitoring period. Additionally, the GSV fell into CS1 characteristic and therefore the overall gas risk can be reduced to CS1 Green.
- ✳ The elevated carbon dioxide is likely due to possible infilled field boundaries.
- ✳ With due consideration to the Conceptual Site Model and the absence of any persistent gas source and gas generation potential, it is considered by E3P that the site can be classified as CS1, and therefore no gas protection measures are required.

2.5. POTABLE WATER SUPPLY INFRASTRUCTURE

This will need to be confirmed following the completion of a UKWIR risk assessment. Post-remediation and enabling works ground conditions may be different from those identified during this site investigation.



3. SITE REMEDIATION AND ENABLING WORKS

3.1. REMEDIATION OPTIONS APPRAISAL

A remediation options appraisal has been completed in accordance with the principles as set out within Environment Agency publication Land Contamination: Risk Management (LC:RM)(updated May 2020).

The LC:RM requires that the following tiered assessments are followed to ensure a sufficiently detailed and robust appraisal of remediation options to inform the selection of the preferred approach and utilisation of the correct technologies to promote safe and sustainable land remediation:

- ✚ Identification of feasible remediation technologies;
- ✚ Detailed evaluation of viable options; and,
- ✚ Selection of appropriate remediation option.

3.2. CONTAMINANTS OF CONCERN (COC)

3.2.1. METALS, PAH, NON-VOLATILE HYDROCARBON (PETROLEUM RANGE) COMPOUNDS

The human health risk drivers for the carcinogenic PAHs and metal CoC are:

- ✚ Direct contact with the soil source by future on-site residents; and
- ✚ Ingestion of impacted soils by future on-site residents.

The exceedances for all determinants are associated with shallow Made Ground deposits with TP115 at 0.30 m bgl.

All the identified elevated concentrations have primary exposure pathways related to dermal contact and ingestion, soil ingestion and consumption of homegrown produce. As all of the exceedances are identified within one exploratory location they are considered to be an isolated hotspot, therefore during the enabling works, it is recommended the impacted Made Ground is excavated and placed within an area of low sensitivity.

The Made Ground identified within TP115 is not considered suitable for use within the upper 300 mm of a residential garden given the presence of deleterious elements. It will therefore be necessary to place a minimum of 150 mm of sub-soil and 150 mm topsoil to constitute a 300mm clean soil matrix within all areas of private gardens where Made Ground remains.

3.2.2. ASBESTOS

No sources of asbestos or trace fibres have been identified on the site at this point.

In the event that a previously unidentified area of asbestos fibre impact is identified, the materials will be subject to analysis and management in accordance with the E3P-developed site CSM.

Where asbestos is identified at concentrations above <0.001%, a hotspot excavation will be required. The impacted Made Ground will require placement >1.00m beneath an area of low sensitivity, such as a public open space per the E3P conceptual site model (Figure 3.1).



FIGURE 3.1 ASBESTOS CONCEPTUAL SITE MODEL



Notes

ND None Detect

0.001% Soils may contain $\leq 0.001\%$ asbestos using composite testing to ensure there is no potential risk to human health. This value is present within areas where there may be a short term low level exposure of soils containing trace asbestos fibres by construction workers where an appropriate level of asbestos management is employed (dust suppression)

0.1% Soils at a depth of $>1.00\text{m}$ bgl may contain $<0.1\%$ asbestos using composite testing where they will not be likely to be disturbed in the future and will therefore be in an area of low sensitivity. Risk assessment completed in accordance with Asbestos JIWG risk assessment tools.

Undefined- this will be dependent upon soils encountered during earthworks, which may be placed at these depths to ensure no potential risk to human health.

All ACM-impacted soils must be managed to ensure no airborne fibre release during construction or placement of impacted material in such a manner as to ensure no future exposure risk.

Soils will be placed in areas of no unacceptable future risk in accordance with the E3P validation method.

If any visible pieces of asbestos-containing material are identified during the site remediation and enabling work, this material must be dealt with in strict accordance with the Control of Asbestos Regulations (CAR) 2012, UK Waste Management Legislation and the Environmental Protection Act 1994. Due to the close proximity of residential dwellings, asbestos in air monitoring in accordance with HSG248 may be required to confirm that no asbestos fibres have been generated from the enabling works activities.

Should off-site disposal be required, then additional asbestos quantification and waste classification testing should be undertaken to ensure that it is classified correctly and disposed of at a suitably licensed facility.



3.3. SUMMARY OF PREFERRED REMEDIATION OPTIONS

Based on the options appraisal, it is considered that the following combination of remediation technologies provides the most sustainable, viable and economic solutions that will ultimately result in the successful remediation for the site:

- ✚ Construction of low permeability **capping system** to limit infiltration of precipitation to reduce mobility of soluble phase impact and ensure no direct exposure pathway to future receptors.
- ✚ **Off site removal** of hazardous materials which cannot be treated will be required, this operation needs to be limited to materials that cannot be treated on-site to promote sustainability and ensure viable regeneration.

3.4. OVERVIEW OF WORKS

Prior to the commencement of works on site, the contractor must establish all necessary plant, equipment and site welfare facilities as is necessary to complete the contract within the agreed timescales to the rationale as outlined in the following subsections.

For the avoidance of any doubt, the proposed operations as set out herein document the required performance objectives and validation sampling protocols; however, the specific methods of work deployed to ensure the remediation objectives are achieved in a compliant manner on site will be the responsibility of the appointed contractor.



RE-1 – Further Investigation Into Southern and Eastern Parcels

At the time of the initial ground investigation, the additional parcels to the south and east (illustrated in figure 2 below) hadn't been investigated. Prior to the commencement of remediation works further investigations should be completed into the additional parcel of land.

Mechanically excavated trial pits will be advanced with additional chemical analysis of the soils completed to confirm no unacceptable risk to human health and controlled waters. If any as yet unidentified contamination is identified, this will be the subject of further investigation including laboratory analysis and subsequent assessment of risk within the context of the agreed parameters. Where a theoretical risk to either human health, controlled waters or the wider environs is identified, appropriate remediation works are to be instigated by the placement of clean cover systems to break the pathway or delineation and source removal where required.

It should be noted that further rotary boreholes should also be completed within the Coal Authority defined development high-risk area within the southwestern corner of the site. the purpose of the further rotary boreholes will be to confirm the absence of shallow workings.

Figure 2 – Further investigation required within additional parcels



RE-2 – Pre-commencement Regulatory Compliance

Prior to commencement of any works on site, all reports relating to the assessment of risk to contaminated land should be submitted to the regulatory authorities to gain written approval.

All relevant Standard Rules Permits should be registered with the EA.

The LAPC Part B Notification for deployment of mobile crushing plant should be implemented prior to the establishment of equipment on site.

If the proposed volume of soils to be reused (excluding crushed materials) exceeds the parameters of the Standard Rules Permit, a CL:AIRE Materials Management Plan (MMP)-qualified declaration should be made by the contractor, having obtained full written approval for the remediation strategy from the LPA and Environment Agency.



It is not anticipated that there will be any requirement to treat any materials on site (such as hydrocarbon-impacted soil or groundwater); however, should any previously unidentified contamination be encountered, the contractor must either notify E3P and, if appropriate, relevant regulators of their intention to complete a minor works operation or arrange for the deployment of the appropriate environmental permit for the specified operation.

RE-3 – Environment and Nuisance Control

Management of all works is required so as to ensure that no environmental nuisance is created through dust emissions, noise or vibration levels.

All works are to be completed in a manner so as not to create any structural risk to the adjacent highways.

Temporary works are to be implemented as necessary to support excavations throughout the duration of the works.

In the event that a complaint is made in respect of dust emissions, noise or vibration levels, remedial measures and a programme of ongoing monitoring should be agreed with the local authority and implemented on site.

RE-4 – Risk to Infrastructure

Site works should be completed in a manner that ensures no risk of disturbance to the adjacent infrastructure.

RE-5 – Identification, Isolation and Treatment of Invasive Plants

Invasive plant species have not been identified on site at this time.

The remediation contractor must satisfy themselves with respect to the extent of all species deemed invasive prior to the commencement of works on site. The contractor shall employ a suitably qualified expert to investigate the presence of invasive plant species on or adjacent to the site. If invasive plant species are identified, these will be treated in strict accordance with an approved method statement to be submitted to the supervising consultant for review prior to the instigation of any works.

Where invasive plant species are identified at the site boundary, a suitable barrier shall be installed to prevent any future reinfestation of the subject site.

Upon completion of the eradication of all invasive species, a validation report should be prepared documenting all identified invasive plant species, their location and the treatment methodology. Where materials are removed from site, all waste transfer notes/duty of care certificates should be included within the validation statement.



RE-6 – Site Clearance Operations

The site is currently overgrown with self-seeded vegetation with extensive above- and below-ground structures; this material should be removed in a controlled manner with full compliance with any ecological mitigation measures that are required for the works. Any such measures are outside the scope of this report.

All vegetation should either be stockpiled at a pre-agreed location or alternatively removed from site in accordance with waste permitting regulations.

All root networks are to be removed in accordance with the requirements of the NHBC/LABC.

RE-7 – Recovery of Natural Topsoil

The site investigation report and subsequent surveys identifies areas of the subject site where natural organic soils (topsoil) are present at the near surface. The contractor should seek to maximise the recovery of this material to promote sustainable construction through careful segregation and subsequent stockpiling of the natural soils.

All recovered topsoil should be covered with a suitable geotextile to limit cross-contamination from anthropogenic elements during remediation, enabling and construction. This will significantly contribute to maximising the recovery and reuse of material.

All material will be subject to validation testing by the supervising consultant in accordance with the testing specification set out herein.

RE-8 – Excavation, Breaking and Processing of All Above- and Below-Ground Structures

Obstructions, relict foundations and infrastructure (apart from live services) are to be removed from the areas of proposed residential development, including plot footprints, rear gardens, private driveways, adopted highway and utilities infrastructure (road box) in their entirety.

Artificially hard materials should be broken out and crushed. Stockpiles will be made, validation testing undertaken, and site-won material reused on site where required. Materials will be processed as per the specifications provided in Section 5 using licensed plant.

The E3P drawings denote the extent of known historic features with obstructions; however, it will be the contractor's responsibility to remove all obstructions.

Obstructions encountered within the near-surface soils will be chased to their full depth and removed; if not possible, the obstruction must be surveyed with the location communicated to E3P, the client and the developer.

Where natural soils are present at a relatively shallow depth, extreme care should be taken to ensure that the natural cohesive deposits remain undisturbed with a full reduced-level survey to be completed to map the depth of filled/processed material.



RE-9 – Cut-And-Filling of Made Ground to Development Levels

Where the proposed enabling works levels require the current landform to be cut, extreme care should be taken so as not to disturb the underlying stratum prior to the placement of the appropriate platform, in compliance with the E3P Geotechnical Specification.

Where the development levels require material to be filled, site-derived MADE GROUND must be sorted in a controlled manner prior to replacement, in accordance with the requirements of this specification for the intended land use.

The maximum dry density must be determined in laboratory conditions utilising UKAS-accredited testing prior to the commencement of filling and compaction works. In-situ density testing is required to demonstrate compliance with the E3P Geotechnical Performance Specification.

RE-10 – Placement and Compaction of Uppill Material to Facilitate Ground Improvement by VSC

Where plots are to be prepared in a manner that will facilitate ground improvement by vibro-stone column, materials must be either compliant with the specified grading requirements for a nominally placed and tracked granular aggregate, or alternatively they should be engineered to a defined geotechnical standard.

Materials compliant with VSC grading for granular backfill: granular matrix are to be graded with all particles < 125 mm with no more than 10% fines (0.63 micron).

Non-compliant material requiring engineering to geotechnical design: material is to be placed and engineered in accordance with the correct method for the Series 600 classification (1, 2 or 6) with moisture contents to be controlled within acceptable design limits. In-situ density to be confirmed to be > 95% of the laboratory determined maximum (2.5 kg) with < 5% air void ratio.

RE-11 – Construction of Temporary Working Platform

Where plots are to be prepared in a manner that will facilitate ground improvement by vibro-stone column, a temporary working platform will be constructed.

The specific design for such a platform should be obtained from E3P; however, as a minimum this will comprise:

-  Proof rolling of the subgrade to ensure a California bearing ratio (CBR) > 3%; and
-  Placement of 300 mm of certified 6F2 to be rolled and compacted to ensure a CBR > 6%.



RE-12 – Replacement of Materials, Geotechnical Engineering Requirements

Material is to be backfilled in strict compliance with the E3P Geotechnical Engineering Specification as presented in detail within Section 5 of this report, which generally requires the reinstatement and compaction criteria presented in Table 3.1.

TABLE 3.1 GEOTECHNICAL ENGINEERING WORKS SCHEDULE

Land Use	Construction Requirement	Requirement
Footprint of Proposed Structure (2 m on All Elevations)	Pile Foundation	Backfill using general method compaction to CBR of 5%.
	Vibro-Stone Column	Particle size distribution (PSD confirmed as < 125 mm with no more than 10% fines (0.63 micron). Or Compaction to achieve > 95% of the laboratory determined maximum dry density (DD) with < 5% air void ratio. CBR > 6% with suitable pile mat. PSD testing of backfill material at 1 sample per 2000 m ³ to confirm.
	Traditional Spread Foundation	Ensure no disturbance of natural soil at shallow depth.
Highways	Adopted Estate Road/Drainage	Manual of Contract Documents for Highways Works (MCHW) Series 600 ensuring CBR > 5% in subgrade (engineered fill).
Driveways	Private Drives and Car Parking	Method compaction to CBR > 5%.
Gardens and Public Open Space	N/A	Method compaction to ensure no settlement.

RE-13 – Preparation of Ground for Vibro-Stone Columns Within Tree Influence

Where trees are present, or within their total zone of influence, the contractor must ensure that all cohesive soils are removed to the required depth with the subsequent replacement with a granular blanket to fully mitigate the potential for volumetric instability in the clay soils.

The zone of tree influence will be indicated within the foundation zoning plan and all resultant excavations and subsequent backfilling must be inspected and approved by E3P.

The depth of the granular blanket required will be determined prior to the commencement of the works and in full agreement of the client, but will nominally be equal to or in excess of 2.5 × foundation width.



RE-14 – Importation of Bulk Fill

Where there is a net shortfall of material required to achieve the proposed ground levels, it will be necessary to import natural inert soils and aggregate as per the engineering requirements (Section 5).

Imported material must be certified as suitable for use in strict accordance with the E3P chemical and geotechnical performance criteria (See Section 5) and in conjunction with the required duty of care notes and waste transfer exemption.

If recycled aggregates are imported, then laboratory testing should be completed to demonstrate compliance with the Waste and Resources Action Programme (WRAP) protocol.

Where inert soils are imported, laboratory testing should be completed in accordance with the requirements of the pertinent environmental permit (i.e. U1 Standard Rules) or CL:AIRE MMP for the reuse of clean, naturally occurring soils.

RE-15 – Preparation of Garden for Cover System

In the event that as yet unidentified pollution sources are present which require remediation action, garden areas will be prepared in a manner that will facilitate the placement of the clean cover system during the development phase of the works. The preparation of the areas requiring clean cover is critical in ensuring delivery of the site in a manner that will ensure no risk to the proposed end users.

Where Made Ground is deemed unsuitable for retention in a garden, the area will be subject to a reduced-level dig to remove unsuitable material to a minimum depth of 600 mm below finished garden level or verified natural stratum (whichever is the shallower).

Excavated soil will be stockpiled pending the results of the appropriate validation testing (to be completed in accordance with this specification) prior to reuse in an area of no sensitivity or, where necessary, this material will be removed from site in accordance with UK waste management legislation.

The placement of certified subsoil and topsoil will be completed as part of the developer works/build-phase mitigation plan. All garden areas where a cover system is required will be subject to plot-specific independent validation.

RE-16 – Provision of Subsoil

It will be necessary to provide a 300 mm growing medium using certified material with appropriate validation within proposed gardens and landscaped areas. Natural drift deposits encountered within the upper 300 mm of finished ground levels can be directly overlain with a suitable cover (minimum 150 mm topsoil).

The shallow natural drift deposits are deemed suitable for use within the growing medium to gardens and areas of soft landscaping.



RE-17 – Provision of Topsoil

A significant quantity of topsoil will be recovered during the 'site strip' operation.

Topsoil will require testing in line with the schedule present within Section 3.5 and Table 3.2.

The garden and landscaped areas will require depth validation to satisfy the requirements of the CML in order to demonstrate that the appropriate thickness has been provided.

RE-18 – Independent Validation: Watching Brief

Given the site history and potential contamination sources identified within the ICSM, a degree of uncertainty remains with regard to the potential for as yet unidentified contamination impact within the near-surface soils and groundwater.

It will therefore be necessary to instigate the site-wide remediation and enabling works under the supervision of a suitably qualified and independent specialist. The specialist is required to attend site as and when appropriate to monitor works, record ground conditions and fully investigate all potential sources of as yet unidentified contamination.

RE-19 – Waste Soils Surplus to Requirements

In the event that a surplus of excavation material is present on site, this, in most cases, will be deemed to be a waste in accordance with the Waste Framework Directive (Article 3(1) Waste Framework Directive 2008/98/EE). The waste producer – but ultimately, the landowner – is responsible for the compliant disposal of such materials.

A formal waste classification assessment must be undertaken, irrespective of any future options or considerations for those materials that will be removed from site. Waste classification should only be made following the Environment Agency *Technical Guidance WM3 – Guidance on the Classification and Assessment of Waste*.

To remove the surplus material from site it will either need to be sent to a disposal site (landfill), to a permitted treatment facility or, dependent on the waste classification assessment, it may be suitable for use on a permitted land improvement or restoration operation.

Subject to suitability, these soils can be transferred to the receiving site, subject to an approved permit or materials management plan following guidance in the CL:AIRE *Definition of Waste: Code of Practice*.

RE-20 – Validation of Materials for Potable Water Supply Infrastructure

PE pipe is likely to be suitable, however, this will need to be confirmed following the completion of a UKWIR risk assessment.

Post remediation and enabling works ground conditions may be different from those identified during the ground investigation. There will be a requirement to import capping materials for highways, which if from a recycled source may preclude the use of standard pipes.

Where imported material is required to construct the potable water infrastructure pipework, this material will need to comply with the requirements of UKWIR pipework thresholds for the specified pipework.



For the avoidance of doubt, the PE thresholds are presented in Section 9.3. Failure to meet the required specification may necessitate further remedial works.

RE-21 – Remedial Verification Report

Collation of information relating to site clearance, chemical testing, remedial works, remedial verification, material movements and waste transfer documentation is required, where appropriate.

Complete remedial validation is to be reported in line with regulatory guidance. This will include a detailed risk assessment. The report will be submitted to the local authority for approval following completion.

3.5. VALIDATION SAMPLING PROTOCOL

In accordance with the current requirements of the regulatory authorities, validation samples will be collected from all materials that are to be subject to movement under the protocols outlined within this remediation and enabling works strategy, or for materials to be imported onto site to facilitate the proposed residential development.

Soil samples destined for chemical analysis will be collected at regular intervals in appropriate sampling containers. All samples will subsequently be stored in cooled boxes prior to submission to a UKAS/MCERTS accredited laboratory.

All samples will be collected using appropriate personal protective equipment (PPE) and sampling equipment, which will be cleaned at each sampling location.

A detailed copy of E3P Ltd sampling methodology, QA procedures and laboratory chain of custody forms will be documented within the site records and presented with the final validation report for the site.

Where material is found to contain concentrations of potential contaminants at levels in excess of the site-specific screening criteria (as detailed within Appendix III), E3P will undertake further assessment and recommendations on the appropriate use for the material in question, which may involve the disposal of such materials off site to a suitable waste management facility.

The sampling frequency for materials to be managed under the remediation strategy is presented within Table 3.2.

TABLE 3.2 SPECIFICATION OF CHEMICAL VALIDATION LABORATORY ANALYSIS

MATERIAL USE	TESTING FREQUENCY	SUITE OF ANALYSIS
Site-Generated		
Site-Generated 6F2	1 Sample per 1000 m ³	A/B/C/D
Site-Won MADE GROUND General Backfill	1 Sample per 250 m ³ where visual and/or olfactory impact is identified	G
Site-Won MADE GROUND General Backfill	1 Sample per 1000 m ³	A/B/C/D
Site-Won MADE GROUND General Backfill	1 Sample per 2000 m ³	I
Site-Won Natural Backfill	1 Sample per 2000 m ³	A/B/C/D



Site-Generated Subsoil (150 mm Garden Cover)	1 Sample per 250 m ³	A/B/C/D
Site-Generated Topsoil Cover (150 mm Garden Cover)	1 Sample per 50 m ³	A/B/C/D
Hotspot Validation Samples	1 Sample per 10 m of linear excavation to base and sidewall	E/G
Imported		
6F2	1 Sample per 1000 m ³	A/B/C/D
Subsoil Greenfield Source (150 mm Garden Cover)	1 Sample per 200 m ³	A/B/C/D
Subsoil Brownfield Source (150 mm Garden Cover)	1 Sample per 50 m ³	A/B/C/D
Topsoil Greenfield Source (150 mm Garden Cover)	1 Sample per 200 m ³	A/B/C/D
Topsoil Brownfield Source (150 mm Garden Cover)	1 Sample per 50 m ³	A/B/C/D
General Engineering Fill (Class 1 and 2 Soil)	1 Sample per 1000 m ³	A/B/C/D

Notes

Suites of Analysis:

- A. Speciated PAH.
- B. Speciated TPH (C5-C35).
- C. Asbestos (ID).
- D. CLEA Inorganic Heavy Metals.
- E. Speciated PAH, Banded TPH and VOCs.
- F. SVOC/Speciated TPH.
- G. On-Site Screening for VOC Using Calibrated PID.
- H. Leachate 2:1 Speciated PAH and Banded TPH.
- I. Leachate Analysis of Inorganic Heavy Metals, TPH, Sulphate and PAH.

All analysis prescribed above to be completed by UKAS-accredited laboratory.

3.6. REMEDIATION CONTRACTOR'S SITE MANAGEMENT AND RESPONSIBILITY

The appointed remediation contractor will take full and overarching responsibility for all methods of work required to complete the site remediation and enabling operations to ensure the delivery of the site and the completion of the objectives in a safe, legislatively compliant manner that ensures no pollution to the subject site or the wider environs.

For individual remediation operations as set out within this performance specification, the contractor will provide site-specific methods of work for individual operations pertaining to the removal and treatment of contaminated liquids and soils. For each and every operation as set out herein, the contractor will provide a written methodology of works to be supplied to the supervising geoenvironmental engineer prior to the instigation of operations on site.

The site manager will be responsible for documentation of each day's activities with a full recorded schedule of works completed and corresponding site-specific method statements that have been utilised to ensure the completion of the task to the required standard.



4. MATERIALS MANAGEMENT AND LEGISLATIVE COMPLIANCE

The processing of recycled aggregates will be completed using LAPC Part B licensed plant with the appropriate deployment notification to the local authority prior to commencement of works. All materials that are recovered as recycled aggregate will be compliant with the requirements of the WRAP protocol and the E3P validation testing requirements and as such would not be deemed to be a waste material.

A U1 Exemption will be registered for the site, which allows the reuse of up to 5000 T of prescribed material within construction, with up to 25,000 T of material permissible to be reused in the construction of roads. It should be noted that only 1000 T of material described as sand, stones or clay soil classified as waste can be reused with a U1.

A T5 Exemption, allowing for the screening and recovery of up to 5000 T of permissible material for subsequent reuse in construction will also be registered.

All materials that are recovered under the WRAP protocol, U1 or T5 exemptions must be analysed to demonstrate that they are both chemically and structurally suitable for use within the context of the development.

The relevant LAPC, U1, T5 and WRAP licences, exemptions and protocols provide the legislative framework for material compliance during the site remediation and enabling works to be completed by the specialist contractor under the supervision of E3P.

Where necessary, operations, as outlined within the remediation enabling works rationale summarised in this report, may be subject to regulation using the appropriate environmental permit, standard rules exemption and materials management plan, to be created in accordance with version 2 of the CL:AIRE *Definition of Waste: Code of Practice (DoW CoP)*.

It is noted that if material is to be imported utilising the CL:AIRE DoW CoP from an alternative development site, then only chemically certified, clean, naturally occurring material can be transferred.

If required, the MMP will be created with due consideration of all proposed remediation and enabling works operations prescribed within this document and will be undertaken by a qualified person with a signed declaration submitted to the EA prior to reuse of materials on the site.

The importation of material for use within the proposed construction of a development platform will be subject to the compliance with the E3P protocol for the importation of materials as set out within the specification for material import included within Appendix IV of this report.



5. ENVIRONMENTAL MONITORING AND VALIDATION

5.1. SITE MANAGEMENT

The tracking of materials will be based on the following hierarchy:

- ✚ The principal contractor will have the responsibility for setting out areas of the site on the basis of the contract specification.
- ✚ Operatives will have instructions only to excavate and to emplace materials in specified areas as assigned by the site manager/foreman.
- ✚ The site manager (employed by the principal contractor) will issue daily instructions to drivers regarding the placement of materials sourced from specific stockpiles or areas, ensuring that appropriate documentary evidence is collected that details which materials are going where and why.
- ✚ An E3P consultant, who will be in attendance as required, will:
 - Inspect the excavation areas and certify that the correct materials are being excavated;
 - Conduct spot checks on loaded vehicles to ensure compliance with this remediation strategy; and
 - Ensure that any loads that fail visual, olfactory or spot checks either remain on the vehicle or, if unloaded, are excavated and set aside. This material will be treated according to the recommendations of the E3P site engineer.
- ✚ E3P will conduct an audit of waste consignment notes. All material imported and removed from site will have duty of care/consignment notes, copies of which will be retained on site by the site manager.
- ✚ Materials directly reusable will be incorporated into the earthworks, subject to operational conditions and phasing of excavations, in which case they will be stockpiled prior to final placement.

5.2. COMPLETION

Following the completion of the remediation works, a report will be compiled by the environmental consultant detailing all site enabling works undertaken, waste consignment notes, and all site investigations, laboratory test certificates and validation testing undertaken.

A certificate of completion of earthworks should be included within the report which should then be issued to the local authority for their approval.

E3P considers that with the adoption of the above best practices the site can be safely redeveloped. The site enabling works process and presence of any residual contamination (if this is the case) should be recorded for future reference by landowners/occupiers. Future development at the site where this may result in penetration of new areas of hardstanding should be subject to no-less-stringent measures with respect to assessment and, where appropriate, monitoring, than those set out herein.



5.3. MITIGATION OF RISK FROM SOILS WITH ASBESTOS FIBRES

5.3.1. PRE-COMMENCEMENT WORKS

Prior to the commencement of works the following requirements must be satisfied:

- ✳ Induction of all people that will be involved with the proposed site works; and
- ✳ All methodologies must be agreed upon by all parties involved.

5.3.2. CONTROL, MONITORING AND REPORTING OF GENERAL AERIAL EMISSIONS FROM DUSTS AND PARTICULATES

DAMPING DOWN OF SOILS – MITIGATE PARTICULATE (DUST) EMISSION

During excavation, as outlined within the detailed working methodologies, soils will be regularly damped down using water to control the generation of dust (this may also comprise precipitation). The contractor will determine the best form of dust suppression to be used when a detailed programme has been issued.

If any previously unidentified asbestos-containing materials are identified, these should be dealt with in strict accordance with the *Control of Asbestos Regulations* (2012) and industry best practice as detailed in CIRIA 733.

GENERAL CONTROL OF DUST

The following control measures should be utilised to ensure that dust levels are kept to a minimum at all times:

- ✳ Where necessary, haul road, work areas and stockpiles will be damped down with water spray.
- ✳ The application of water to haul roads, work areas and stockpiles should be closely monitored by the resident engineer to ensure that soils are not saturated and, therefore, that the potential for water run-off is appropriately mitigated.
- ✳ Once completed, any stockpiles will be sealed by compacting at the surface.
- ✳ Vehicle speeds and movements on site will be kept to a minimum (< 5 mph) during civil excavation works to reduce the potential to generate dust.



PERSONAL PROTECTIVE EQUIPMENT (PPE)

In accordance with the HSE *Guidance Note em6: Asbestos Essentials, Personal protective equipment (including RPE)*, E3P recommend that all site operatives present within the work area where potential asbestos-impacted soils are being excavated are supplied with the following personal protective equipment:

Overalls:

- ✳ Disposable overalls.
 - Type 5 (BS EN ISO 13982-1) are suitable.
 - Cotton overalls hold dust and need specialist laundering.
- ✳ Waterproof overalls for outdoor work.
- ✳ Use oversized overalls - this will help to prevent ripping at the seams.
- ✳ If the cuffs are loose, seal them with tape.
- ✳ Avoid wearing a long-sleeved shirt as these are difficult to cover properly.
- ✳ Wear the overall legs over footwear as tucking them in lets dust into footwear.
- ✳ Wear the hood over the RPE straps.

Failure to utilise and correctly employ PPE will result in immediate cessation of works. Works will not be permitted to recommence until the individual has undergone further training in the use of PPE or the individual is removed from the works area.

At this current time, with the levels of ACM identified within the soils, the above-listed PPE is not considered to be required for all site personnel during the entire management of these soils.

When handling asbestos-impacted soils during the enabling works, asbestos monitoring works should be conducted in accordance with, but not limited to, the following HSE legislation and guidance:

- ✳ *Health & Safety at Work Act 1974;*
- ✳ *The Control of Asbestos Regulations 2012;*
- ✳ CL:AIRE, 2016. *Control of Asbestos Regulations 2012 - Interpretation for Managing and Working with Asbestos in Soil and Construction and Demolition Materials: Industry guidance;*
- ✳ *Approved Code of Practice L143 Work with materials containing asbestos;*
- ✳ *Management of Health and Safety at Work Regulations 1999;*
- ✳ *HSE Guidance Note HSG248 Asbestos, the analysts guide to sampling and analysis;*
- ✳ *HSE Guidance Note HSG247 Asbestos: The licensed contractors' guide; and*
- ✳ *CIRIA 733 Asbestos in soil and made ground: a guide to understanding and managing risks.*



If required, air monitoring in accordance with HSG248 will be undertaken intermittently throughout the duration of the works at a frequency to be determined by the contractor, entirely dependent on whether asbestos-impacted soils are being handled at any given time. In general terms, during any one monitoring period, ten standard monitoring pumps will be run throughout the day, for the appropriate time period to achieve the required limit of detection. These slides will be analysed immediately by the on-site UKAS-accredited laboratory.

Once any monitoring has been analysed by the on-site UKAS-accredited laboratory, the results will be delivered to the resident engineer who will then follow the correct site procedure. The results will then be included within the verification report.



6. GEOTECHNICAL ENGINEERING SPECIFICATION

6.1. E3P GEOTECHNICAL ENGINEERING SPECIFICATION

The overarching philosophy of the site enabling works will be the delivery of the following:

- ✚ Preparation of plot footprint (+ 2 m on all elevations) to be suitable for ground improvement by vibro-stone column, where depth of stiff clay/medium-dense sands exceeds 1.5 m from proposed finished floor level (FFL).
- ✚ Preparation of plots to be suitable for construction with shallow spread foundation where firm to stiff clay and medium-dense sands are present at a depth < 1.5 m from proposed FFL across the complete plot.
- ✚ Preparation of plots for piled foundations.
- ✚ Engineer all areas of proposed adopted road and private drive to be compliant with the E3P Geotechnical Specification with CBR and elevation defined by the client.

In the event that it is not possible to prepare the site in a manner that will achieve the required foundation solution, the supervising engineer and client should be contacted at the first available opportunity.

The contractor should employ a suitably experienced engineer to be present on site during these earthwork operations to ensure soil suitability, placement, compaction and testing is undertaken in accordance with this specification and to ensure that any unforeseen circumstances, such as adverse weather, do not compromise the earthworks process.

Works should be halted during periods of intermittent or prolonged rainfall to ensure the materials are not placed in a manner that would result in softening of either the formation or the newly placed material. It will be the contractor's responsibility to determine appropriate weather conditions and determine the suitability of works.

Particular attention must be given to variable weather conditions when re-engineering clay soils as a moisture content fluctuation ($\pm 2\%$) of the tolerable limit will result in an unacceptable degree of compaction loss.

6.2. LOCALLY-WON FILL MATERIAL

It is proposed to upfill and level the site with material won from the development area. From the site-specific investigations undertaken to date, it is expected that the majority of the soils won from the processing of demolition material will be granular and cohesive soil matrices.

Due to climatic weather conditions and variance in long-term differential settlement associated with even well-compacted granular soils, and the need to facilitate future re-engineering using vibro-replacement stone columns to support a shallow reinforced strip foundation, it is essential that the cut-and-fill process is well controlled and materials are placed/compacted in accordance with this specification.

Where site-won materials are to be used as fill to achieve the required development platform, they must be compacted to ensure in-situ densities that are in excess of 95% of the maximum dry density, as determined using a 4.5 kg laboratory Proctor test.

Materials should only be compacted when the actual moisture content is within 2% ($\pm$) of the optimum for the soil matrices as determined by laboratory bench testing.



6.3. CLASSIFICATION OF FILL MATERIAL

This specification should be read in conjunction with the following:

- ✳ The Manual of Contract Documents for Highway Works, Volume 1, Specification for Highway Works, Series 600, Earthworks as amended in February 2016; and
- ✳ BS 1377-1:2016 Methods of test for soils for civil engineering purposes. General requirements and sample preparation

6.3.1. GENERAL CLASSIFICATION

The contractor should ensure that all earthworks materials comply with Clause 601 of the *Specification for Highway Works* and shall fall into one of the following general classifications as defined in Table 6/1 of the *Specification for Highway Works*.

- ✳ General granular fill (Class 1);
- ✳ General cohesive fill (Class 2), excluding Class 2A and 2E; or
- ✳ Selected granular fill (Class 6).

6.3.2. PRE-COMMENCEMENT EARTHWORKS TESTING FREQUENCY / PERFORMANCE

To determine the geotechnical classifications of any material to be placed and compacted in layers, representative samples will be taken at a frequency of **1 per 2,000m³** and submitted for particle size distributions (PSDs). Maximum Dry Density and Natural and Optimum Moisture Content determinations.

To determine the geotechnical classifications of any cohesive material to be placed and compacted in layers, representative samples will be taken (following removal of any inclusions of oversize material, metal, timber, plastic, etc.) at a frequency of **1 per 1,000m³** and submitted for liquid and plastic limits, plasticity index and natural moisture content determinations. Organic matter determinations shall be prescribed at the discretion of the supervising consultant, dependent on visual observations.

Representative samples of all proposed backfill shall be taken at a frequency of **1 per 3000m³ (minimum 3nr)** and submitted for Dry Density / Optimum Moisture Content analysis using either a 4.5Kg or 2.5kg rammer to determine the optimum moisture content and maximum dry density for the engineering of structural fill.

For an unaltered fill material to be deemed suitable for use, the natural moisture content must be within 2% (+/-) of the optimum to achieve the required maximum dry density. Where the laboratory test indicates that the soil parameters are outside this requirements, stabilising agents should be added to assess suitability for use to the contractors own design.



TABLE 6.1 E3P EARTHWORKS GEOTECHNICAL COMPACTION SPECIFICATION

SOIL/MATERIAL TYPE	CLASS	DESCRIPTION	COMPACTION EQUIPMENT	LAYER THICKNESS	ROLLER PASSES
Granular Fill (Sand and Gravel Matrices)	1 A	Sandy Gravel with some cobbles	> 5000 kg vibrating roller	225 mm	4
	1 B	Sand or Gravel of same grading size	> 5000 kg vibrating roller	250 mm	10
	1 C	Coarse gravels with many cobbles	> 5000 kg vibrating roller	400 mm	5
Cohesive Fill (Clay with Minor Sand and Gravel Component)	2 A	Wet Clay	> 1000 kg vibrating tamping roller (sheep foot only)	100–225 mm	3
	2 B	Dry Clay	> 5000 kg vibrating roller or 1400 kg tamping (trench roller)	225 mm or 125 mm	4 or 12
	2 C	Gravelly Clay	> 5000 kg vibrating roller or 1400 kg tamping (trench roller)	225 mm or 125 mm	4 or 12
	2 D	Silty/Sandy Clay	> 5000 kg vibrating roller or 1400 kg tamping (trench roller)	225 mm or 125 mm	4 or 12
Recycled Aggregate Crush (< 125 mm Well Graded)	6F2	Any combination of inert hard materials, other colliery spoil, or rock with substantial amounts of clay-like component	> 5000 kg vibrating roller	250 mm	6



6.3.3. USE OF FILL MATERIALS

In addition to any grading requirement, the maximum particle size of any fill material shall be no more than two-thirds of the compacted layer thickness except that cobbles having an equivalent diameter of more than 150 mm shall not be deposited within the restored surface level unless directed otherwise by the engineer. Un-burnt colliery spoil, pulverised fuel ash or furnace bottom ash shall not be used as a fill material.

6.4. GENERAL REQUIREMENTS

The contractor shall employ only plant and working methods that are suited to the materials to be handled and traversed. The contractor shall be responsible for maintaining the nature of the acceptable material so that when it is placed and compacted it remains acceptable in accordance with the contract.

For the purposes of this contract, the proposed earthworks requirements have been split into distinct end use categories, with the corresponding requirements for the earthworks specification assigned to individual areas.



TABLE 6.2 COMPACTION/BACKFILL REQUIREMENTS

LAND USE REQUIREMENT	COMPACTION METHODOLOGY AND GENERAL PERFORMANCE CRITERIA
Traditional Spread Foundation	Ensure no disturbance of natural soil at shallow depth.
Re-Engineering of Soils Using Vibro-Replacement Stone Column (VRSC)	Materials to be placed in a controlled manner to facilitate the construction of vibro-replacement stone columns (VRSC). to limit differential settlement and increase net Allowable Bearing Pressure (ABP) These works are to be completed within the building structure footprint and +2 m of all elevations. Material must be 90% granular in composition with less than 10% fines (which are classified as materials < 0.6 microns in size). No material greater than 125 mm in size is permitted, with 90% of the soils placed conforming to grading < 90 mm. Material is to be placed when actual moisture content is within tolerable limits of the optimum, with specific attention to soils that are notably wetter than the optimum. Material to be placed in a manner so as to ensure a minimum CBR of 5% at formation to facilitate machine movement and piling mat construction. Where site-won materials are used to upfill, levels must be compacted to an “end product” performance specification where the in-situ density exceeds 95% of the maximum (determined by laboratory conditions). Where rock is present at a shallow depth, the remediation contractor will ensure the substratum is prepared to ensure that a minimum of 1000 mm of appropriately graded granular material is present to the underside of the proposed doubly reinforced concrete strip foundation. The substratum must be prepared to ensure a vibro-stone column treatment depth is not less than 80% of the immediate adjacent profile.
Piled Foundation	All plot footprint (+ 2 m) must be free of any deleterious elements, tree roots and obstructions > 150 mm. Where upfill is proposed, material is to be placed using method compaction specification to achieve a CBR as required by the developer for piling mat construction. Piling mat is to be placed and constructed in accordance with the approved geotechnical engineer’s temporary works design.



Adopted Highways (+ 2 m from Back of Footpath)	<i>Method Compaction – MCHW Specification For Highway Works Series 600</i> is to be followed, with in-situ validation testing to meet requirement of adoptions authority. A CBR > 5% is required at subgrade formation (prior to placement of capping).
Estate Roads	<i>Method Compaction – MCHW Specification For Highway Works Series 600</i> is to be followed to achieve a CBR > 5%.
Gardens, POS and Other External Areas	Material is to be placed in layers not exceeding 300 mm and must be rolled using dedicated plant (no earth moving equipment) and in general compliance with the requirements of <i>MCHW Specification For Highway Works Series 600</i> .

Acceptability shall be determined in accordance with Table 6/1 of the *Specification for Highway Works*.

Laboratory testing for the purposes of determining acceptability and compaction requirements will be conducted by the engineer.

Haulage of material to embankments or other areas of fill shall proceed only with sufficient spreading and compaction. Plant is operating at the place of deposition to ensure compliance with Clause 612 of the *Specification for Highway Works*.

No excavated acceptable material or unacceptable material required to be processed, other than surplus to the requirements of the contract, shall be removed from the site.

Where the excavation reveals a combination of acceptable and unacceptable materials, the contractor shall carry out the excavation in such a manner that the acceptable materials are excavated separately for use in the permanent works without contamination by the unacceptable materials. Unless otherwise described in the contract, classes of fill material required to be deposited separately shall be excavated separately without contamination by other classes of material.

The contractor shall make their own arrangements for the stockpiling of acceptable material, and unacceptable material to be processed, and for the provision of site for this purpose.

The contractor shall ensure that they do not adversely affect the stability of excavations or fills by their methods of stockpiling materials, use of plant or siting of temporary buildings or structures.

Topsoil shall, wherever practicable, be used immediately after its stripping and, if not, shall be stored in stockpiles of heights not exceeding 2 m. Topsoil shall not be stockpiled for more than two years. Topsoil shall not be unnecessarily trafficked, either before stripping or when in a stockpile. Stockpiles shall not be surcharged or otherwise loaded and multiple handling shall be kept to a minimum.

Excavations requiring backfilling shall remain open only for the minimum period necessary.



The contractor shall keep earthworks free of water, including:

- ✳ Arranging the rapid removal of water:
 - shed on to the earthworks; and
 - entering the earthworks from any source;
- ✳ Provide, where necessary, temporary watercourses, drains, pumping and the like;
- ✳ Discharge accumulated water and groundwater into the permanent outfalls of the drainage system where practicable; and
- ✳ Provide adequate means for trapping silt on temporary systems discharging into permanent drainage systems.

The contractor shall carry out and maintain groundwater lowering or other treatment as required.

Where materials are designated either Class U1B or Class U2 (according to the *Specification for Highway Works*), the contractor shall carry out any special requirements for their handling. Where such materials are encountered during the progress of the works, the contractor shall make all necessary arrangements for their safe handling and disposal after consultation with the appropriate environmental authority.

6.4.1. CONSTRUCTION OF FILLS – HIGHWAYS

All fills shall be constructed:

- ✳ In the locations as shown in the contract drawings to the lines and levels stated therein;
- ✳ Of classes of material complying with this specification;
- ✳ By deposition, as soon as practicable after excavation, in layers to meet the compaction requirements as required for each class of material as specified; and
- ✳ To the requirements of this clause and any other requirements for fill in this specification.

Before commencing work on any area of fill, the contractor shall ensure that:

- ✳ The base is sound and stable by excavating and removing any topsoil as soft subsoil;
- ✳ Base layers are not exposed until the fill layer is ready for placement; and
- ✳ Uncompacted material on the side slopes of previously backfilled zones shall be removed and benches of between 1.0 m and 1.5 m height cut in compacted fill immediately prior to deposition of the new fill to ensure that the new backfill placed against the slope is properly integrated.

Whenever fill is to be placed on surfaces inclined at 1 vertical to 7 horizontal or steeper, the surface shall be benched immediately prior to deposition of the fill in order to achieve horizontal basal surfaces. The benches shall be between 1.0 m and 1.5 m in height.



Areas of fill shall, unless otherwise permitted by the engineer, be constructed evenly over their fullest possible extent and the contractor shall carefully control and direct construction plant and other vehicular traffic uniformly over the area of compacted fill. The minimum plan dimensions of any one panel of backfilling shall be properly integrated with areas of previous backfilling. Damage by construction plant and other vehicular traffic shall be made good by the contractor with material having the same characteristics and strength as the material had before it was damaged.

Temporary slopes within compacted and uncompacted backfill shall be formed at gradients that ensure stability.

6.4.2. CONSTRUCTION OF FILLS – ADOPTED HIGHWAYS, ESTATE ROADS AND CAR PARK

The contractor shall carry out compaction upon the materials that require to be compacted, as soon as practicable after deposition.

Compaction shall be either method as required for the classes of fill in Table 6/1 that require to be compacted.

The contractor shall obtain permission from the overseeing organisation before carrying out compaction requirements as listed in Table 6/1 for the class of material being compacted.

Method compaction shall be undertaken using the plant and methods appropriate to the compaction requirements as listed in Table 6/1 for the class of material being compacted.

Earthmoving plant shall not be accepted as compaction equipment nor shall the use of a lighter category of plant to provide any preliminary compaction to assist the use of heavier plant be taken into account when assessing the amount of compaction required for any layer.

If more than one class of material is being used in such a way that it is not practicable to define the areas in which each class occurs, the contractor shall compact with plant operating as if only the material which required the greater compaction effort is being compacted.

If the results of field tests show densities that indicate the state of the compaction to be inadequate, then if this is due to failure of the contractor to comply with requirements of the contract, the contractor shall carry out such further work as is required to comply with the contract.

Refer to Clause 612/10 of the *MCHW Specification for Highway Works* for definition of plant to be used in accordance with these specified works.

The contractor will be responsible for assessing the class of fill in accordance with Table 6/1 of the *Specification for Highway Works*. Table 6/4 of the *Specification for Highway Works* should then be employed to assess the method of compaction to be employed. The test results and method statements shall be submitted to the consulting engineers for approval.

6.4.3. UNACCEPTABLE MATERIAL

The contractor is solely responsible for ensuring full and detailed analysis of all reported ground conditions and areas of risk in terms of the potential for unacceptable material to be present within the proposed earthworks. Limitations in the available information should be highlighted to the supervising engineer prior to the commencement of earthworks. The contractor is to make full and unequivocal arrangements to investigate the potential presence for unsuitable materials within the earthworks and



construction of highway fill. All unsuitable materials are to be identified for removal in accordance with this specification.

Unacceptable material Class U1A shall be:

Material which does not comply with the permitted constituents and material properties of MCHW Table 6/1 and contract specific Appendix 6/1 for acceptable material; and;

Material, or constituents of materials, composed of the following unless otherwise described in contract specific Appendix 6/1:

- ✳ Peat, materials from swamps, marshes and bogs;
- ✳ Logs, stumps and perishable material;
- ✳ Materials in a frozen condition;
- ✳ Clay having a liquid limit determined in accordance with BS 1377: Part 2, exceeding 90 or plasticity index determined in accordance with BS 1377: Part 2, exceeding 65; and,
- ✳ Material susceptible to spontaneous combustion except unburnt colliery spoil complying with sub-Clause 15 of this Clause;(ii)unacceptable material

Unacceptable material Class U1B shall be:

Contaminated materials, including controlled wastes (as defined in the Environmental Protection Act 1990 Part IIA) whose level of contamination is above that given either in contract specific Appendix 6/14 or in contract specific Appendix 6/15, but excluding all hazardous wastes (as Volume 1 Series 600 Specification for Highway Works Earthworks W2 Amendment – February 2016 defined in the Hazardous Waste (England and Wales) Regulations 2005) and radioactive wastes (as defined in the Radioactive Substances Act 1993).3(02/16).

Unacceptable material Class U2 shall be:(i) hazardous waste (as defined in the Hazardous Waste (England and Wales) Regulations 2005) and radioactive waste (as defined in the Radioactive Substances Act 1993).4(02/16).

Where required in contract, unacceptable material (other than Class U2) shall be processed by mechanical, chemical or other means to render the material acceptable for use in the permanent works in accordance with the requirements of Table 6/1 and contract specific MCHW Appendix 6/1.



6.5. EARTHWORKS MATERIAL TESTS

Prior testing of the potential sources of fill shall be undertaken by the contractor and submitted to the consulting engineers for approval. This testing shall include, but not necessarily be limited to, the compaction and backfill requirements detailed in Table 6.3.

TABLE 6.3 COMPACTION/BACKFILL REQUIREMENTS

LAND USE	COMPACTION METHODOLOGY and GENERAL PERFORMANCE CRITERIA				
Liquid and Plastic Limits	BS 1377: Part 2				
Grading	BS 1377: Part 2				
Uniformity Coefficient	Calculated from grading curve				
Moisture Content Multi-point moisture condition value (MCV) (to assess optimum moisture content).	BS 1377: Part 2				
Organic Matter (Maximum 2.5% Total Organic Content)	BS 1377: Part 3				
Water Soluble Sulphate	TRL Report 447 Test No 1				
Total Sulphate Content	TRL Report 447 Test No 4				
Earthwork In-situ Tests Subsequent to the filling and compaction of the material, a series of in-situ tests shall be undertaken to confirm the success of the compaction process. This testing shall include, but necessarily be limited to, the following: <table><tr><td>Test</td><td>Test Method</td></tr><tr><td>Plate Load Tests (Equivalent CBR of 5%)</td><td>BS 1377: Part 9</td></tr></table>	Test	Test Method	Plate Load Tests (Equivalent CBR of 5%)	BS 1377: Part 9	Clause 632 (BS 1377: Part 4)
Test	Test Method				
Plate Load Tests (Equivalent CBR of 5%)	BS 1377: Part 9				
Disposal of Materials The contractor shall be responsible for the safe disposal of any excess of unsuitable material found on the site.					
Proctor Compaction Testing	BS 1377: Part 4				

6.6. SPECIFICATION FOR GROUND IMPROVEMENT BY VIBRO-STONE COLUMN

The over-arching method and specification for the placement and compaction of non-compliant material where the fine constituent (< 0.63 micron) exceeds the standard requirements for ground improvement by VSC is given in Table 6.4 & 6.5.



TABLE 6.4 OVERVIEW OF WORKS OPERATIONS

Step 1	Carefully segregate materials excavated during civil engineering works (on site and import) into the following soil types: ✿ Sand/granular soils; ✿ Dry sandy clay; ✿ Wet clay soil; and ✿ Silt. Ensure all stockpiles are sealed to minimise water ingress in approved locations.
Step 2	Analyse bulk sample from each (site-won or imported) soil matrix as per the requirements of the E3P specification for: ✿ Dry density/optimum moisture content (Procter); and ✿ Particle size grading coefficient.
Step 3	On-site observations in conjunction with particle size distribution (PSD) grading will confirm the classification of material and thus the corresponding method for compaction.
Step 4	The dry density/moisture content testing should be used to ensure that the material is within $\pm 3\%$ of the optimum to ensure compaction can be achieved.
Step 5	The classified material should be placed and compacted in accordance with the corresponding method for the material under conditions where the moisture content is within the tolerable limits.
Step 6	Once placed and compacted, the required validation testing should be completed at formation to demonstrate compliance. The testing will include: ✿ In-situ density and air void ratio; ✿ Moisture condition value; and ✿ Undrained shear strength.



TABLE 6.5 COMPACTION AND VALIDATION OF NON-STANDARD MATERIAL BACKFILL TO VSC

REQUIRED PARAMETERS	THE COMPACTION MUST ACHIEVE THE FOLLOWING MATERIAL PARAMETERS:	
Verification Testing and Report	Bulk Density (ρ)	95% of the maximum dry density and must be within 3% of the optimum moisture content.
	All materials used for upfilling must be durable and inert.	
	In order to verify that the aforementioned material parameters have been attained, representative sampling and testing must be undertaken. All testing will be in accordance with BS EN ISO 17892-1:2014 and BS EN ISO 17892-2:2014. All testing is to be undertaken by a laboratory with the relevant UKAS accreditation. The following tests are required:	
	In-situ Density (ρ)	Approved methods of in-situ testing (i.e. calibrated nuclear density probe (NDP), sand replacement test).
	Moisture Content	Moisture content test.
	In-situ density testing on every 500 m ³ and in each layer of upfill well-spread over site within and around the proposed structures' footprint.	
	Testing must be from a range of depths throughout the treated fill. A minimum of six samples must be taken and tested.	
	A drawing depicting the location of each sample and test point must be provided along with a list of each point and the relevant test/sample depth. A list of all geotechnical testing results for each sample and test must be provided along with the relevant test certificates.	
	If the soils are not suitable, due to the moisture content being higher than the optimum moisture content, then lime modification may also be required.	
	The above is given strictly on the basis that it does not conflict with other elements of the project-specific requirements.	

6.7. CURRENT AND PROPOSED SITE TOPOGRAPHY AND SLOPE INTERACTION

The current and proposed site topography, changes in elevation and any existing or new slopes are beyond the scope of this specification. Where any earth slopes exceed a design gradient of 1(v) in 3(h) either on site or within the conjectured zone of structural influence, extreme care should be taken with a full and detailed geotechnical slope analysis to inform the retained design solution.



7. RECORD-KEEPING AND VERIFICATION

7.1. RECORD-KEEPING

During the course of the remediation and site enabling works, the on-site E3P consultant will undertake the following record-keeping protocols:

- ✚ Detailed daily site diary including material movements;
- ✚ Sampling register, testing results, photographs, details of locations of hydrocarbon-impacted soils (drawings), details of hotspot removals, details of consignment notes of any hydrocarbon-impacted material that is required to be disposed of off site; and
- ✚ Detailed surveys (volumes).

Record-keeping on site, in particular movements and analysis of specific material types, will be in the form of site diaries and a remediation excavation record. This record will remain on site and will be completed by the E3P on-site engineer during the course of the remediation and site enabling works.

7.2. VERIFICATION

The records listed above will then be compiled into a validation report produced by E3P on completion of the remediation and site enabling works, clearly referencing the origin of the materials used and testing carried out to confirm its suitability for use, where required. E3P will also prepare an as-built development drawing clearly detailing the materials present on site to be cross referenced with the supporting validation documentation.

The validation report will include the following:

- ✚ Remediation strategy (including copies of confirmation from regulatory authorities agreeing criteria);
- ✚ Detailed surveys of all excavations and production of as-built drawings for the earthworks;
- ✚ Copy of consignment notes relating to the movement of wastes to a licensed waste management facility;
- ✚ Detailed drawings showing all sampling locations for both chemical and geotechnical testing;
- ✚ Chemical test results;
- ✚ Geotechnical test results;
- ✚ Details of qualified persons signed declaration; and
- ✚ Monitoring results if undertaken (e.g. asbestos in air, gas water).



8. CONTINGENCY PLAN

8.1. PREVIOUSLY UNIDENTIFIED CONTAMINANTS

Should significantly impacted material be encountered during the development, then it will be excavated and stockpiled on an impermeable material and sampled and tested for an appropriate range of determinants.

Once the laboratory analysis of the material is available, an assessment will be undertaken to determine whether it can be retained on site as part of the material management plan or whether it should be disposed of off site.

Depending on the nature of any such impact, it may be necessary to undertake validation testing of the excavation faces in order to demonstrate that no such materials are left in situ.



9. SECOND PHASE MITIGATION AND MANAGEMENT – BUILD PHASE

This document details the construction works that are required to ensure full compliance with the remediation Strategy, Regulatory Authorities, Building Control & Warranty Providers;

The following should be implemented during the build phase of the development:

-  Chemical validation of any additional topsoil or subsoil imported for use within gardens;
-  Placement and validation of the 300 mm growing medium.

The validation protocols are presented within the E3P Remediation and Enabling Works Strategy and are presented below.

9.1. PLACEMENT OF GROWING MEDIUM

The Remediation and Enabling Works Strategy for the site, with respect to human health of the future site users includes the provision of a chemically suitable clean material to be installed in all gardens and landscaped areas.

It will be necessary to provide a 300 mm growing medium using certified material with appropriate validation within proposed gardens and landscaped areas. Natural drift deposits encountered within the upper 300 mm of finished ground levels can be directly overlain with a suitable cover (minimum 150 mm topsoil).

In accordance with the current requirements of the regulatory authorities, validation samples will be collected from all materials that are to be imported or re-used on site to confirm the proposed development will pose no unacceptable risk to human health or the wider environ.

Subsoil and topsoil shall be free of any deleterious materials, such as buildings materials, timber, plastics etc and conform to the requirements of BS 3882:2007.

Testing requirements for top-soil and sub-soil are presented in Table 9.1.

TABLE 9.1 SPECIFICATION FOR SOIL TESTING

MATERIAL USE	TESTING FREQUENCY	SUITE OF ANALYSIS
Subsoil Greenfield Source (150 mm Garden Cover)	1 Sample per 200 m ³	A/B/C/D
Subsoil Brownfield Source (150 mm Garden Cover)	1 Sample per 50 m ³	A/B/C/D
Topsoil Greenfield Source (150 mm Garden Cover)	1 Sample per 200 m ³	A/B/C/D
Topsoil Brownfield Source (150 mm Garden Cover)	1 Sample per 50 m ³	A/B/C/D
General Engineering Fill (Class 1 and 2 Soil)	1 Sample per 1000 m ³	A/B/C/D

Notes

Suites of Analysis:

- A. Speciated PAH.
- B. Speciated TPH (C5-C35).



- C. Asbestos (ID).
- D. CLEA Inorganic Heavy Metals.

9.1.1. PROCEDURE FOR PLACEMENT OF CHEMICALLY SUITABLE COVER SYSTEM

The placement of certified growing medium will be completed as part of the developer works/build-phase mitigation plan.

Gardens and landscaped areas need to be backfilled with 150 mm chemically validated topsoil overlying the natural drift deposits. Topsoil is required to be confirmed as chemically suitable prior to placement.

The placement of clean material will be undertaken during the build phase works of the project.

If proposed utilities are to be placed within the cover system, the clean cover should be placed prior to installation of these utilities.

If natural drift deposits are encountered, excavation can cease here.

E3P will collect photographic evidence of the placement of 150 mm of certified topsoil and 150 mm of subsoil on completion of construction works. This element will also be checked by the Building Control Officer as part of the site completion prior to issuing of a CML certificate.

The garden validation procedure is detailed in Table 9.2.

TABLE 9.2 GARDEN VALIDATION PROCEEDURE

PROCEDURE	METHOD
Chemical Validation	Topsoil and subsoil will need to be chemically analysed to confirm suitability for use with the proposed cover system prior to installation and completion of the garden systems. E3P will issue an email to the appropriate party with an assessment of the chemical suitability of both sub soils and top soils. If acceptable the materials can be installed to the required depth at which time the plot will be deemed complete following a validation procedure by a suitability qualified E3P engineer.
Trial Holes	Trial holes are deemed necessary to demonstrate the depth of topsoil overlying the natural drift deposits or placed subsoil.
Validation	Photographic evidence will be taken by E3P of the topsoil placement demonstrating the depth of topsoil and practical completion of works are required for each and every plot.
Validation Certificate	Once the photographs of the placement of topsoil (over the clean material) have been provided, E3P will issue a plot specific validation certificate to demonstrate that the required subsoil and topsoil has been placed in the required garden plots along with the chemical analysis.
Completion Report	Upon completion of all garden and landscaped areas within the development, a Completion Report will be issued providing the confirmation that all remediation requirements have been achieved.

Plate 1 provides an example of a garden validation photographs that will be required for each plot.



PLATE 1 **EXAMPLE PLOT COVER SYSTEM VALIDATION**

Plot No: 70		
	0.00-0.15	Validated TOPSOIL
Depth of Strata (m bgl)	0.15-0.60	Validated SUBSOIL
Depth of Cover System Materials		Depth of Cover System Materials
		
Depth of Cover System at Ground Level		Depth of Cover System in Relation to Plot
		



9.2. POTABLE WATER SUPPLY – CONTAMINANT ASSESSMENT CRITERIA

Table 9.3 provides a summary of the threshold concentrations that must not be exceeded within remediated ground at pipeline depth in order to PE pipe works to be acceptable for the proposed development.

TABLE 9.3 PIPELINE SELECTION PE THRESHOLD CONCENTRATIONS

Contaminant Group	PE-threshold
Total VOC	0.5
Total BTEX And MTBE	0.1
Total SVOCs (Excluding PAH and those substances marked with an *)	2
EC5-EC10 Aliphatic and Aromatic Hydrocarbons	2
EC10-EC16- Aliphatic and Aromatic Hydrocarbons	10
EC16-EC40 Aliphatic and Aromatic Hydrocarbons	500
Phenols (From SVOC Analysis)*	2
Cresols and Chlorinated Phenols (From SVOC Analysis)	2
Ethers*	0.5
Nitrobenzene*	0.5
Ketones*	0.5
Aldehydes*	0.5
Amines	Fail

Upon completion of the remedial works a full UKWIR Risk Assessment should be undertaken.

END OF REPORT



APPENDIX I

LIMITATIONS

1. This report and its findings should be considered in relation to the terms of reference and objectives agreed between E3P and the Client as indicated in Section 1.2.
2. For the work, reliance has been placed on publicly available data obtained from the sources identified. The information is not necessarily exhaustive and further information relevant to the site may be available from other sources. When using the information it has been assumed it is correct. No attempt has been made to verify the information.
3. This report has been produced in accordance with current UK policy and legislative requirements for land and groundwater contamination which are enforced by the local authority and the Environment Agency. Liabilities associated with land contamination are complex and requires advice from legal professionals.
4. During the site walkover, reasonable effort has been made to obtain an overview of the site conditions. However, during the site walkover, no attempt has been made to enter areas of the site that are unsafe or present a risk to health and safety, are locked, barricaded, overgrown, or the location of the area has not been made known or accessible.
5. Access considerations, the presence of services and the activities being carried out on the site limited the locations where sampling locations could be installed and the techniques that could be used.
6. Site sensitivity assessments have been made based on available information at the time of writing and are ultimately for the decision of the regulatory authorities.
7. Where mention has been made to the identification of Japanese Knotweed and other invasive plant species and asbestos or asbestos-containing materials, this is for indicative purposes only and do not constitute or replace full and proper surveys.
8. The executive summary, conclusions and recommendations sections of the report provide an overview and guidance only and should not be specifically relied upon without considering the context of the report in full.
9. E3P cannot be held responsible for any use of the report or its contents for any purpose other than that for which it was prepared. The copyright in this report and other plans and documents prepared by E3P is owned by them and no such plans or documents may be reproduced, published or adapted without written consent. Complete copies of this may, however, be made and distributed by the client as is expected in dealing with matters related to its commission. Should the client pass copies of the report to other parties for information, the whole report should be copied, but no professional liability or warranties shall be extended to other parties by E3P in this connection without their explicit written agreement there to by E3P.
10. New information, revised practices or changes in legislation may necessitate the re-interpretation of the report, in whole or in part.



APPENDIX II

GLOSSARY

TERMS

ACM	Asbestos-containing material	MMP	Materials management plan
ADS	Acoustic design statement	ND	Not detected
AST	Above-ground storage tank	NDP	Nuclear density probe
BGS	British Geological Survey	NMP	Noise management plan
BSI	British Standards Institute	NPSE	Noise policy statement for England
BTEX	Benzene, toluene, ethylbenzene, xylenes	NR	Not recorded
CA	Coal Authority	PAH	Polycyclic aromatic hydrocarbon
CBR	California bearing ratio	PCB	Polychlorinated biphenyl
CIEH	Chartered Institute of Environmental Health	PI	Plasticity index
CIRIA	Construction Industry Research Association	PID	Photo ionisation detector
CLEA	Contaminated land exposure assessment	POS	Public open space
CML	Council of Mortgage Lenders	PPE	Personnel protective equipment
CoC	Contaminants of concern	ProPG	Professional practice guidance
CSM	Conceptual site model	QA	Quality assurance
DNAPL	Dense non-aqueous phase liquid (chlorinated solvents, PCB)	SGV	Soil guideline value
DWS	Drinking water standard	SPH	Separate-phase hydrocarbon
EA	Environment Agency	SPT	Standard penetration test
EQS	Environmental quality standard	SVOC	Semi-volatile organic compound
FFL	Finished floor level	TPH	Total and speciated petroleum hydrocarbon
GAC	General assessment criteria	TPH CWG	Total Petroleum Hydrocarbon (Criteria Working Group)
GL	Ground level	UKWIR	United Kingdom Water Infrastructure Risk
GSV	Gas screening value	UST	Underground storage tank
HCV	Health criteria value	VCC	Vibro-concrete column
ICSM	Initial conceptual site model	VOC	Volatile organic compound
LEL	Lower explosive limit	VRSC	Vibro-replacement stone columns
LMRL	Lower method reporting limit	VSC	Vibro-stone columns
LNAPL	Light non-aqueous phase liquid (petrol, diesel, kerosene)	WHO	World Health Organisation
MCV	Moisture condition value	WRAP	Waste and Resources Action Programme
MIBK	Methyl isobutyl ketone	WTE	Water table elevation



Land South of Lickers Lane

Remediation and Enabling Works Strategy

August 2022


m	Metres	ppm	Parts per million
km	Kilometres	mg/m³	Milligram per metre cubed
% v/v	Percent volume in air	m bgl	Metres below ground level
mb	Millibars (atmospheric pressure)	m bcl	Metre below cover level
l/hr	Litres per hour	mAOD	Metres above ordnance datum (sea level)
µg/l	Micrograms per litre (parts per billion)	kN/m²	Kilonewtons per metre squared
ppb	Parts per billion	µm	Micrometre
mg/kg	Milligrams per kilogram (parts per million)	SSRT	Site Specific Remediation Target
PSD	Particle Size Distribution	DD	Dry Density
CL:AIRE	Contaminated Land: Applications in Real Environments	Mc	Moisture Content
ρ	Bulk Density	GPR	Ground Penetrating Radar
NDP	Nuclear Density Probe	FFL	Finished Floor Level
LEL	Lower Explosive Limit	UKWIR	UK Water Industry Research
CIRIA	Construction Industry Research and Information Association	LOD	Limit of Detection



APPENDIX III

DRAWINGS

DRAWING 15-065-001 – SITE LOCATION PLAN

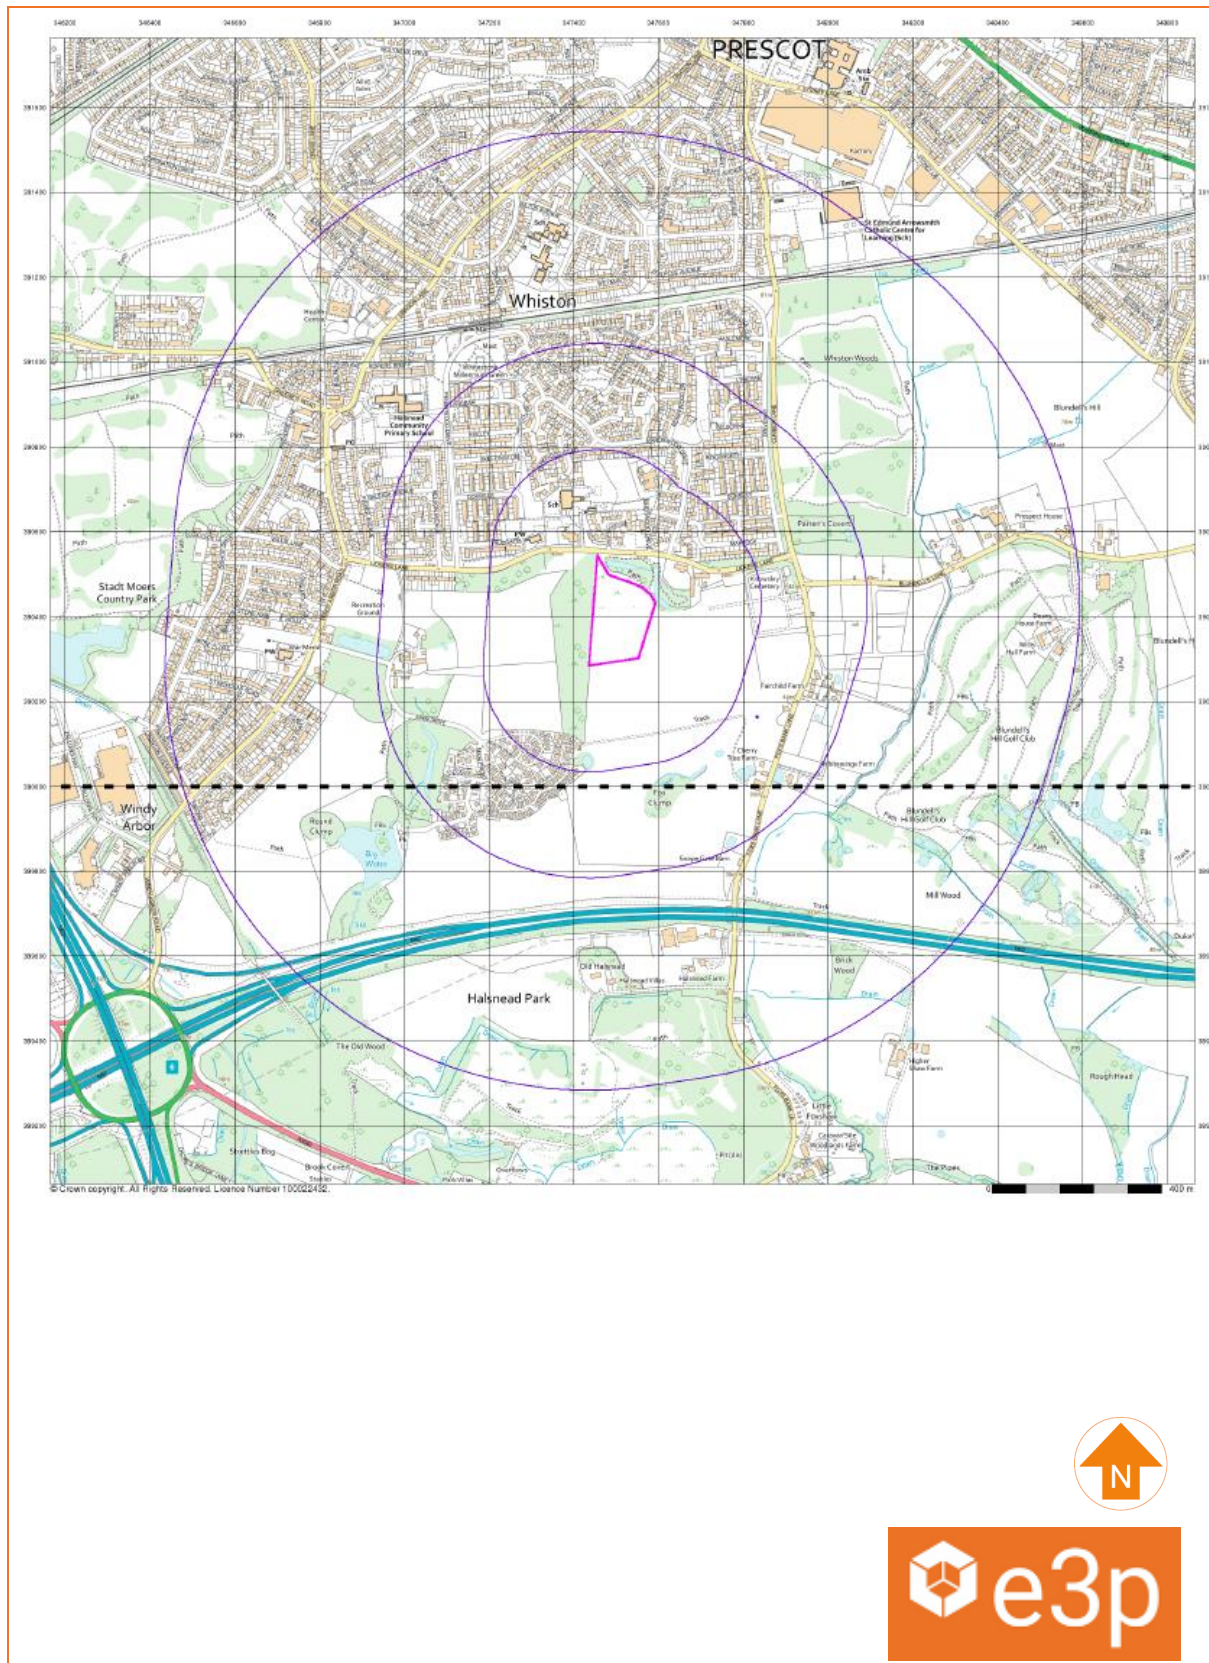



Notes:				
P1	REVA	21.07.2022	EB	NS
Phase	Issue	Date	Drawn	Checked


Client:	
Vistry	
Job Title:	
Hainsead, Lickers Lane	

Job No:	15-065	Date:	21.07.2022
Drawing No:	002	Scale:	NTS@ A3
Drawing Title:		Proposed Development Plan	



Environmental Engineering
Partnership Ltd
Taylor Road, Trafford Park
Urmston, Manchester, M41 7JQ
Tel: 0161 707 9612
E-mail: info@e3p.co.uk
Website: www.e3p.co.uk

The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.

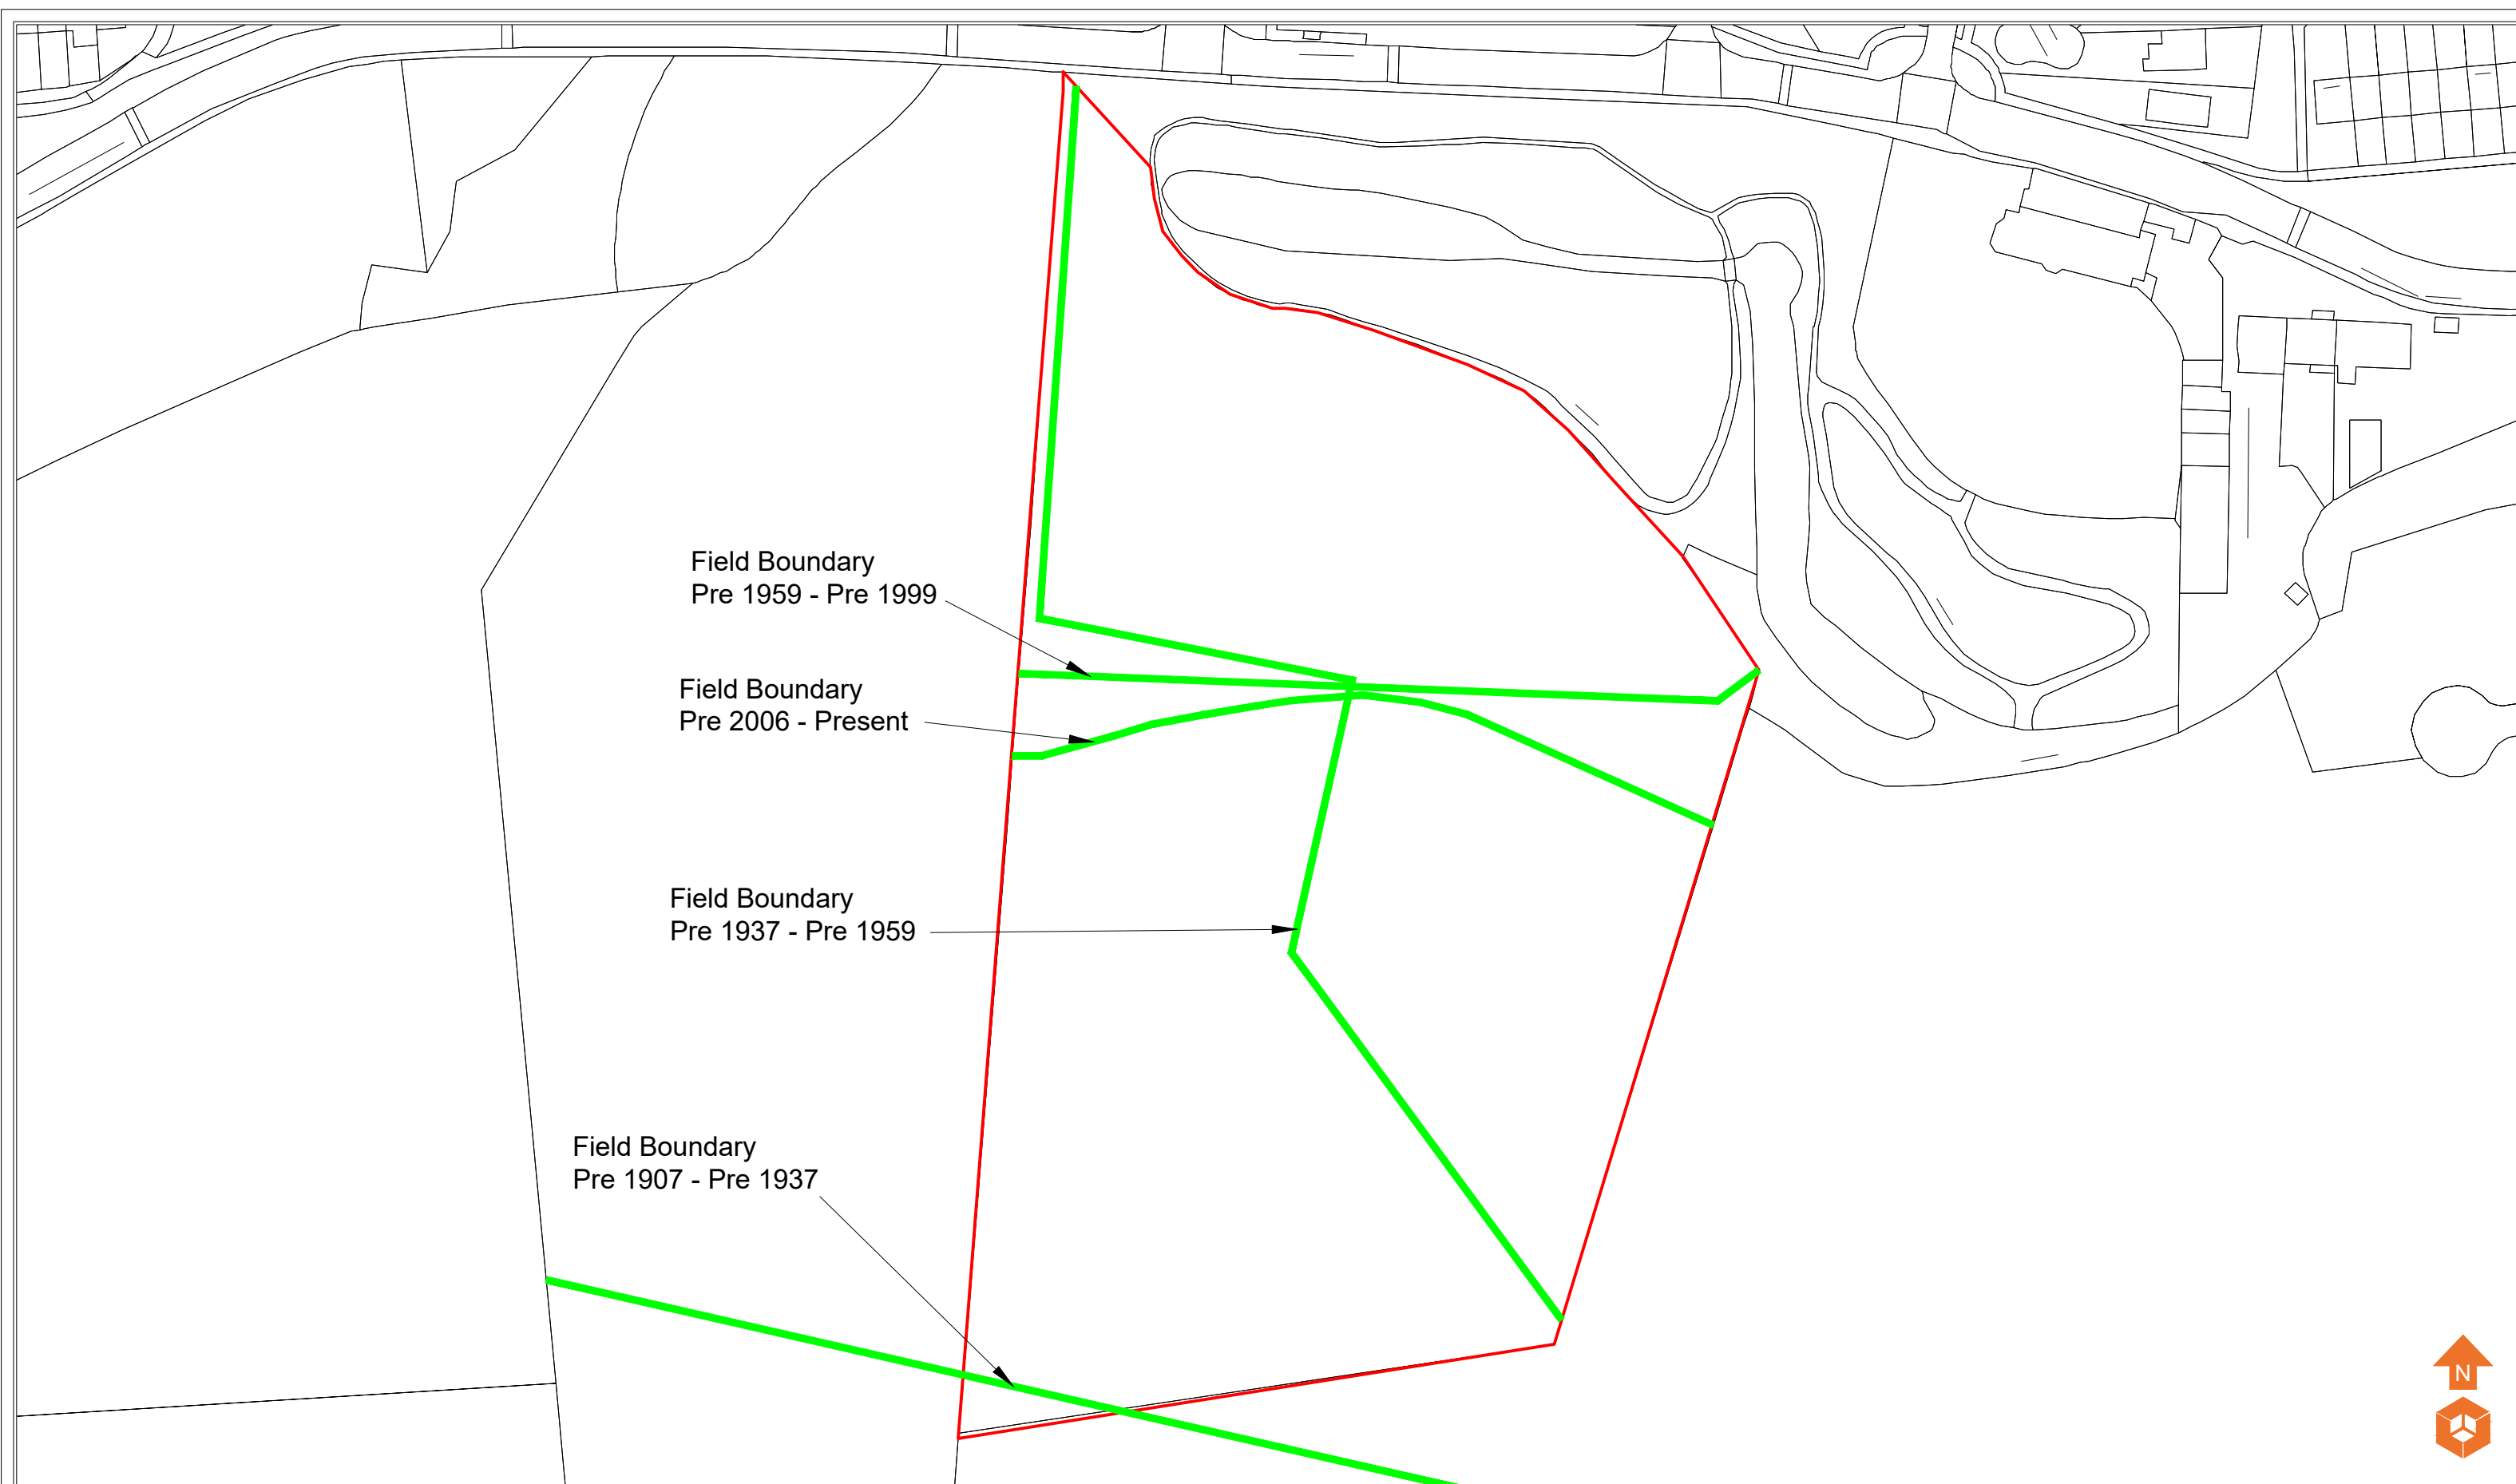

Historical Features
Field Boundary

Notes:				

Client:
Vistry

Job No:
15-065
Drawing No:
003

Date:
20.10.2021
Scale:
NTS@ A3




Environmental Engineering
Partnership Ltd
Taylor Road, Trafford Park
Urmston, Manchester, M41 7JQ
Tel: 0161 707 9612
E-mail: info@e3p.co.uk
Website: www.e3p.co.uk

P1	REVA	20.10.2021	CB	RH
Phase	Issue	Date	Drawn	Checked


Job Title:
Halnsead, Lickers Lane

Drawing Title:
Historical Features Plan


The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.

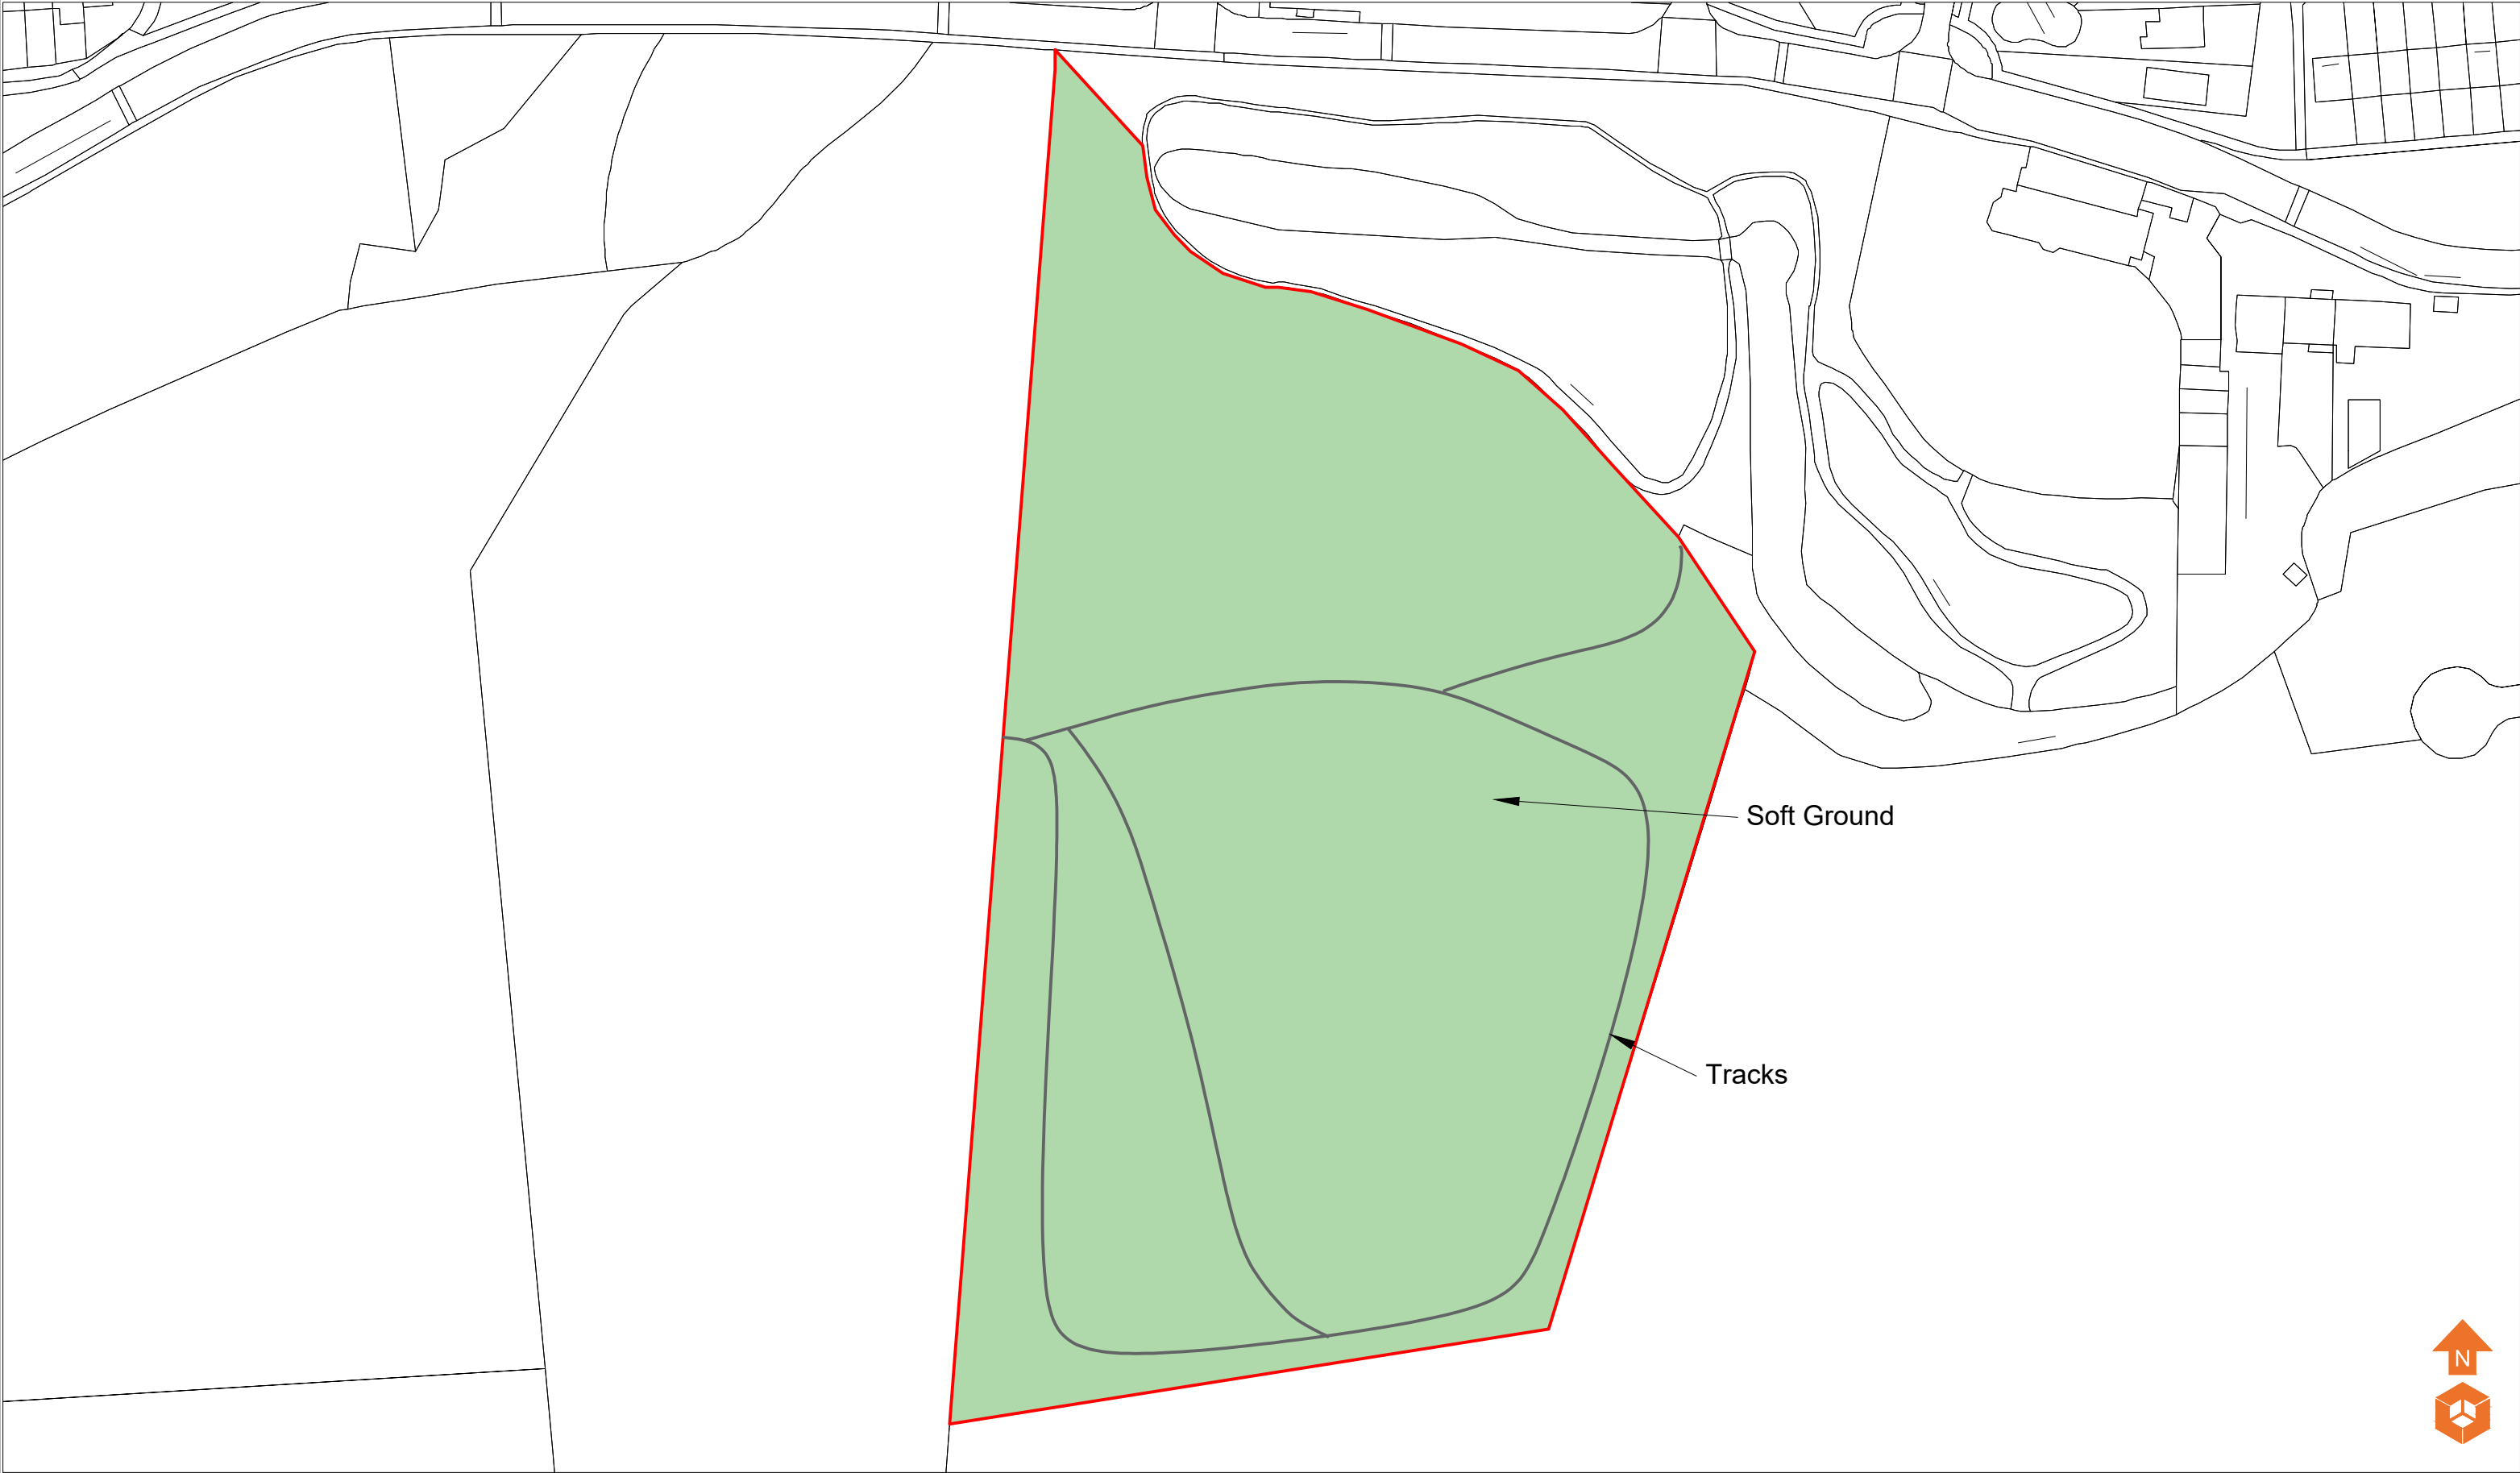

Site Features Soft Ground Tracks	Notes:					Client: Vistry	Job No: 15-065	Date: 27.10.2021	e3p Environmental Engineering Partnership Ltd Taylor Road, Trafford Park Urmston, Manchester, M41 7JQ Tel: 0161 707 9612 E-mail: info@e3p.co.uk Website: www.e3p.co.uk	
							Drawing No: 004	Scale: NTS@ A3		
						Job Title: Hainsead, Lickers Lane	Drawing Title: Site Features Plan			The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.
	P1	REVA	27.10.2021	EB	RH					
	Phase	Issue	Date	Drawn	Checked					

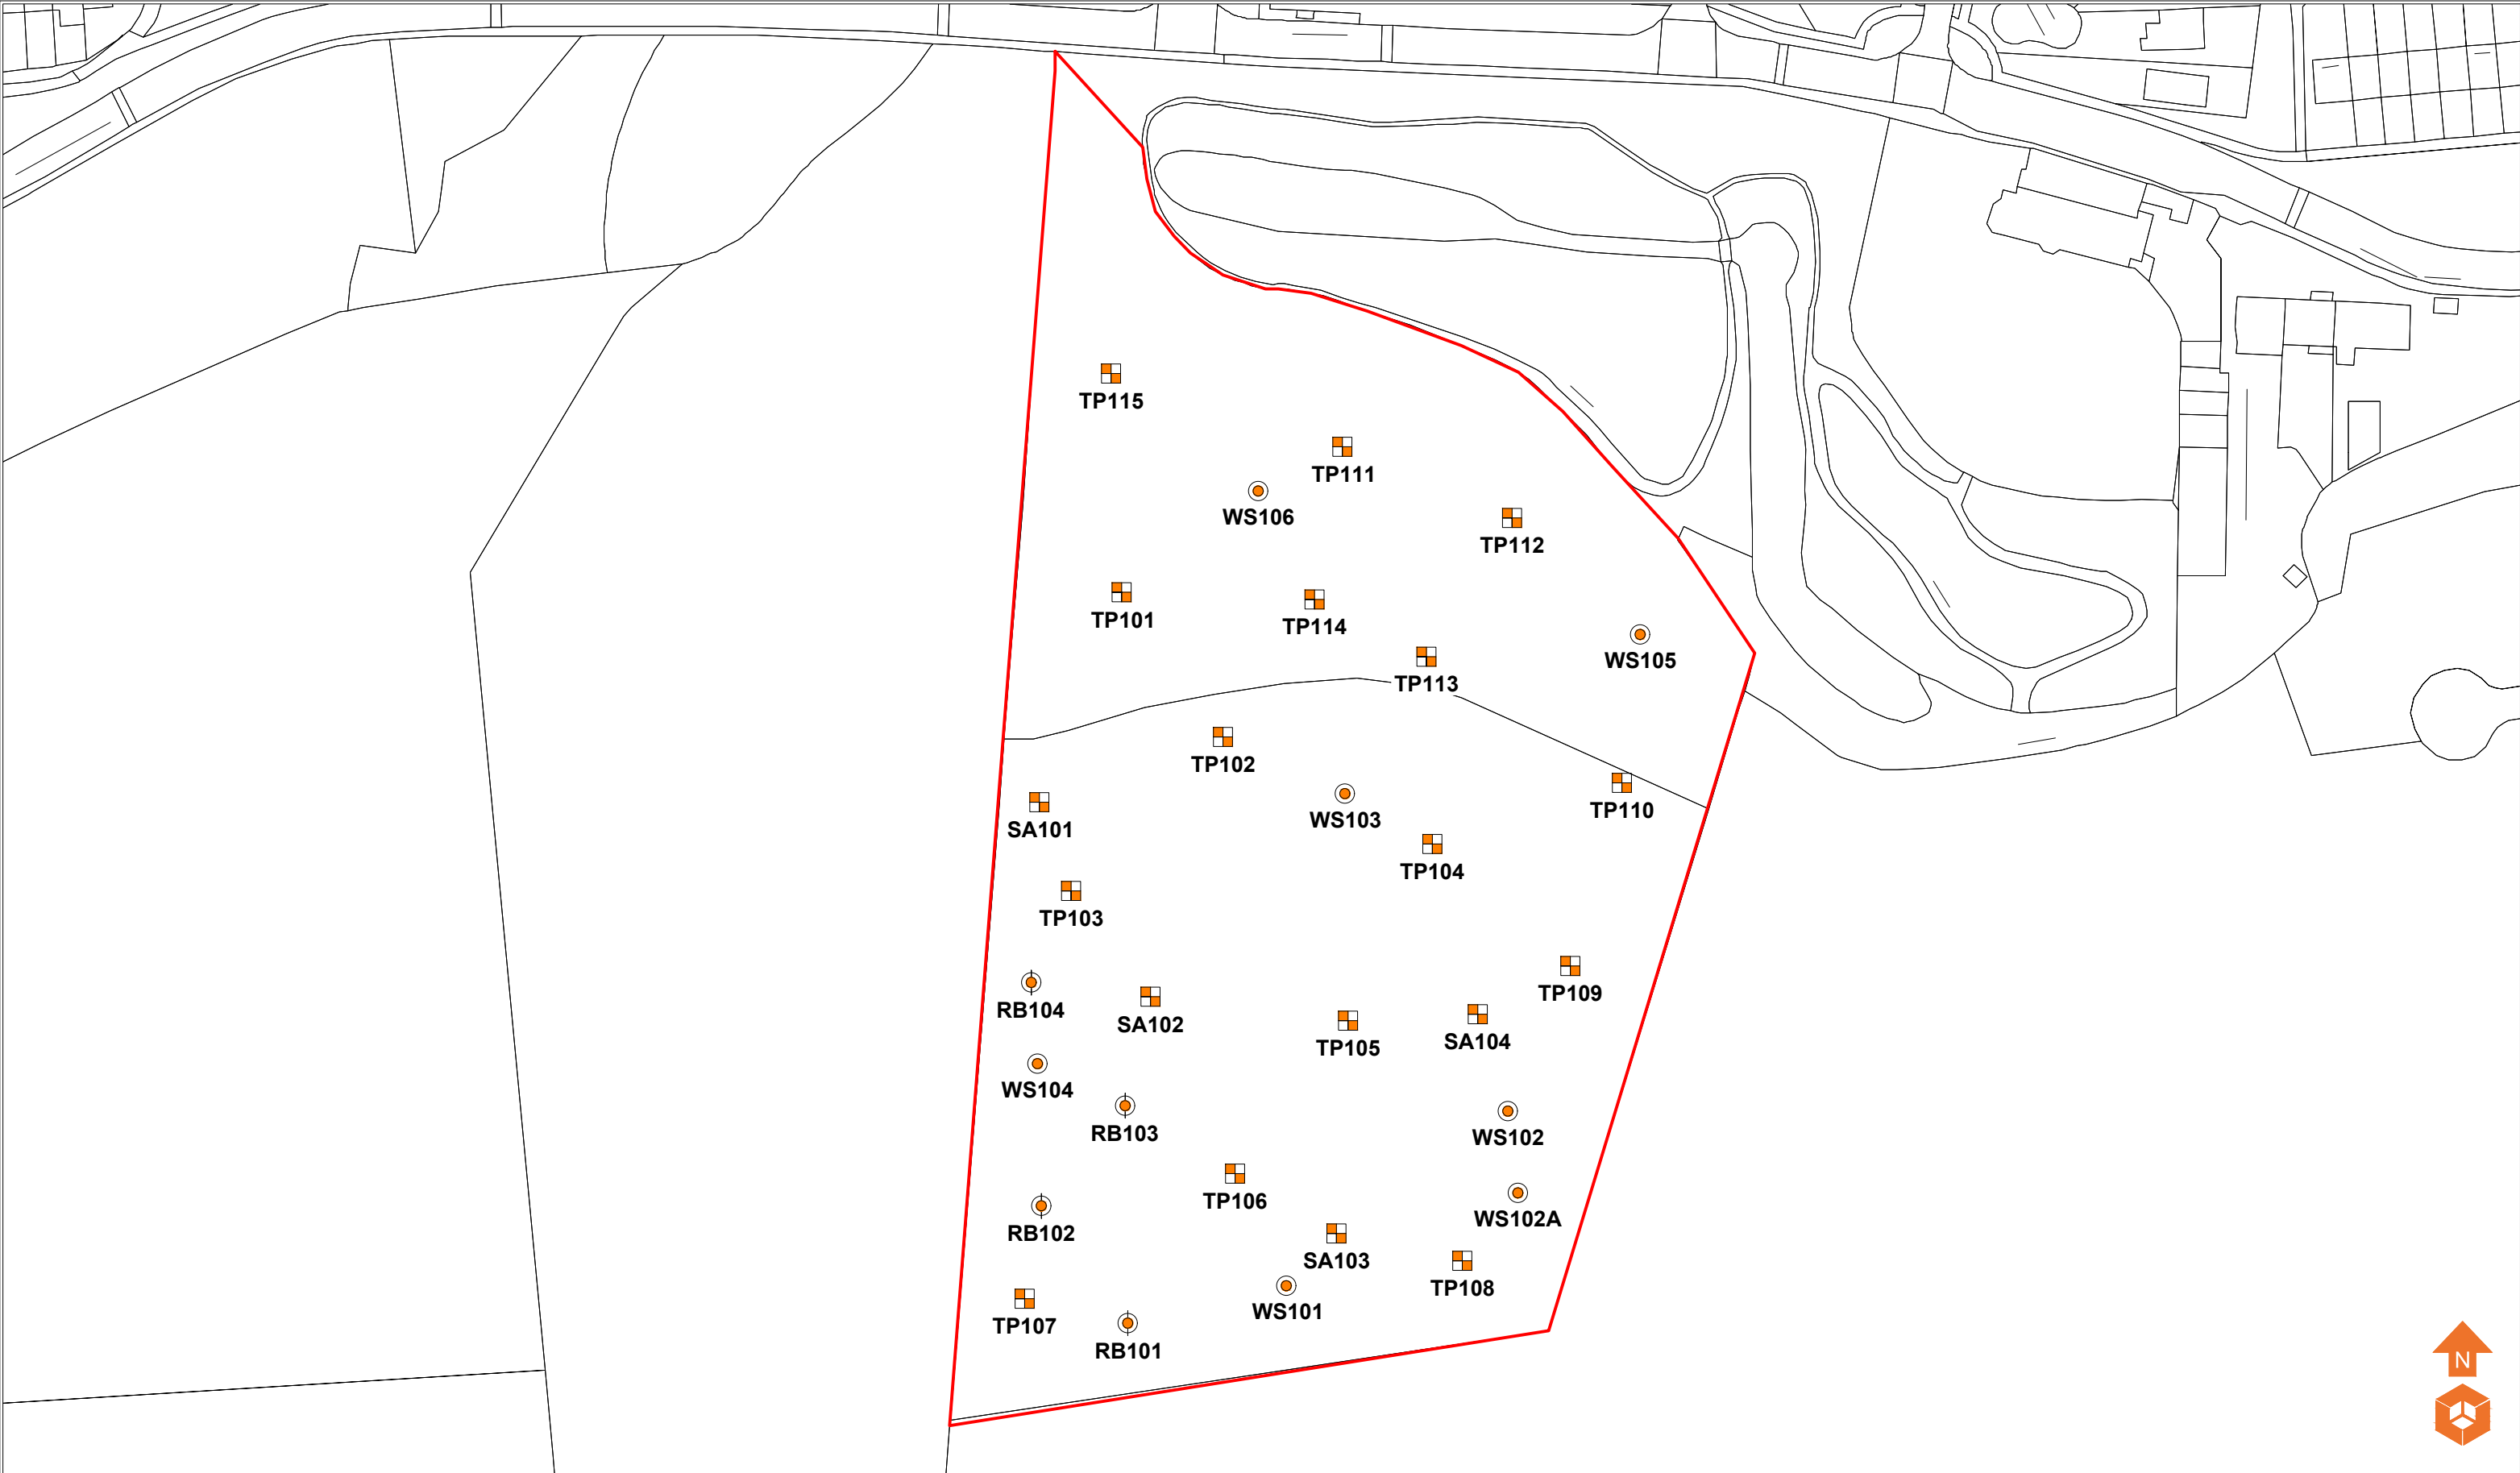

Location Symbols  WS101 Approximate Window Sample Probehole Location  TP101 Approximate Trial Pit Location  RB101 Approximate Rotary Borehole Location  SA101 Approximate Soakaway Test Location					Notes:					Client: Vistry		Job No: 15-065		Date: 25.11.2021		 Environmental Engineering Partnership Ltd Taylor Road, Trafford Park Urmston, Manchester, M41 7JQ Tel: 0161 707 9612 E-mail: info@e3p.co.uk Website: www.e3p.co.uk														
										Drawing No: 005		Scale: NTS@ A3																		
					<table><tr><td>P1</td><td>REVB</td><td>25.11.2021</td><td>LM</td><td>RH</td></tr><tr><td>P1</td><td>REVA</td><td>18.10.2021</td><td>EB</td><td>RH</td></tr><tr><td>Phase</td><td>Issue</td><td>Date</td><td>Drawn</td><td>Checked</td></tr></table>					P1	REVB	25.11.2021	LM	RH	P1	REVA	18.10.2021	EB	RH	Phase	Issue	Date	Drawn	Checked	Job Title: Halnsead, Lickers Lane		Drawing Title: Exploratory Hole Location Plan		The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.	
P1	REVB	25.11.2021	LM	RH																										
P1	REVA	18.10.2021	EB	RH																										
Phase	Issue	Date	Drawn	Checked																										

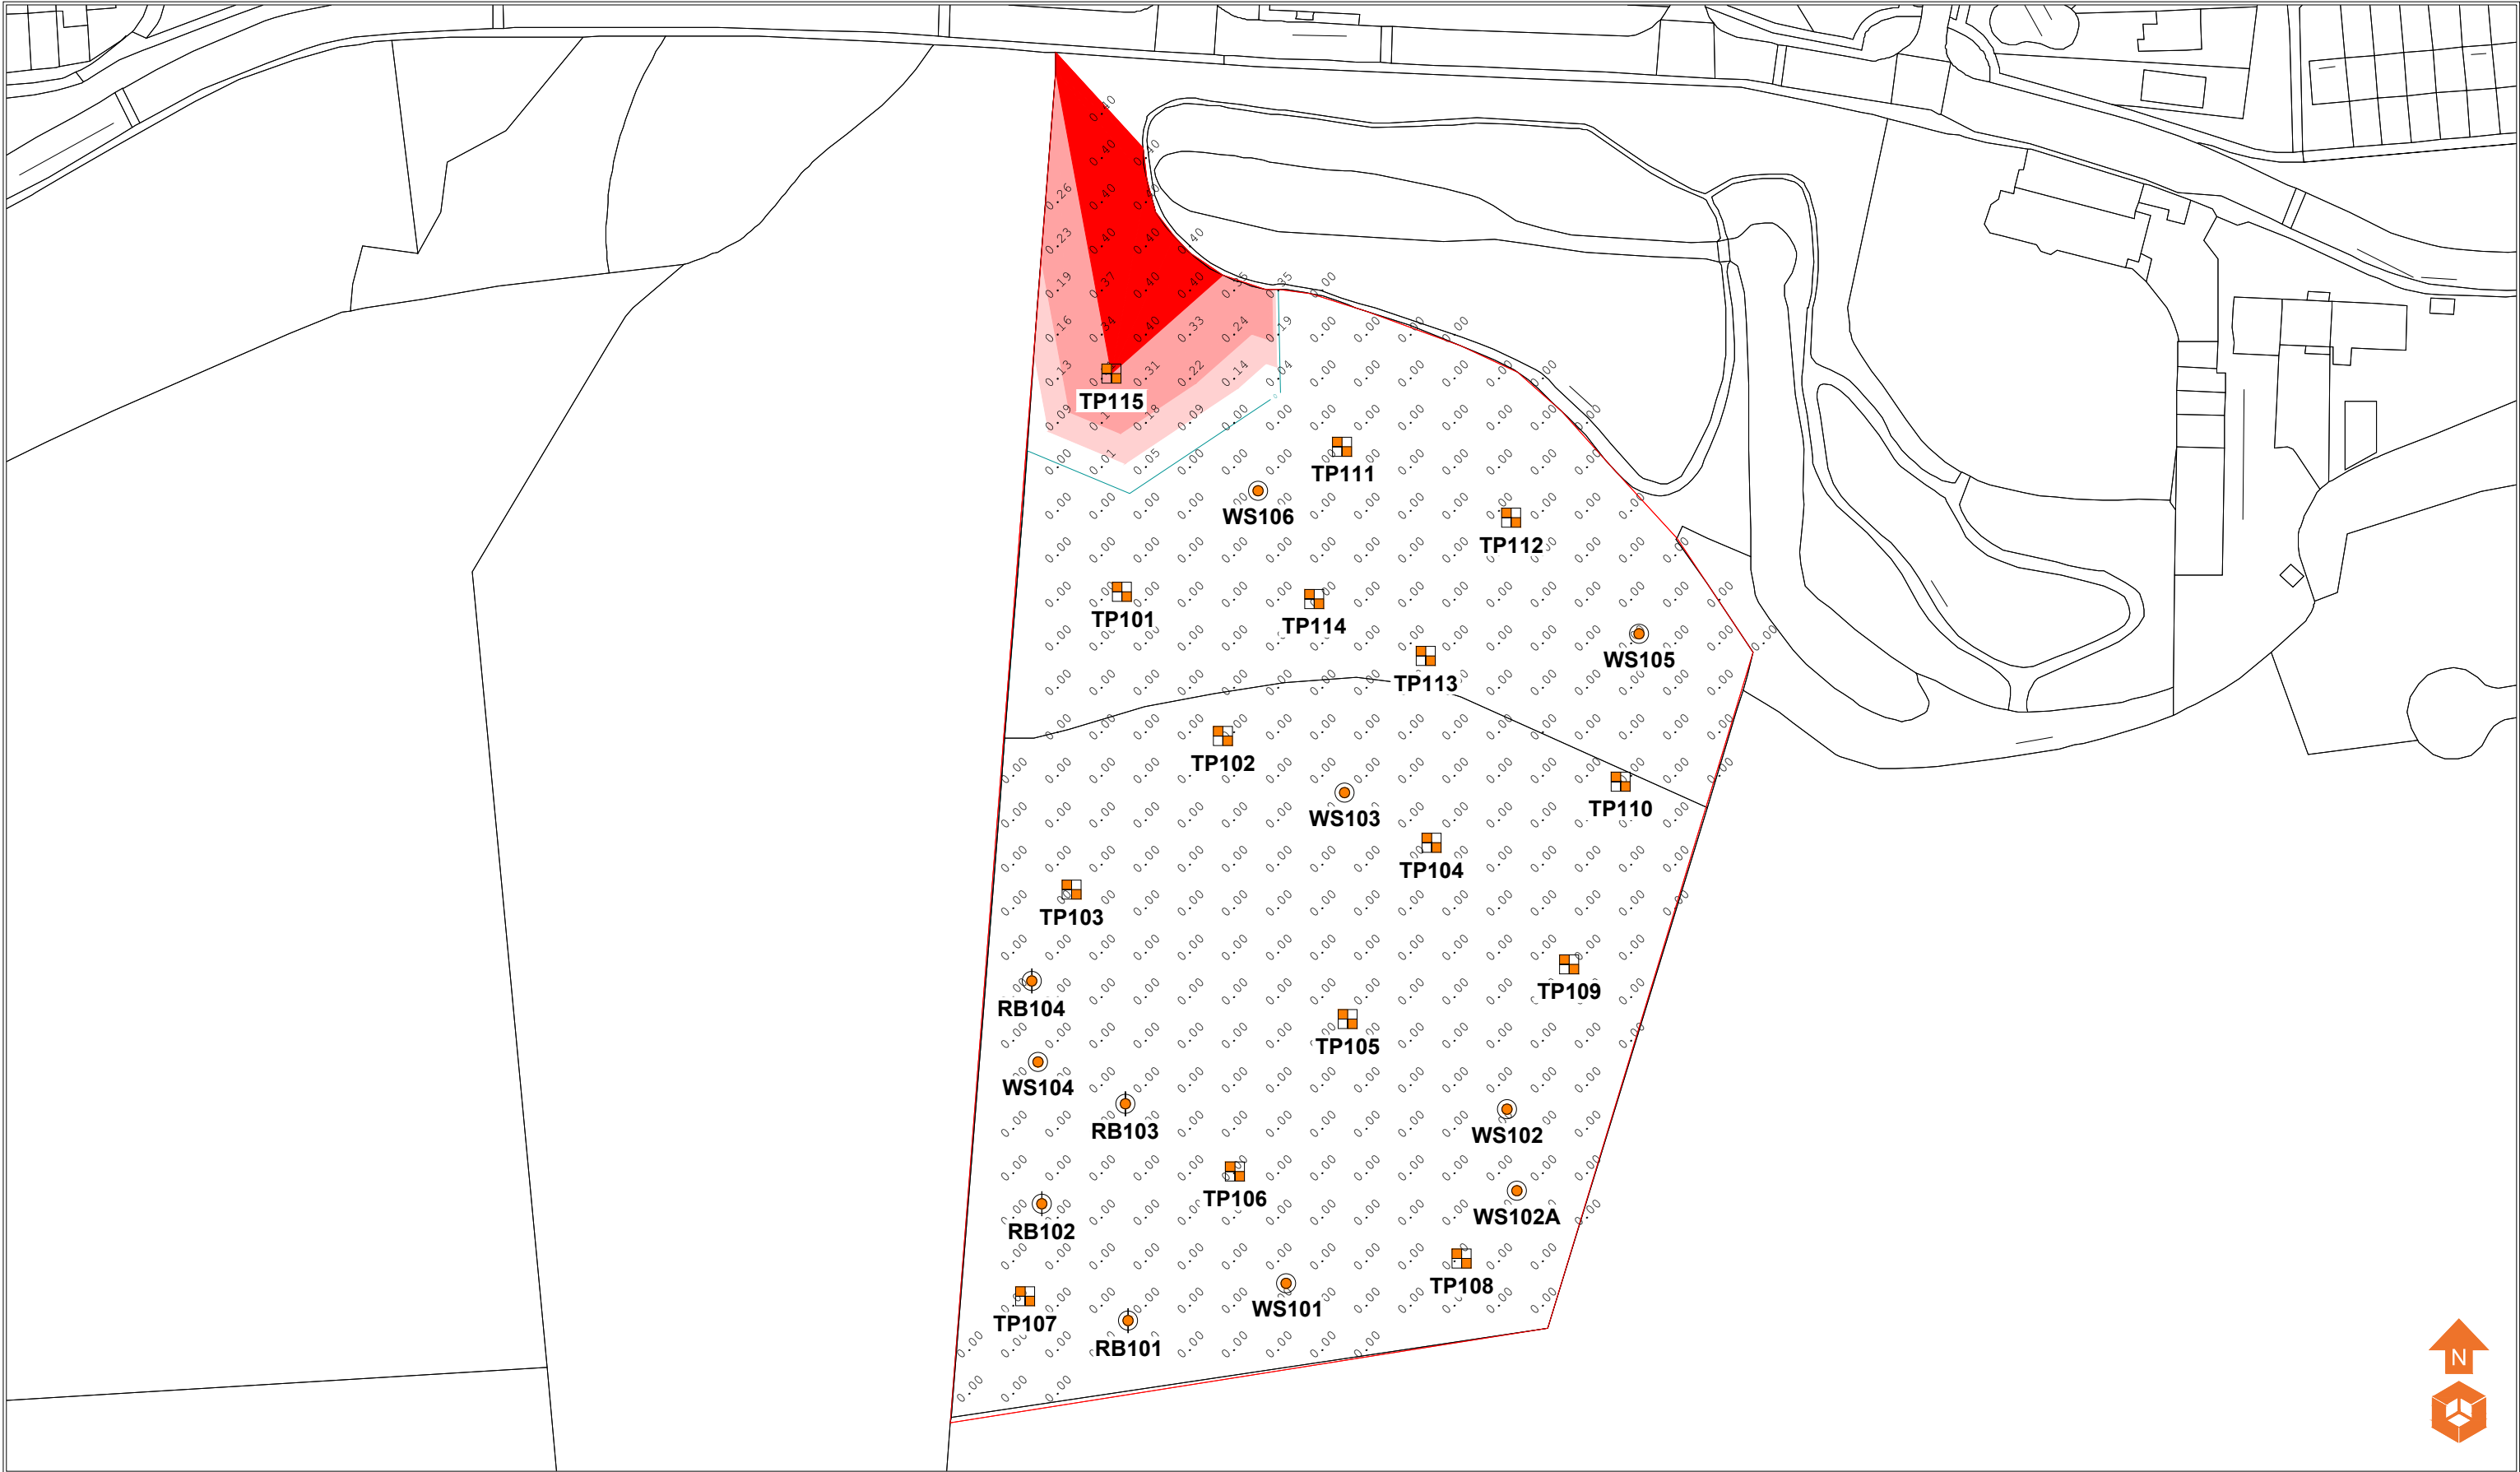

- Location Symbols**
- Approximate Window Sample Probehole Location
 - Approximate Trial Pit Location
 - Approximate Rotary Borehole Location

- Made Ground Depth (m)**
- Made Ground not Identified
 - Depth of Made Ground 0.00 - 0.19m
 - Depth of Made Ground 0.20 - 0.39m
 - Depth of Made Ground >0.40m

Notes:

Client:

Vistry

Job No:

15-065

Date:

03.11.2021

Drawing No:

006

Scale:

NTS@ A3

Environmental Engineering
Partnership Ltd
Taylor Road, Trafford Park
Urmston, Manchester, M41 7JQ
Tel: 0161 707 9612
E-mail: info@e3p.co.uk
Website: www.e3p.co.uk

P1	REVB	03.11.2021	LM	MJ
P1	REVA	20.10.2021	CB	RH
Phase	Issue	Date	Drawn	Checked


Job Title:

Hainsead,
Lickers Lane

Drawing Title:

Depth of Made Ground Plan

The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.

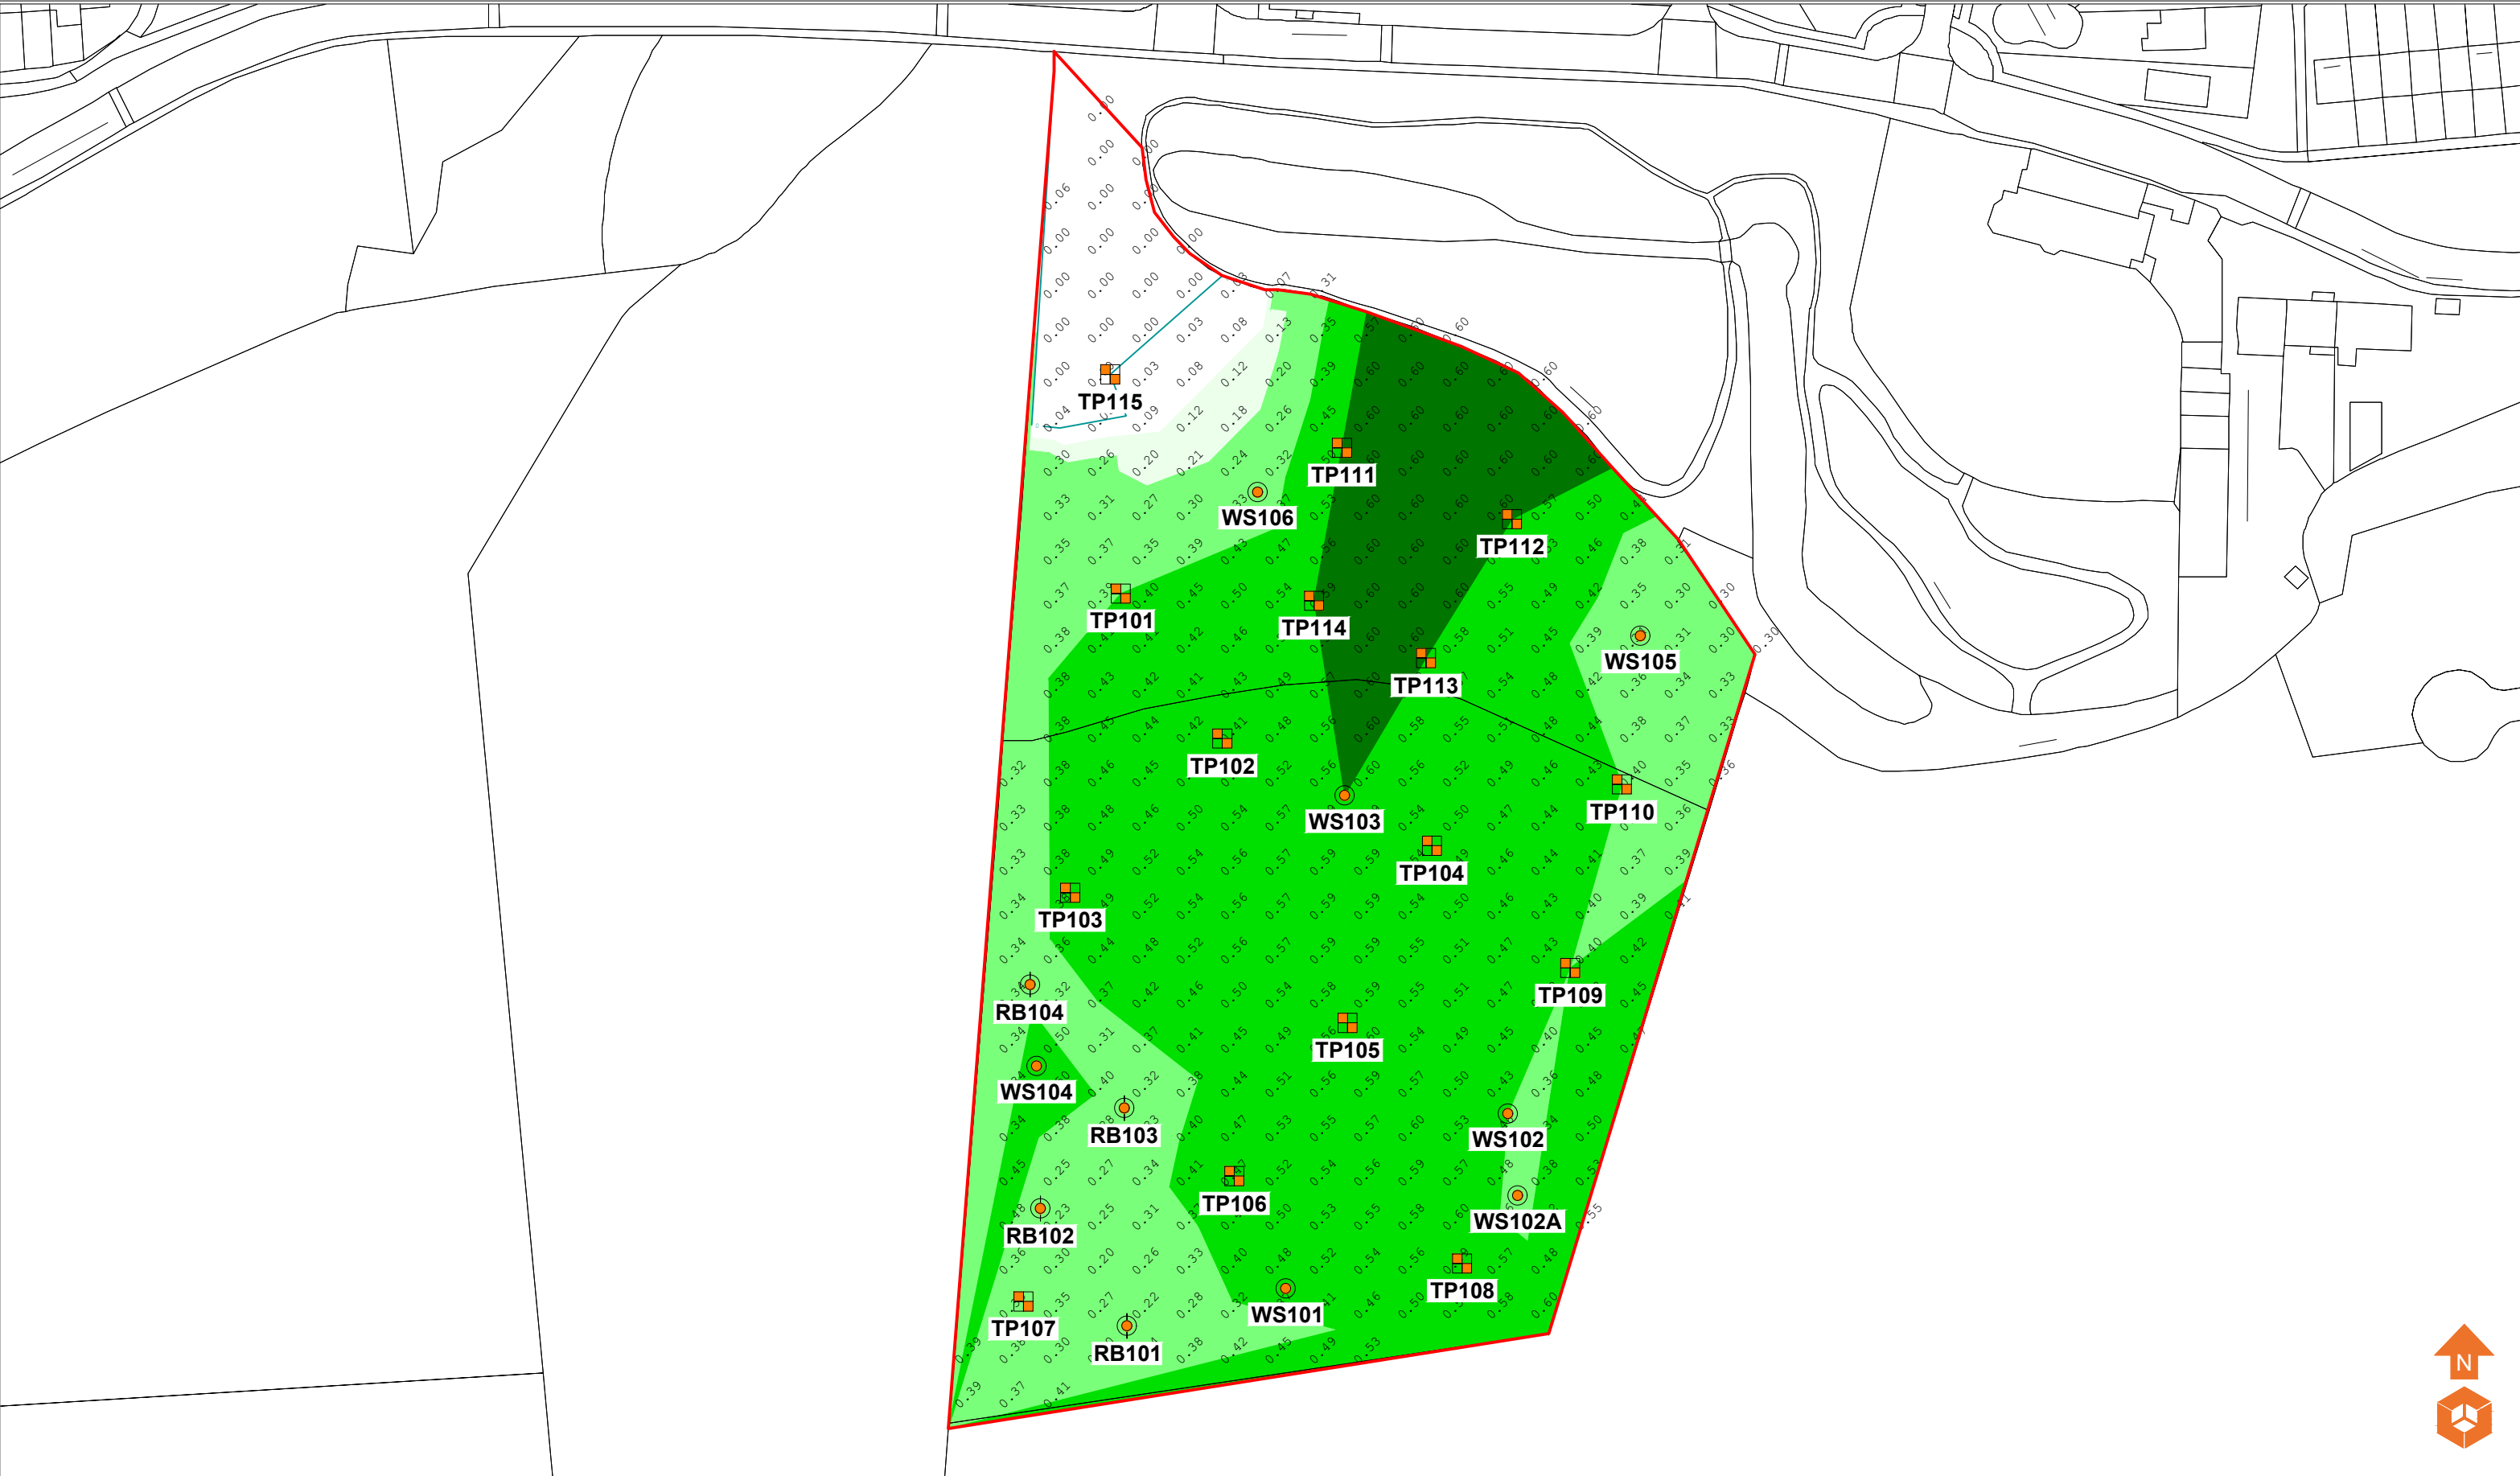

Location Symbols

- Approximate Window Sample Probehole Location
- Approximate Trial Pit Location
- Approximate Rotary Borehole Location

Topsoil Depth (m)

- Topsoil not Identified
- Depth of Topsoil 0.00 - 0.19m
- Depth of Topsoil 0.20 - 0.39m
- Depth of Topsoil 0.40 - 0.59m
- Depth of Topsoil >0.60m

Notes:

P1	REVA	20.10.2021	CB	RH
Phase	Issue	Date	Drawn	Checked

Client:

Vistry

Job Title:

Hainsead,
Lickers Lane

Job No:

15-065

Drawing No:

007

Date:

20.10.2021


Scale:

NTS@ A3





Environmental Engineering
Partnership Ltd
Taylor Road, Trafford Park
Urmston, Manchester, M41 7JQ
Tel: 0161 707 9612
E-mail: info@e3p.co.uk
Website: www.e3p.co.uk

The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.

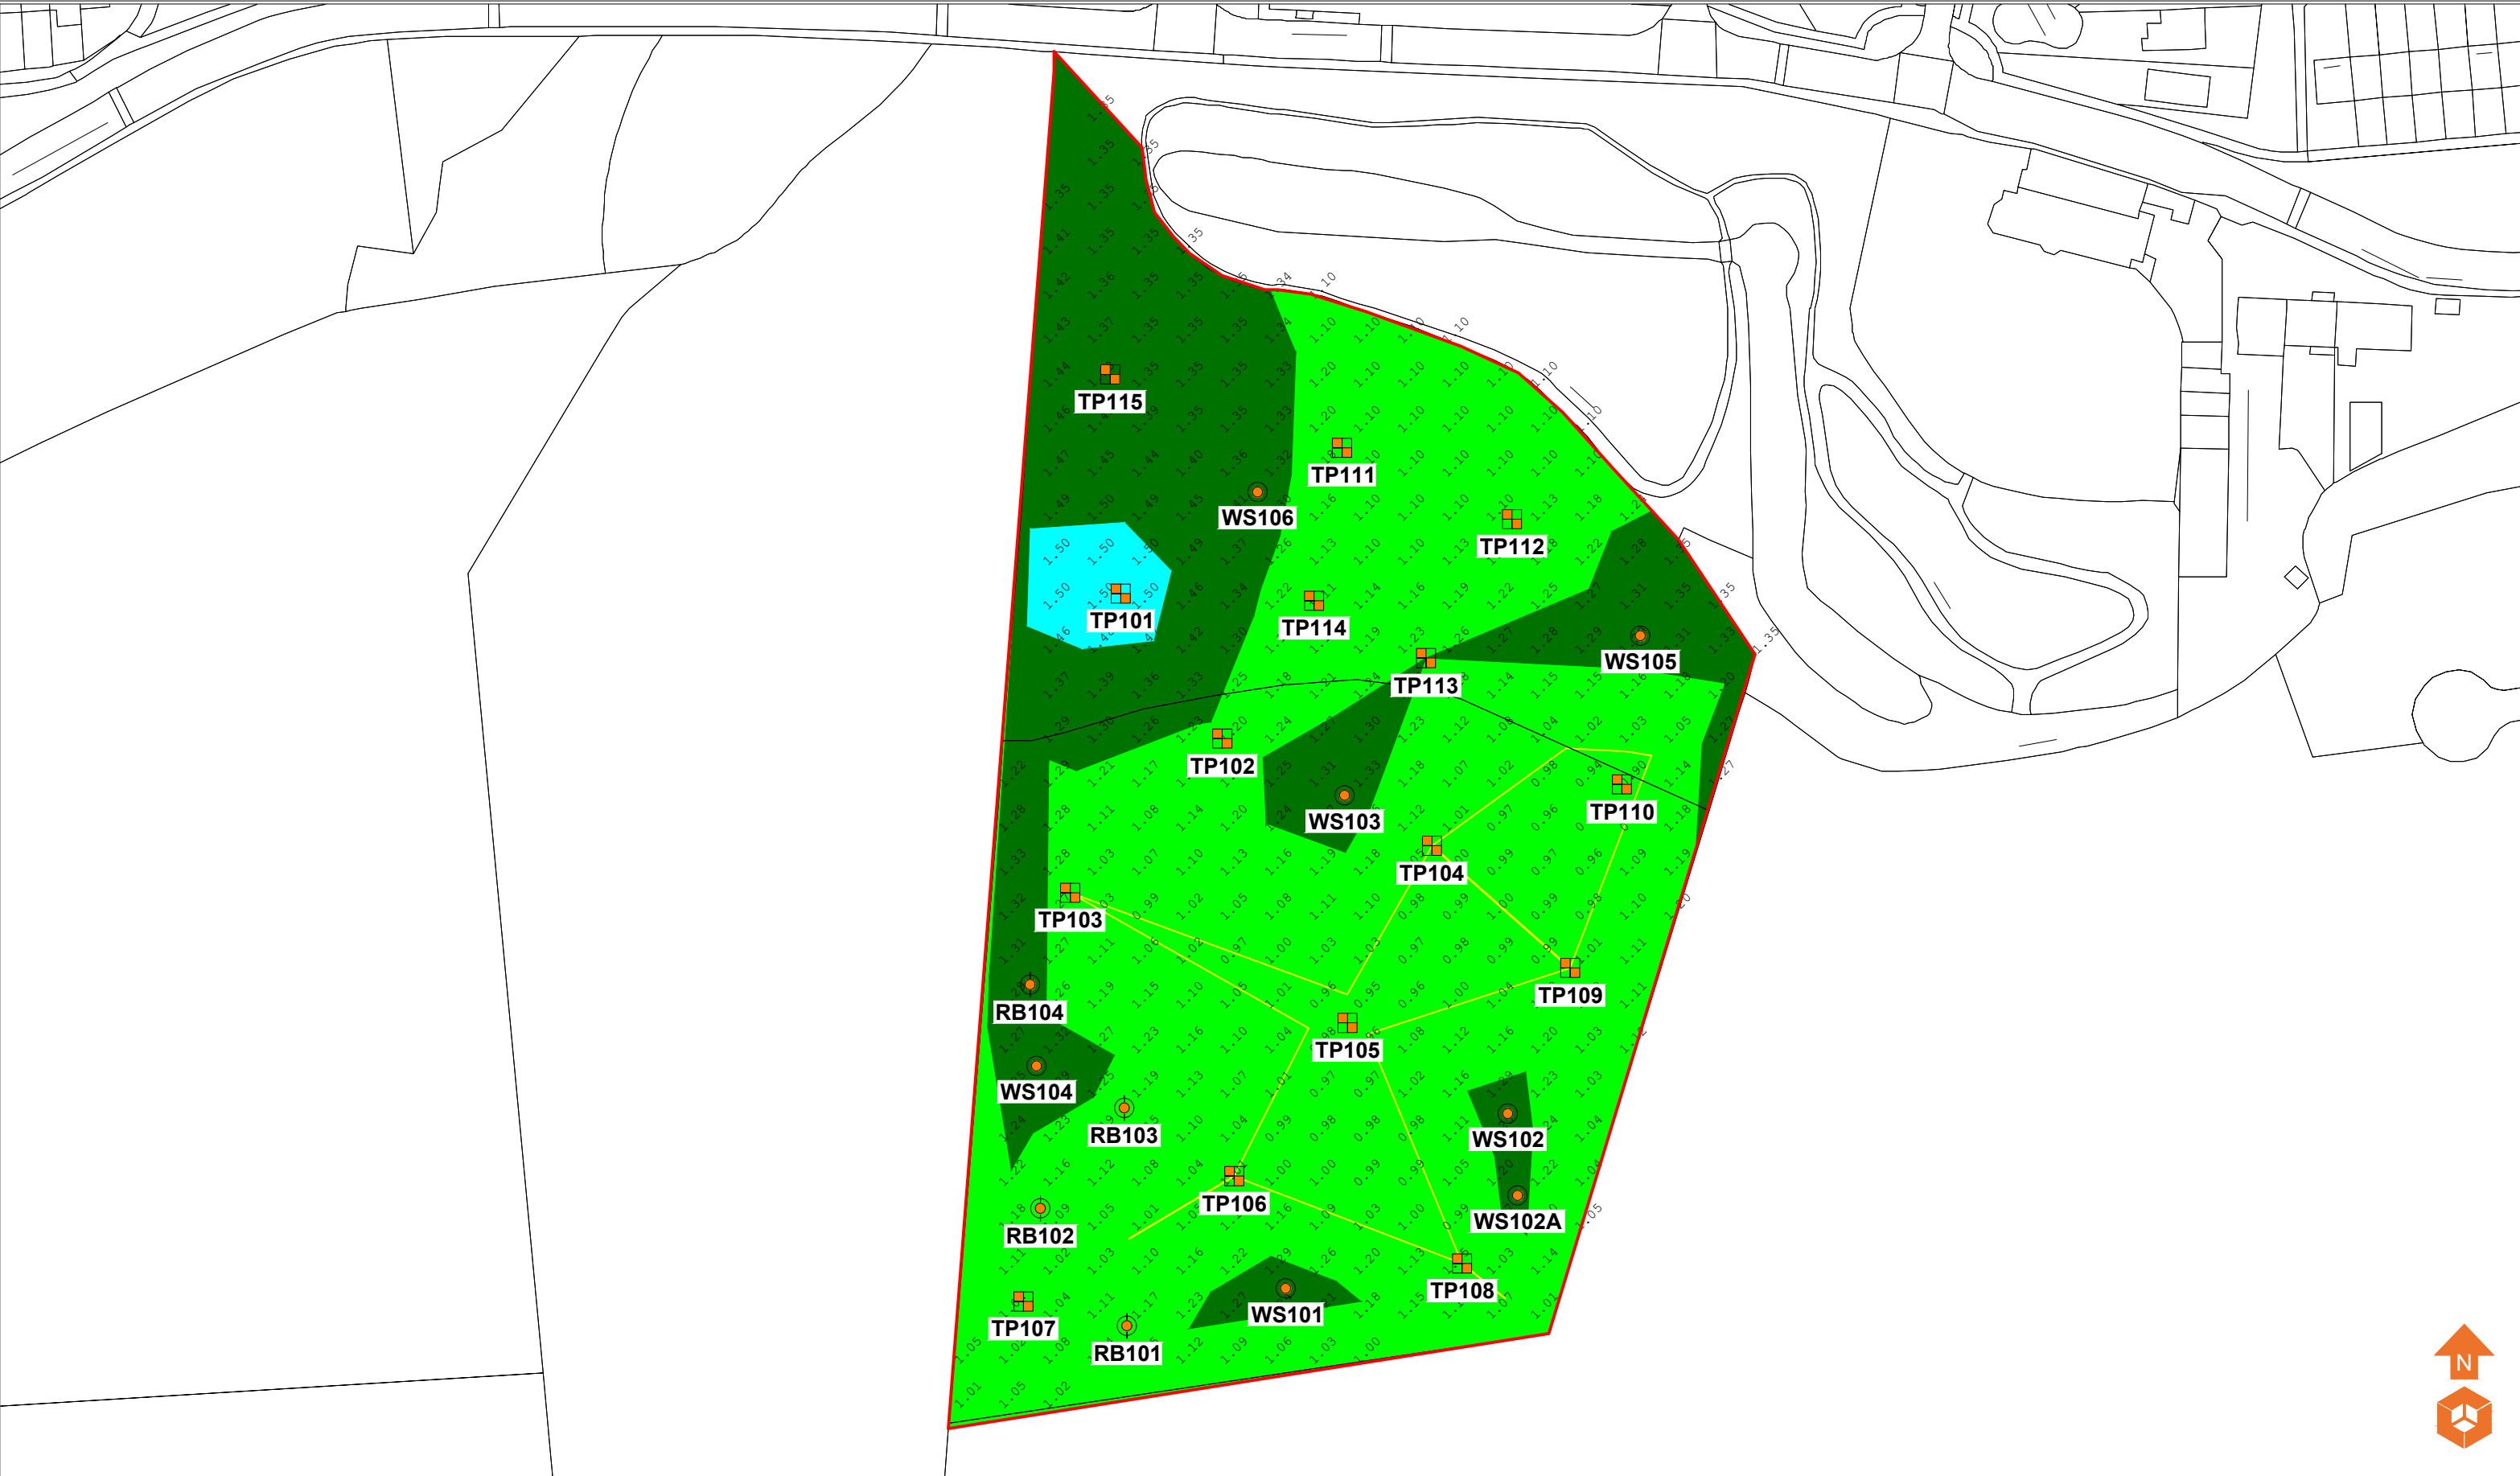


Location Symbols WS101 Approximate Window Sample Probehole Location TP101 Approximate Trial Pit Location RB101 Approximate Rotary Borehole Location

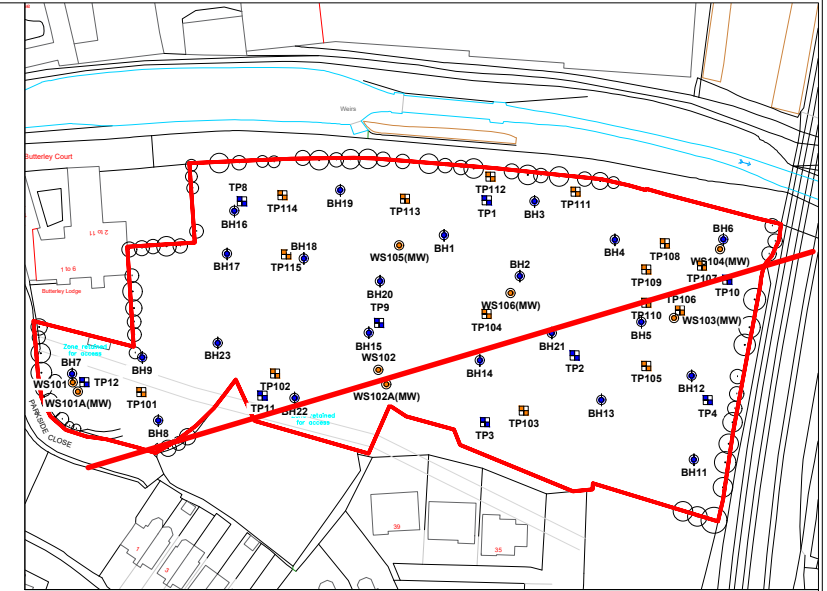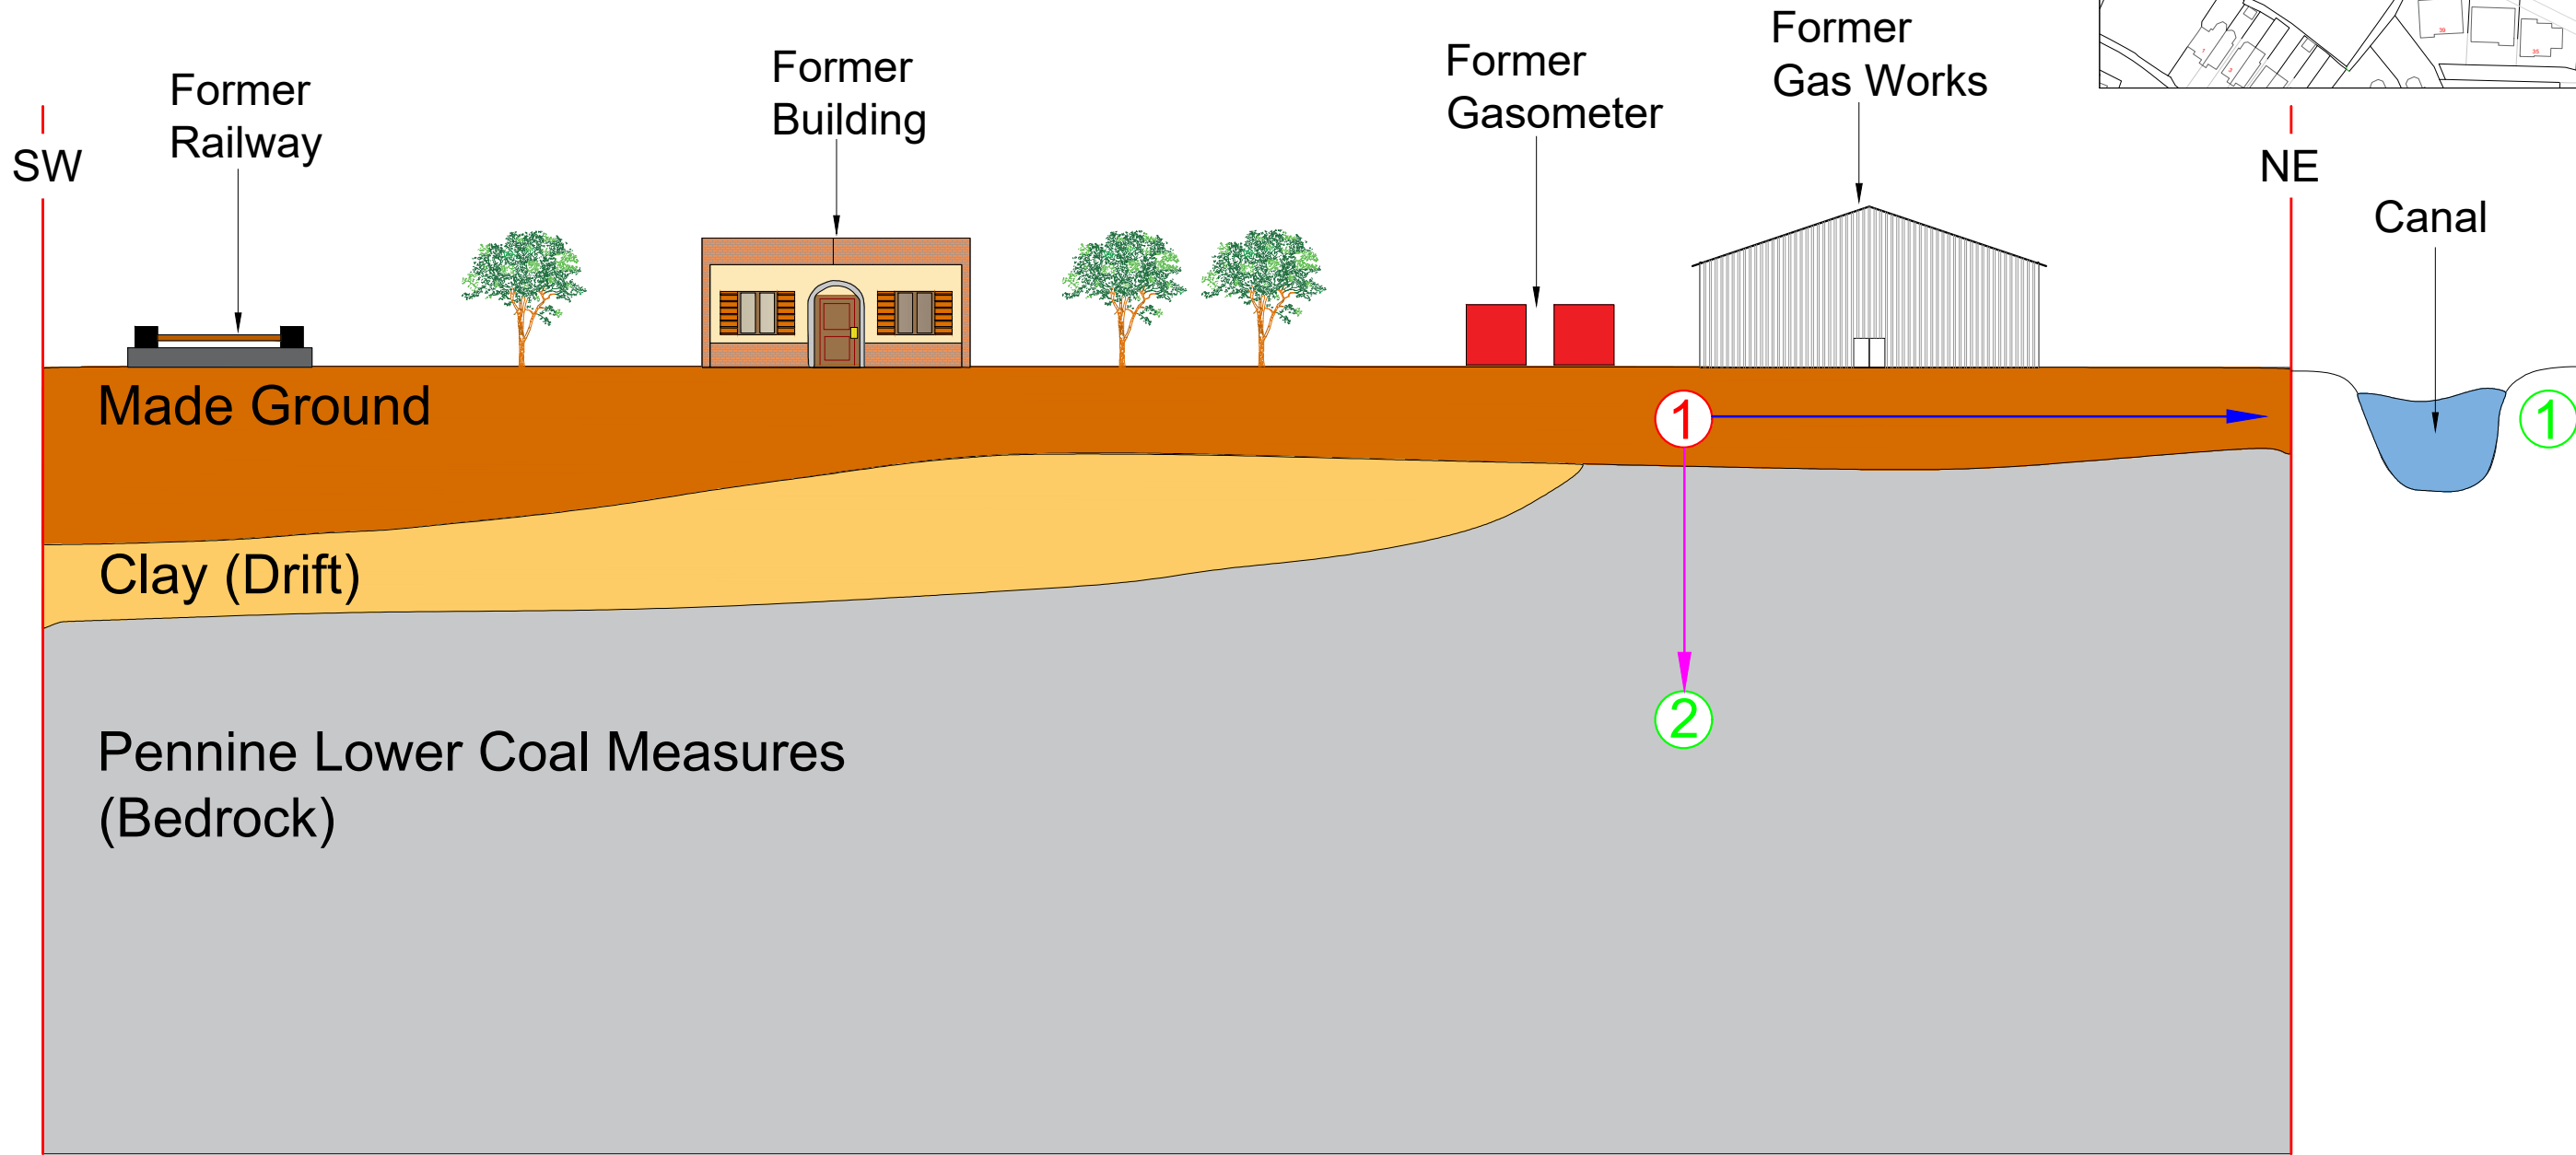

Geology Key Made Ground Clay Pennine Coal Measures Canal Gasometers	Sources ① Mobile Contaminants (Hydrocarbons)	Pathways ① River ② Shallow Groundwater ③ Potential Future Residents / Industrial Employees ④ Buildings	Receptor ① Surface Water features (Inland river, Canal) ② Secondary A aquifer (Bedrock)	Notes:					Client: SEP Construction Services Ltd		Job No: 15-343	Date: 25.11.2021	e3p Environmental Engineering Partnership Ltd Taylor Road, Trafford Park Urmston, Manchester, M41 7JQ Tel: 0161 707 9612 E-mail: info@e3p.co.uk Website: www.e3p.co.uk	
											Drawing No: 010	Scale: 1:1000 @ A3		
											Drawing Title: Conceptual Site Model - Controlled Waters			
					Job Title: Parkside Close, Nottingham							The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.		
					P1	REVA	25.11.2021	LM	NS					
					Phase	Issue	Date	Drawn	Checked					

The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.

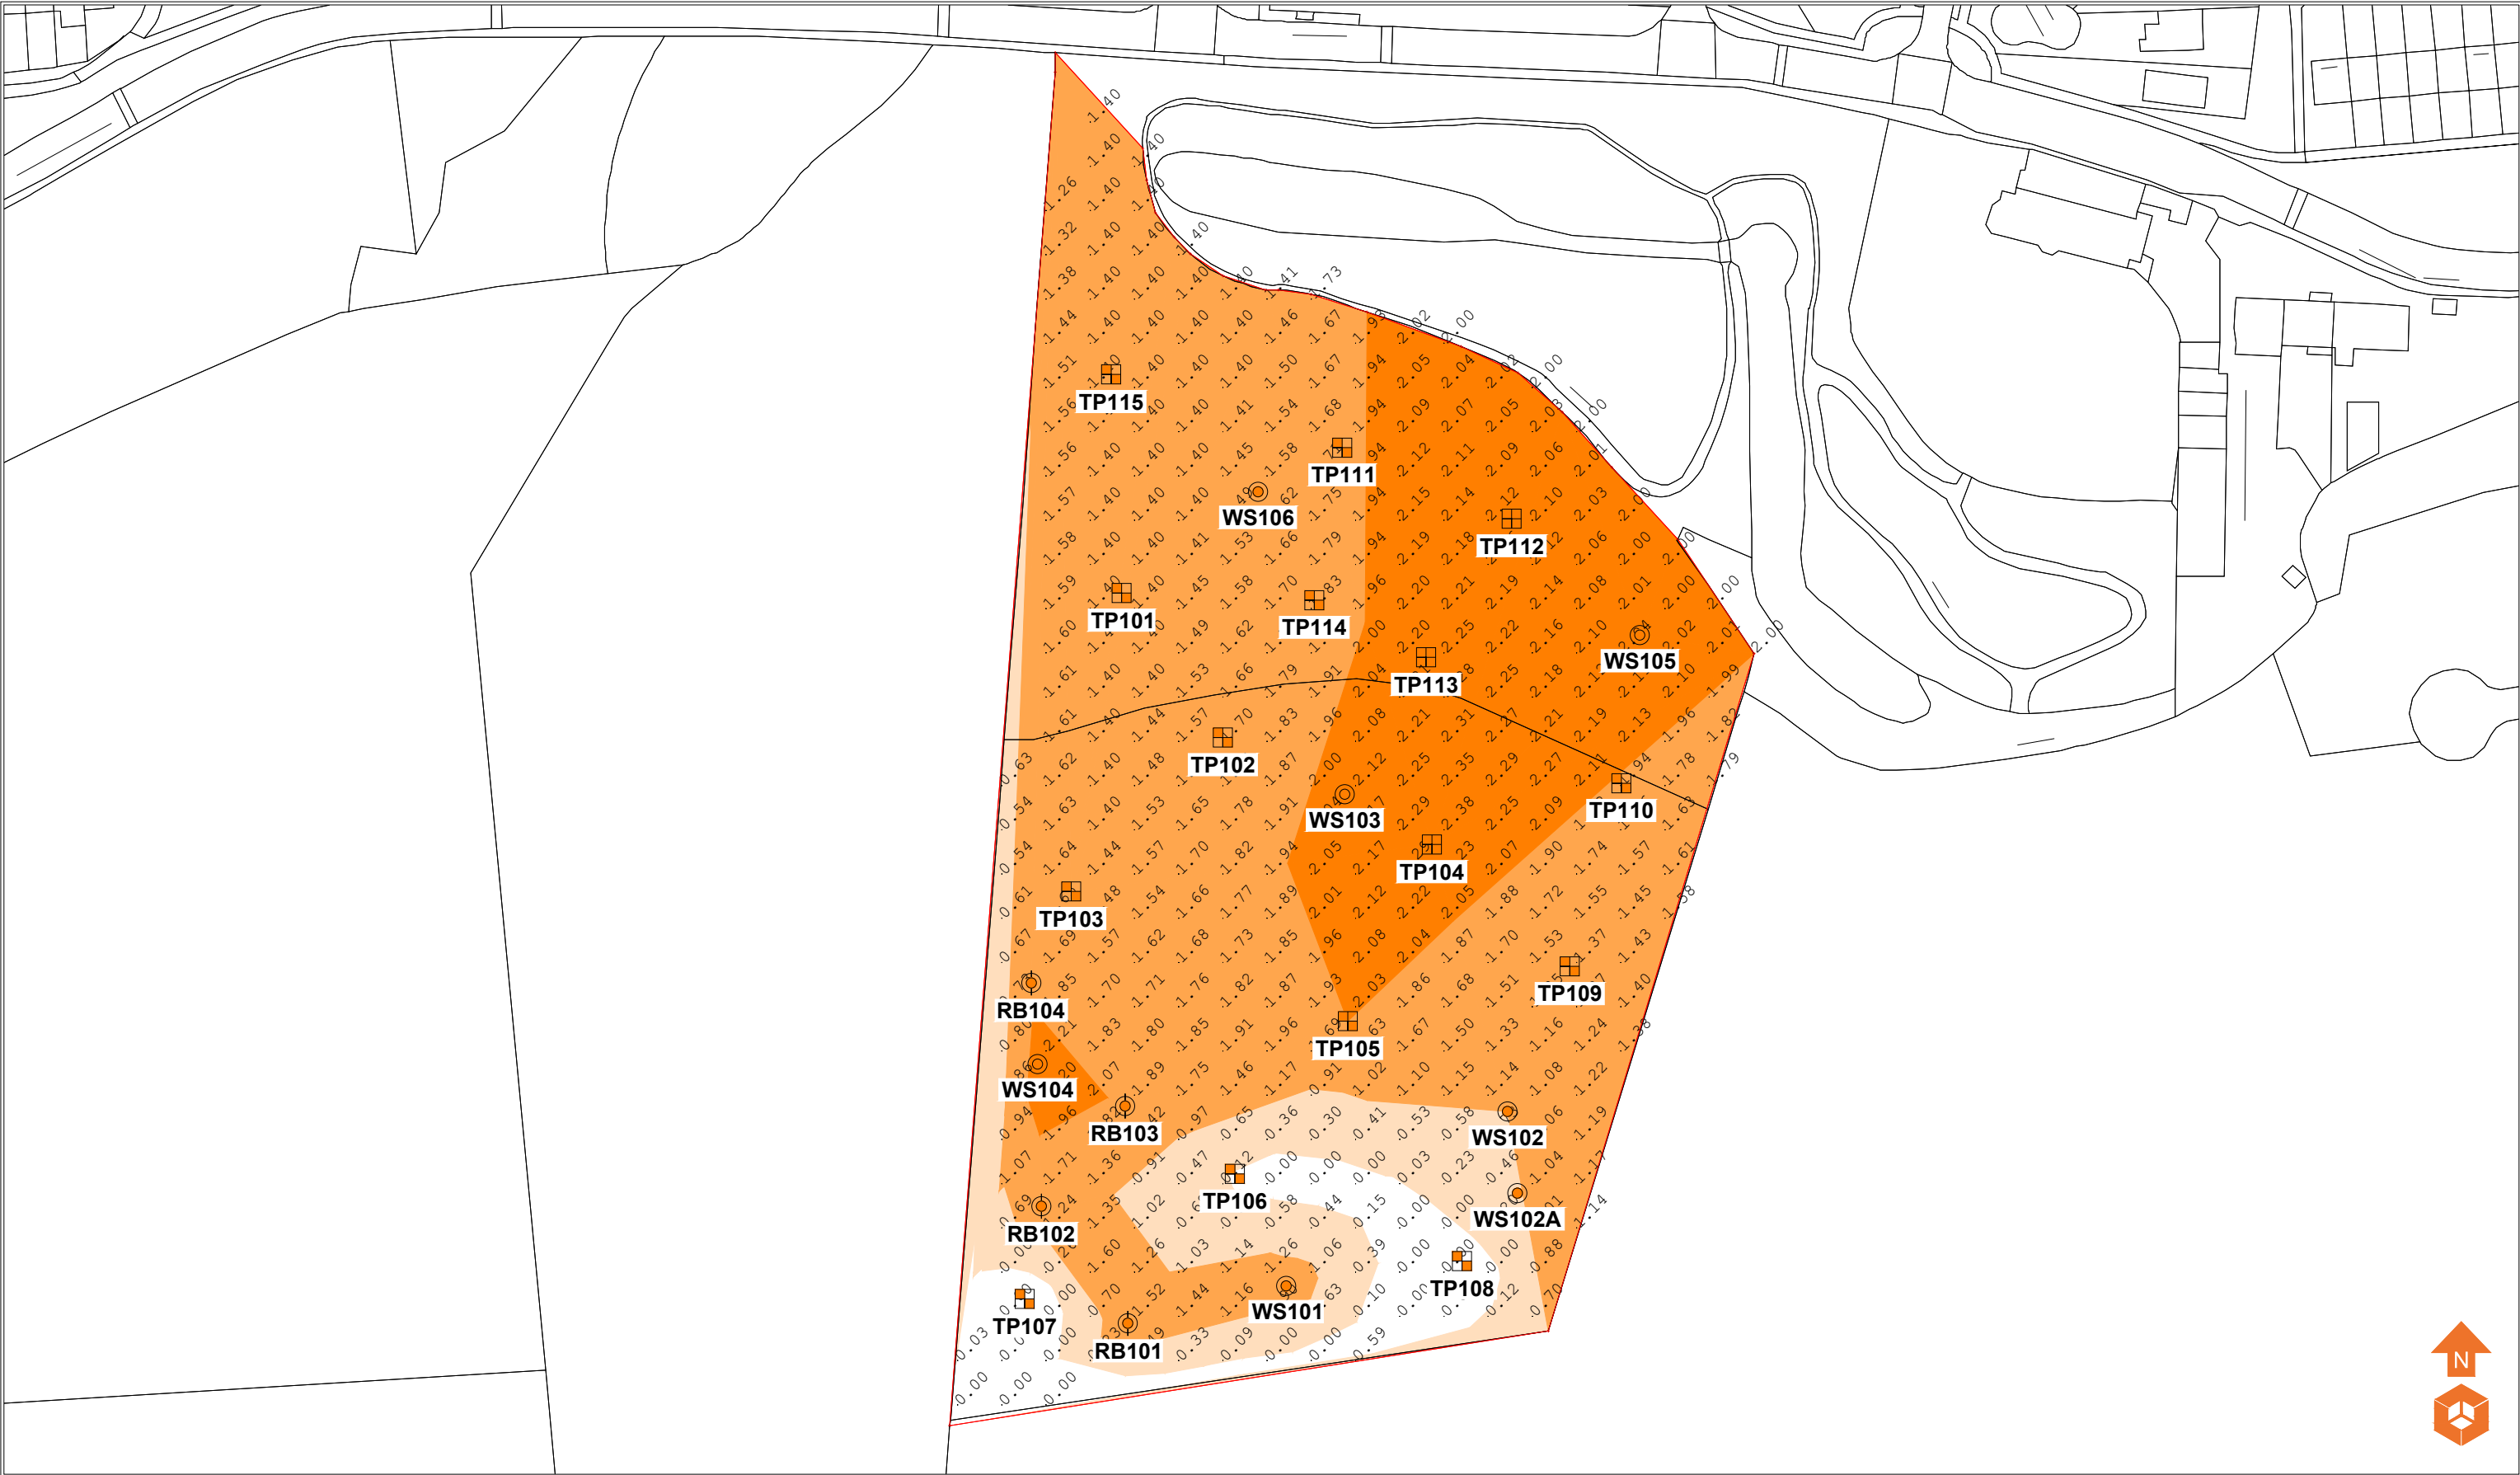

- Location Symbols**
- Approximate Window Sample Probehole Location
 - Approximate Trial Pit Location
 - Approximate Rotary Borehole Location

- Depth to Bedrock (m)**
- Bedrock not Identified
 - Depth to Bedrock 0.00 - 0.99m
 - Depth to Bedrock 1.00 - 1.99m
 - Depth to Bedrock >2.00m

Notes:

Client:

Vistry

Job No:

15-065

Date:

03.11.2021

Drawing No:

012

Scale:

NTS@ A3

Environmental Engineering Partnership Ltd
Taylor Road, Trafford Park
Urmston, Manchester, M41 7JQ
Tel: 0161 707 9612
E-mail: info@e3p.co.uk
Website: www.e3p.co.uk

P1	REVC	03.10.2021	LM	MJ
P1	REVA	20.10.2021	CB	RH
Phase	Issue	Date	Drawn	Checked


Job Title:

Hainsead,
Lickers Lane

Drawing Title:

Depth to Bedrock Plan

The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.

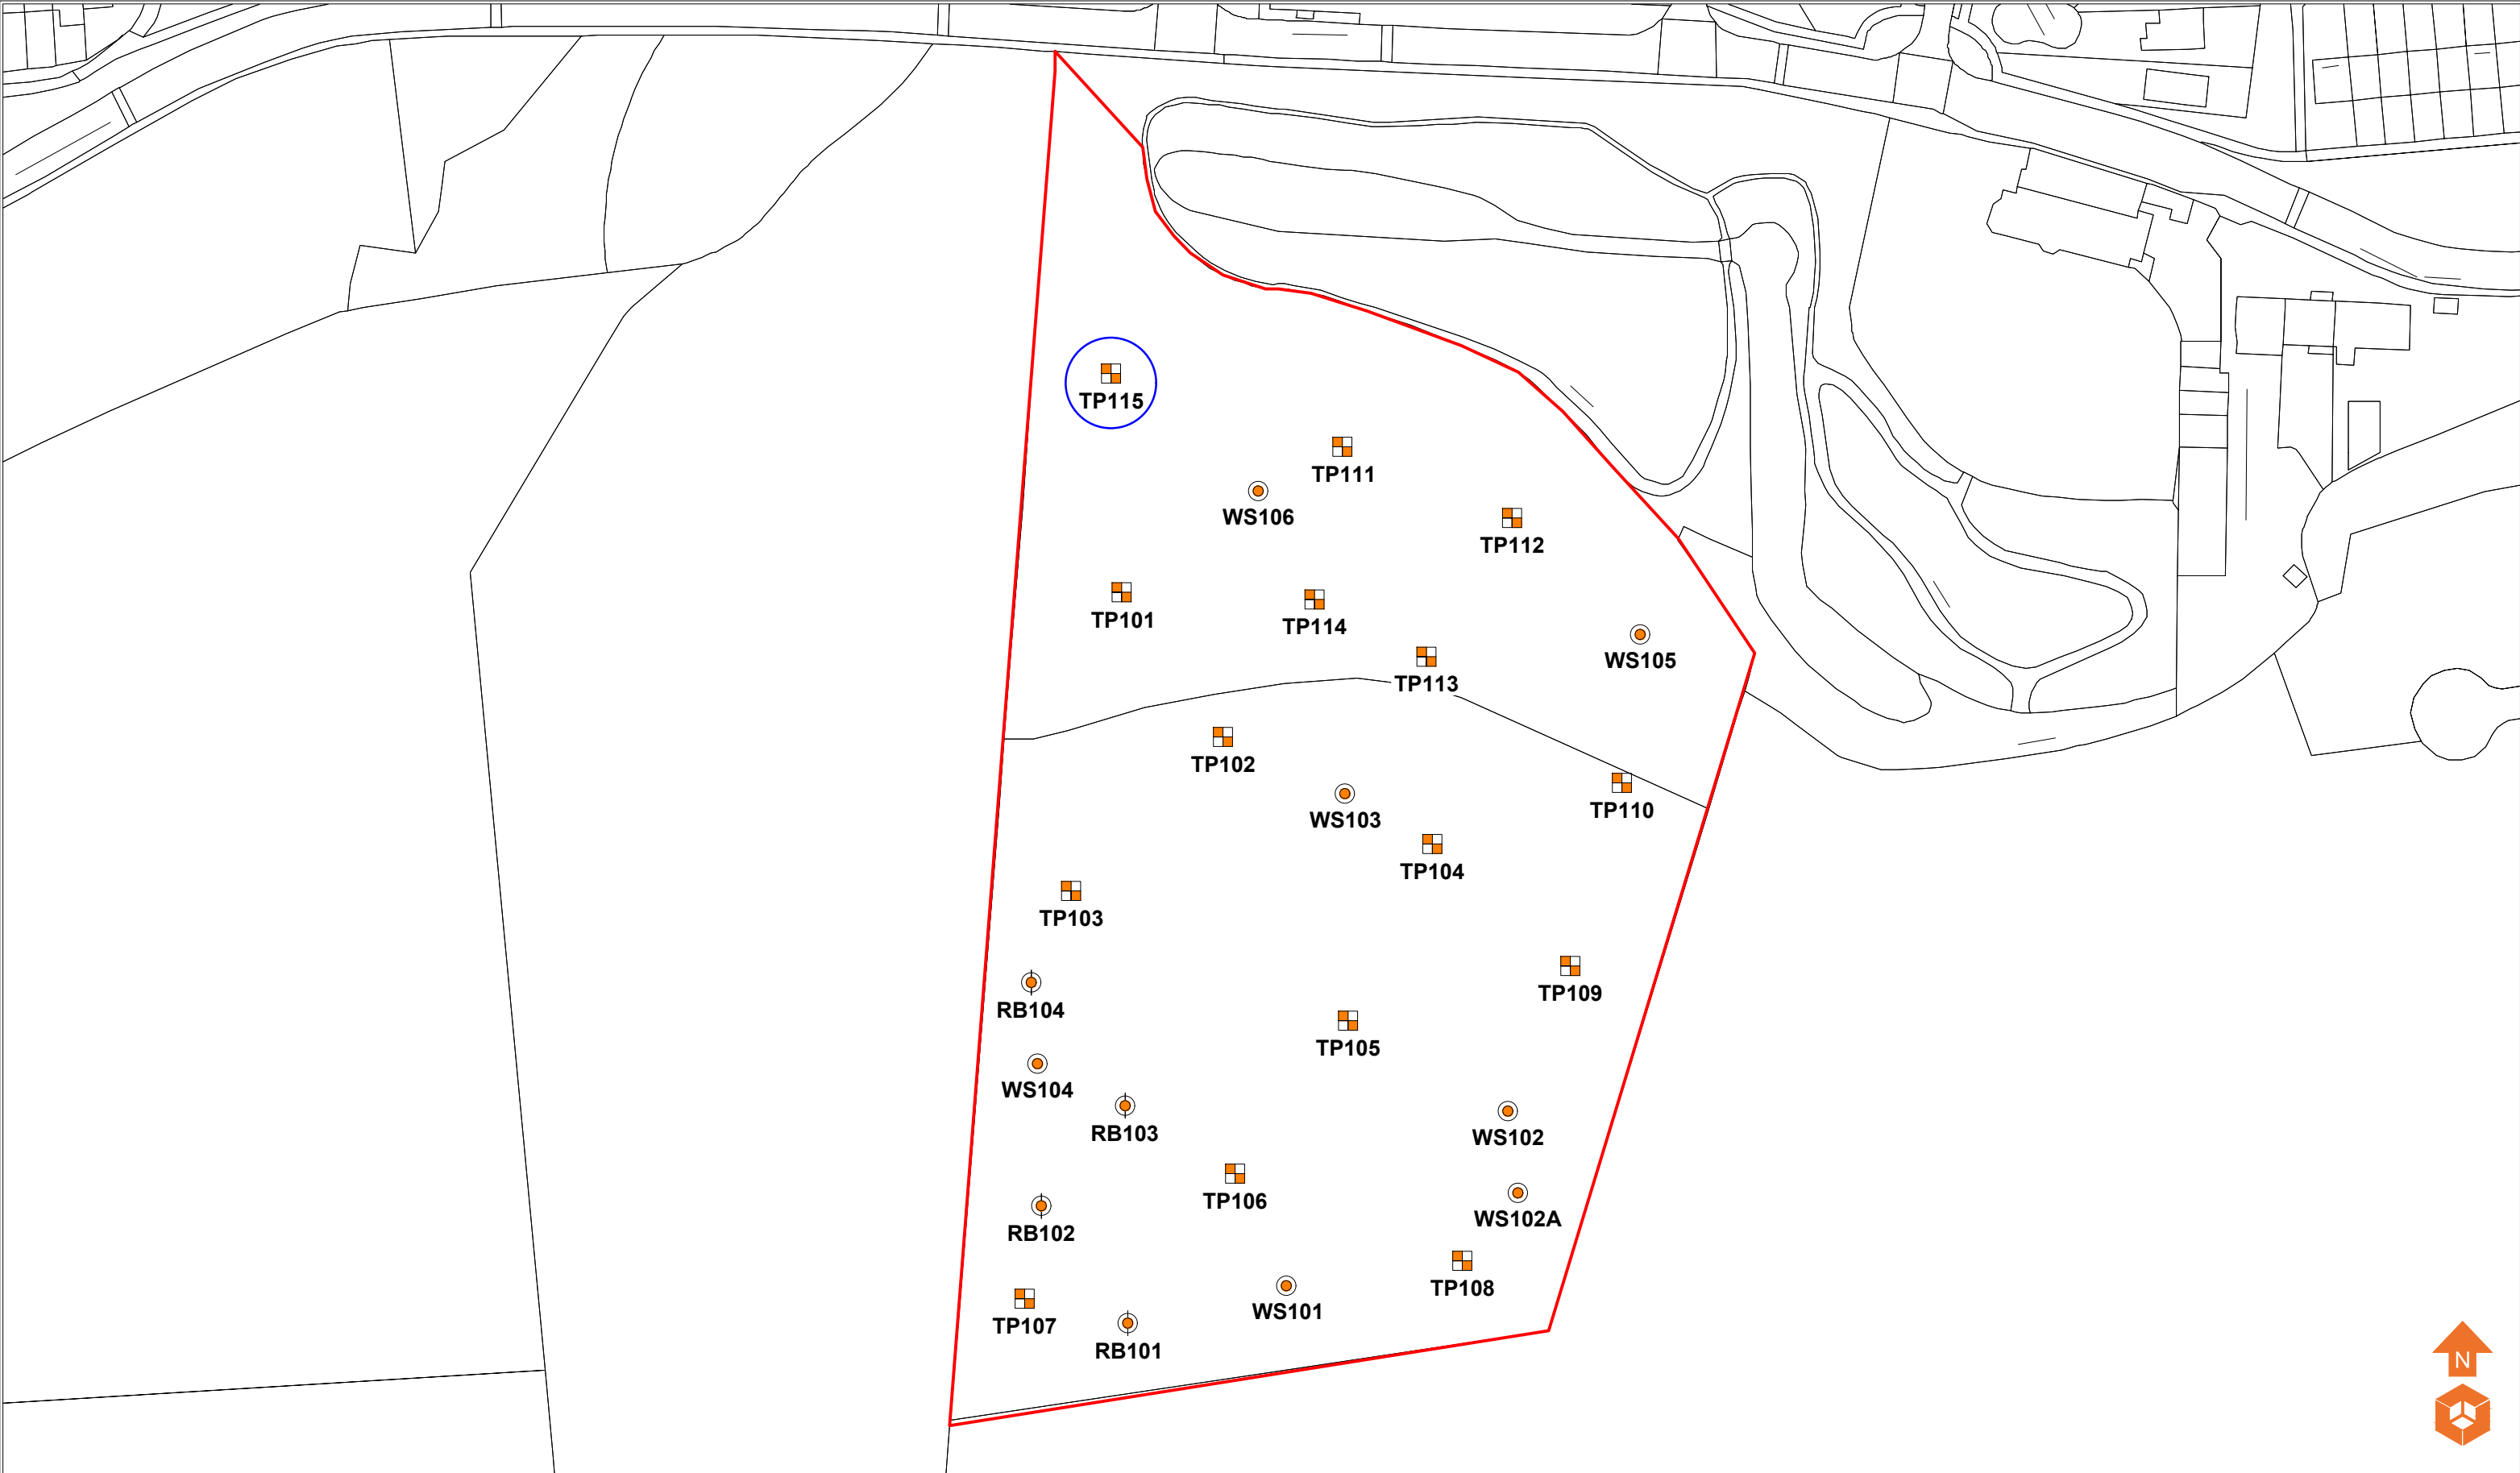

Location Symbols  Approximate Window Sample Probehole Location  Approximate Trial Pit Location  Approximate Rotary Borehole Location					Contamination Issues  PAH					Notes:					Client: Vistry					Job No: 15-065		Date: 02.11.2021		 Environmental Engineering Partnership Ltd Taylor Road, Trafford Park Urmston, Manchester, M41 7JQ Tel: 0161 707 9612 E-mail: info@e3p.co.uk Website: www.e3p.co.uk				
					<table><tr><td>P1</td><td>REVA</td><td>02.11.2021</td><td>EB</td><td>MJ</td></tr><tr><td>Phase</td><td>Issue</td><td>Date</td><td>Drawn</td><td>Checked</td></tr></table>					P1	REVA	02.11.2021	EB	MJ	Phase	Issue	Date	Drawn	Checked	Job Title: Hainsead, Lickers Lane								
P1	REVA	02.11.2021	EB	MJ																								
Phase	Issue	Date	Drawn	Checked																								
															Drawing Title: Contamination Issues Plan					The client must not amend any drawing, design or other intellectual property produced by E3P Ltd without permission in writing from E3P Ltd in advance of any amendments being made. In the event that such written permission is not obtained in advance of the amendments being made, E3P Ltd shall not be liable for any damage and/or losses occurring as a result of the amended drawing, design or intellectual property.								

APPENDIX IV E3P REMEDIATION/ VALIDATION CRITERIA

HUMAN HEALTH REMEDIATION TARGETS – LOW-RISE RESIDENTIAL END USE

DETERMINAND	UNITS	WITHIN 600 mm COVER SYSTEM (GARDEN)	HARD STANDING AND >600 mm OF COVER	PUBLIC OPEN SPACE 300 mm COVER	PUBLIC OPEN SPACE > 300 mm	PATH- WAY
Arsenic	mg/kg	37 ⁽ⁱ⁾	40 ⁽ⁱⁱ⁾	79 ⁽ⁱⁱⁱ⁾	170 ^(iv)	1
Cadmium	mg/kg	11 ⁽ⁱ⁾	85 ⁽ⁱⁱ⁾	120 ⁽ⁱⁱⁱ⁾	532 ^(iv)	1
Chromium (Hexavalent)	mg/kg	6 ⁽ⁱ⁾	6 ⁽ⁱⁱ⁾	7.7 ⁽ⁱⁱⁱ⁾	220 ^(iv)	1
Lead	mg/kg	200 ^(vi)	310 ^(vii)	630 ^(viii)	1300 ^(viii)	1
Elemental Mercury	mg/kg	1.2 ⁽ⁱ⁾	1.2 ⁽ⁱⁱ⁾	16 ⁽ⁱⁱⁱ⁾	30 ^(iv)	2
Nickel	mg/kg	130 ⁽ⁱ⁾	180 ⁽ⁱⁱ⁾	230 ⁽ⁱⁱⁱ⁾	800 ^(iv)	1
Selenium	mg/kg	250 ⁽ⁱ⁾	430 ⁽ⁱⁱ⁾	1100 ⁽ⁱⁱⁱ⁾	1800 ^(iv)	1
Copper	mg/kg	2400 ⁽ⁱ⁾	7100 ⁽ⁱⁱ⁾	12,000 ⁽ⁱⁱⁱ⁾	44,000 ^(iv)	1
Zinc	mg/kg	3700 ⁽ⁱ⁾	40,000 ⁽ⁱⁱ⁾	81,000 ⁽ⁱⁱⁱ⁾	170,000 ^(iv)	1
Phenol	mg/kg	120 ^{(i)(xi)}	440 ^{(xiv)(xi)}	440 ^{(iii)(xi)}	440 ^{(iv)(xi)}	2
Naphthalene	mg/kg	2.3 ^{(i)(xi)}	2.3 ^{(xiv)(xi)}	1200 ^{(iv)(xi)}	1200 ^{(iv)(xi)}	2
Acenaphthylene	mg/kg	170 ^{(i)(xi)}	500 ^(v)	15,000 ^{(iii)(xi)}	29,000 ^{(iv)(xi)}	3
Acenaphthene	mg/kg	210 ^{(i)(xi)}	500 ^(v)	15,000 ^{(iii)(xi)}	29,000 ^{(iv)(xi)}	1
Fluorene	mg/kg	170 ^{(i)(xi)}	500 ^(v)	9900 ^{(iii)(xi)}	20,000 ^{(iv)(xi)}	1
Phenanthrene	mg/kg	95 ^{(i)(xi)}	500 ^(v)	3100 ^{(iii)(xi)}	6200 ^{(iv)(xi)}	3
Anthracene	mg/kg	500 ^{(i)(xi)}	500 ^(v)	74,000 ^{(iii)(xi)}	150,000 ^{(iv)(xi)}	3
Fluoranthene	mg/kg	280 ^{(i)(xi)}	500 ^(v)	3100 ^{(iii)(xi)}	6300 ^{(iv)(xi)}	3
Pyrene	mg/kg	500 ^{(i)(xi)}	500 ^(v)	7400 ^{(iii)(xi)}	15,000 ^{(iv)(xi)}	3
Benzo(a)Anthracene	mg/kg	7.2 ^{(i)(xi)}	11 ^{(ii)(xi)}	29 ^{(iii)(xi)}	49 ^{(iv)(xi)}	3
Chrysene	mg/kg	15 ^{(i)(xi)}	30 ^{(ii)(xi)}	57 ^{(iii)(xi)}	93 ^{(iv)(xi)}	3
Benzo(b)Fluoranthene	mg/kg	2.6 ^{(i)(xi)}	3.9 ^{(ii)(xi)}	7.1 ^{(iii)(xi)}	13 ^{(iv)(xi)}	3
Benzo(k)Fluoranthene	mg/kg	77 ^{(i)(xi)}	110 ^{(ii)(xi)}	190 ^{(iii)(xi)}	370 ^{(iv)(xi)}	3
Benzo(a)Pyrene	mg/kg	2.2 ^{(i)(xi)}	3.2 ^{(ii)(xi)}	5.7 ^{(iii)(xi)}	11 ^{(iv)(xi)}	3
Indeno(123-cd)Pyrene	mg/kg	27 ^{(i)(xi)}	45 ^{(ii)(xi)}	82 ^{(iii)(xi)}	150 ^{(iv)(xi)}	3
Dibenzo(a,h)Anthracene	mg/kg	0.24 ^{(i)(xi)}	0.31 ^{(ii)(xi)}	0.57 ^{(iii)(xi)}	1.1 ^{(iv)(xi)}	3
Benzo(ghi)Perylene	mg/kg	320 ^{(i)(xi)}	360 ^{(ii)(xi)}	640 ^{(iii)(xi)}	1400 ^{(iv)(xi)}	3
TPH C ₅ -C ₆ (aliphatic)	mg/kg	42 ^{(i)(xi)}	42 ^{(ii)(xi)}	42 ^{(iii)(xi)}	10,000 ^{(xiv)(xi)}	2
TPH C ₆ -C ₈ (aliphatic)	mg/kg	100 ^{(i)(xi)}	100 ^{(ii)(xi)}	100 ^{(iii)(xi)}	10,000 ^{(xiv)(xi)}	2
TPH C ₈ -C ₁₀ (aliphatic)	mg/kg	27 ^{(i)(xi)}	27 ^{(ii)(xi)}	27 ^{(iii)(xi)}	10,000 ^{(xiv)(xi)}	2
TPH C ₁₀ -C ₁₂ (aliphatic)	mg/kg	130 ^{(i)(xi)}	130 ^{(ii)(xi)}	130 ^{(iii)(xi)}	10,000 ^{(xiv)(xi)}	2
TPH C ₁₂ -C ₁₆ (aliphatic)	mg/kg	1000 ^{(xiv)(xi)}	1000 ^{(xiv)(xi)}	1000 ^{(xiv)(xi)}	10,000 ^{(xiv)(xi)}	1
TPH C ₁₆ -C ₂₁ (aliphatic)	mg/kg	1000 ^{(xiv)(xi)}	1000 ^{(xiv)(xi)}	1000 ^{(xiv)(xi)}	10,000 ^{(xiv)(xi)}	1
TPH C ₂₁ -C ₃₅ (aliphatic)	mg/kg					1
TPH C ₅ -C ₇ (aromatic)	mg/kg	70 ^{(i)(xi)}	370 ^{(ii)(xi)}	370 ^{(iii)(xi)}	10,000 ^{(xiv)(xi)}	2
TPH C ₇ -C ₈ (aromatic)	mg/kg	130 ^{(i)(xi)}	860 ^{(ii)(xi)}	860 ^{(iii)(xi)}	10,000 ^{(xiv)(xi)}	2
TPH C ₈ -C ₁₀ (aromatic)	mg/kg	34 ^{(i)(xi)}	47 ^{(ii)(xi)}	47 ^{(iii)(xi)}	10,000 ^{(xiv)(xi)}	2
TPH C ₁₀ -C ₁₂ (aromatic)	mg/kg	74 ^{(i)(xi)}	250 ^{(ii)(xi)}	250 ^{(iii)(xi)}	10,000 ^{(xiv)(xi)}	2



TPH C₁₂-C₁₆ (aromatic)	mg/kg	140 ^{(i)(xi)}	1800 ^{(ii)(xi)}	1800 ^{(ii)(xi)}	10,000 ^{(xiv)(xi)}	1
TPH C₁₆-C₂₁ (aromatic)	mg/kg	260 ^{(i)(xi)}	1900 ^{(ii)(xi)}	1900 ^{(ii)(xi)}	10,000 ^{(xiv)(xi)}	1
TPH C₂₁-C₃₅ (aromatic)	mg/kg	1000 ^{(xiv)(xi)}	1900 ^{(ii)(xi)}	1900 ^{(ii)(xi)}	10,000 ^{(xiv)(xi)}	1
Asbestos	Fibres Volume Weight (%)	NFD	0.001%	NFD	0.001	4

Notes 1

NFD = No Fibres Detected

Asbestos will be screened visually on site by a qualified environmental consultant and where potential ACM is identified, representative samples will be subject to quantitative analysis of % volume by weight.

Should any ACM be identified within the soil matrices, further detailed % assessment would be required when the reported laboratory result exceeds the limit of detection for the analytical method at 0.01% by volume (weight).

Notes 2

Excludes matrices where free product is observed.

No viable exposure pathway beneath hardstanding and cover system.

Notes 3

Main exposure pathways: 1 = soil ingestion, 2 = vapour inhalation (indoor), 3 = dermal contact and ingestion, 4 = dust inhalation.

Abbreviations: GAC = general assessment criteria, n = number of samples, MC = maximum concentration, N/A = Not Applicable (no exceedance of assessment criteria), Loc of MC = location of exceedances.

- i. Value derived from LQM Sutable 4 Use Levels (S4ULs) for residential end use with plant uptake.
- ii. Value derived from LQM Sutable 4 Use Levels (S4ULs) for residential end use without plant uptake – these levels used below 600 mm cover system within residential gardens as soils will be present within a residential setting yet soils will not be disturbed and garden plants will not reach these soils.
- iii. Value derived from LQM Sutable 4 Use Levels (S4ULs) for public open space (POS) residential.
- iv. Value derived from LQM Sutable 4 Use Levels (S4ULs) for public open space (POS) park – these levels used below 300 mm POS cover system as soils will not be disturbed by any future site users and exposure to these soils will be similar to a park end use.
- v. Value derived from LQM Sutable 4 Use Levels (S4ULs) alongside assessment with WM3 to ensure that materials remaining on site do not exceed the WM3 toxicity criteria for hazardous waste.
- vi. Value derived from Category 4 Screening Levels (C4SL) for residential land use with homegrown produce.
- vii. Value derived from Category 4 Screening Levels (C4SL) for residential land use without homegrown produce.
- viii. Value derived from Category 4 Screening Levels (C4SL) for public open space (POS) residential.
- ix. Value derived from Category 4 Screening Levels (C4SL) for public open space (POS) park.
- x. Mercury – based on elemental mercury.
- xi. PAH and TPH levels used are for 1% SOM.
- xii. Xylenes based on p-xylene (o-xylene 2600 mg/kg, m-xylene 3500 mg/kg) and is capped by its solubility.
- xiii. Value derived from LQM Sutable 4 Use Levels (S4ULs) for residential end use with plant uptake due to the volatilisation risk.
- xiv. BTEX is not SOM-related due to inhalation pathway.



REMEDIATION TARGETS – COMPARISON OF GROUNDWATER / LEACHATE ANALYSIS WITH TIER 1 SCREENING LEVELS

DETERMINAND	UNIT	EQS SCREENING VALUE ^{1, 2, 3}		DWS ^{3,4,5}
		AA	MAC	
Arsenic	µg/l	50	–	10
Cadmium	µg/l	0.08-0.25	0.45-1.5	5
Chromium (VI)	µg/l	3.4	–	–
Chromium (III)	µg/l	4.7	–	50
Copper	µg/l	1	–	2000
Total Cyanide	µg/l	1	–	50
Lead	µg/l	1.2	14	10
Mercury	µg/l	–	0.07	1.0
Nickel	µg/l	4	34	20
Selenium	µg/l	–	–	10
Zinc	µg/l	10.9	–	–
pH		6–9		
Naphthalene	µg/l	2	130	10*
Anthracene	µg/l	0.1	0.1	
Benzo[b]fluoranthene	µg/l	0.00017*	0.017	
Benzo[k]fluoranthene	µg/l	0.00017*	0.017	
Benzo(a)pyrene	µg/l	0.00017*	0.27	
Indeno(123-cd)pyrene	µg/l	0.00017*	5*	
Benzo(ghi)pyrene	µg/l	0.00017*	5*	
Fluoranthene	µg/l	0.0063	0.12	
Benzo(ghi)perylene	µg/l	1.7–4	8.2–3	
TPH C5-C6 (benzene)	µg/l	10	50	1
TPH C6-C8 (toluene)	µg/l	74	–	700
TPH C8-C10 (ethyl benzene)	µg/l	20	–	300
TPH C10-C12 (xylene)	µg/l	30	–	500
TPH C12-C16	µg/l	2	130	90 ⁵
TPH C16-C35	µg/l	50#	50#	90 ⁵
TPH C5-C6	µg/l	–	–	15000
TPH C6-C8	µg/l	–	–	15000
TPH C8-C10	µg/l	–	–	300
TPH C10-C12	µg/l	–	–	300
TPH C12-C16	µg/l	–	–	300



Land South of Lickers Lane

Remediation and Enabling Works Strategy

August 2022

DETERMINAND	UNIT	EQS SCREENING VALUE ^{1, 2, 3}		DWS ^{3,4,5}
		AA	MAC	
TPH C16 – C21	µg/l	–	–	300**
TPH C21-C35	µg/l	–	–	300**
Tetrachloroethylene	µg/l	0.4	–	10
Trichloroethylene	µg/l	10	–	10
Trichlorobenzene	µg/l	0.4	–	–
Trichloromethane	µg/l	2.5	–	–
Dichloromethane	µg/l	20	–	200
Carbon Tetrachloride	µg/l	12	–	3
Vinyl Chloride	µg/l	–	–	0.3

Notes

Solubility <0.01µg/l

AA – Annual Average

MAC- Maximum Admissible Concentration

* Polyaromatic hydrocarbons (PAH) - Benzo(a)pyrene (BaP), Benzo(b)fluoranthene, Benzo(k)fluoranthene, Benzo(g,h,i)-perylene and Indeno(1,2,3-cd)-pyrene. Benzo(a)pyrene can be considered as a marker for the other PAHs, hence only benzo(a)pyrene needs to be monitored for comparison with the biota EQS or the corresponding AA-EQS in water

** There are no WHO Guideline Values for aliphatic fractions C16-C21 and C21-C35, therefore the guideline value for aliphatic fractions inclusive of C8-C16 (300µg/l) has been applied.

1. The Water Environment (Water Framework Directive) (England and Wales) (Amendment) Regulations (2015)
2. Directive establishing a framework for Community action in the field of water policy (Water Framework Directive)
3. Council Directive on pollution caused by certain dangerous substances discharged into the aquatic environment of the Community (Dangerous Substances Directive) - List II substances
4. Council Directive on the quality of water intended for human consumption (Drinking Water Directive)
5. WHO Guidelines for Drinking Water Quality. Third edition (2004)



APPENDIX V

E3P MATERIAL IMPORT CRITERIA

SITE OF IMPORTATION ADDRESS		E3P +44 (0) 161 707 9612 info@e3p.co.uk 
Client		
Main Contractor		
Earthworks Contractor		
Haulier		
Date of Planned Import		
Overview of Planned Material Import		
Material Source (Site of Origin) and Postcode		
Site Investigation Report	Report Title and Reference: Date: Information Supplied By:	
Reason for Generation of Excess Material at Site of Origin		
Chemical Test Results for Stockpile at Site of Origin	Date: Laboratory Certificate Ref: Organisation Responsible for Stockpile Sampling:	
Geotechnical Material Classification and Testing	Delete as Appropriate: Class 1 / Class 2 / Class 6 / Topsoil	
Pictures of Material Stockpile Pending Transportation	Delete as Appropriate: Yes / No	
Person or Organisation Responsible for Ensuring Quality Control at Site of Origin		
Quantity of Material to Be Imported (m³)		
Proposed Area of Deposition (Site of Reuse)		
Waste Exemption/Permit or CL:AIRE MMP		Delete as Appropriate: U1 Standard Rules / CL:AIRE MMP (Direct Transfer) / Bespoke



APPENDIX VI CONTRACTOR PRE- COMMENCEMENT CHECK SHEET

GEOTECHNICAL ENABLING WORKS PRE-START FORM

Prior to the commencement of any site remediation or enabling works, this form will be completed by E3P, in the presence of the appointed contractor, to ensure that all pertinent remediation and enabling works activities are fully discussed and understood.

Activity	Testing Responsibility	Contractors Method Statement Required (Y/N)	Comment/Action
Deployment of Environmental Permit			Ref No:
Deployment of LAPC Part B – Mobile Plant Permit			Ref No:
CL:AIRE MMP and Qualified Person Declaration			Ref No:
Identification of All Invasive Plant Species and Production of Eradication Plan with Appropriate Supervision by Specialist			Appointed specialist:
Removal of All Vegetation			Note disposal location:
Removal of All Root Bulbs and Root Networks			Note disposal location:
Identification of Contamination Hotspots, Removal of Material and Stockpile			Rationale:
Legislatively Compliant Procedure to Deal with Contamination Excavated from Hotspot			Rationale:
Processing and Recycling of Aggregate with Geotechnical and Chemical Validation Testing			Note stockpile location and anticipated volume:
Stockpiling of Subsoil and Certification of Suitability for Reuse			Stockpile location:
Decommission of All Redundant Drainage Infrastructure			
Decommission of All Former Interceptors			
Decommission of All Former Above- and Below-Ground Tanks			
Removal of All Asbestos to a Licensed Facility			
Engineering of Plots for Shallow Spread Foundation in Accordance with E3P Geotechnical Specification			Plot Numbers



Land South of Lickers Lane

Remediation and Enabling Works Strategy

July 2022

Activity	Testing Responsibility	Contractors Method Statement Required (Y/N)	Comment/Action
Engineering of Plots for VSC in Accordance with E3P Geotechnical Specification			Plot Numbers.
Engineering of Plots for Pile Foundation in Accordance with E3P Geotechnical Specification			Plot Numbers
Engineering of Plots for Raft Foundation in Accordance with E3P Geotechnical Specification			Plot Numbers
Stockpiling of Topsoil and Certification of Suitability for Reuse			Stockpile location
Engineering of Highways Bulk Upfill in Accordance with E3P Specification with Compliant Validation Testing			Upfill specification
Engineering of Highways Subgrade in Accordance with E3P Specification with Compliant Validation Testing			Upfill specification
Engineering of Highways Capping in Accordance with E3P Specification with Compliant Validation Testing			Upfill specification
Cut-and-Fill the Development Site to Clients' Required Elevation with As-Built Survey			Required formation elevations



APPENDIX VII CONTRACTOR COMPLETION CHECK SHEET

GEOTECHNICAL ENABLING WORKS COMPLETION FORM

Upon completion of all site remediation and enabling works, this form will be completed by E3P, in the presence of the appointed contractor, to ensure that all pertinent geotechnical enabling works activities are complete or, where a deviation from the specification has occurred, all future limitations and issues are documented for the client's records.

Activity	Complete			Signature
	Yes	No	N/A	(initial)
Eradication of all invasive plant species				
Removal of all vegetation				
Removal of all root bulbs and root networks				
Stockpiling of topsoil and certification of suitability for reuse				
Stockpiling of subsoil and certification of suitability for reuse				
Stockpile all recycled aggregate with geotechnical and chemical validation testing				
Removal of all relict foundations and infrastructure in their entirety				
Decommission of all redundant drainage infrastructure				
Decommission of all former interceptors				
Decommission of all former above- and below-ground tanks				
Removal of all waste materials to a licensed facility				
Removal of all asbestos to a licensed facility				
Engineering of all plots for shallow spread foundation in accordance with E3P Geotechnical Specification				
Engineering of all plots for VSC in accordance with E3P Geotechnical Specification				
Engineering of all plots for pile foundation in accordance with E3P Geotechnical Specification				
Engineering of all plots for raft foundation in accordance with E3P Geotechnical Specification				
Engineering of highways bulk upfill in accordance with E3P Specification with compliant validation testing				
Engineering of highways subgrade in accordance with E3P Specification with compliant validation testing				
Engineering of highways capping in accordance with E3P Specification with compliant validation testing				
Cut-and-fill the development site to client's required elevation with as-built survey				



POST-REMEDIATION AND ENABLING LIMITATIONS

All and every deviation from the approved specification for works should be documented by the remediation and enabling works contractor below.



