


# LAKESIDE PHASE 01


# DRAFT CONSTRUCTION PROGRAMME

## Filter: None

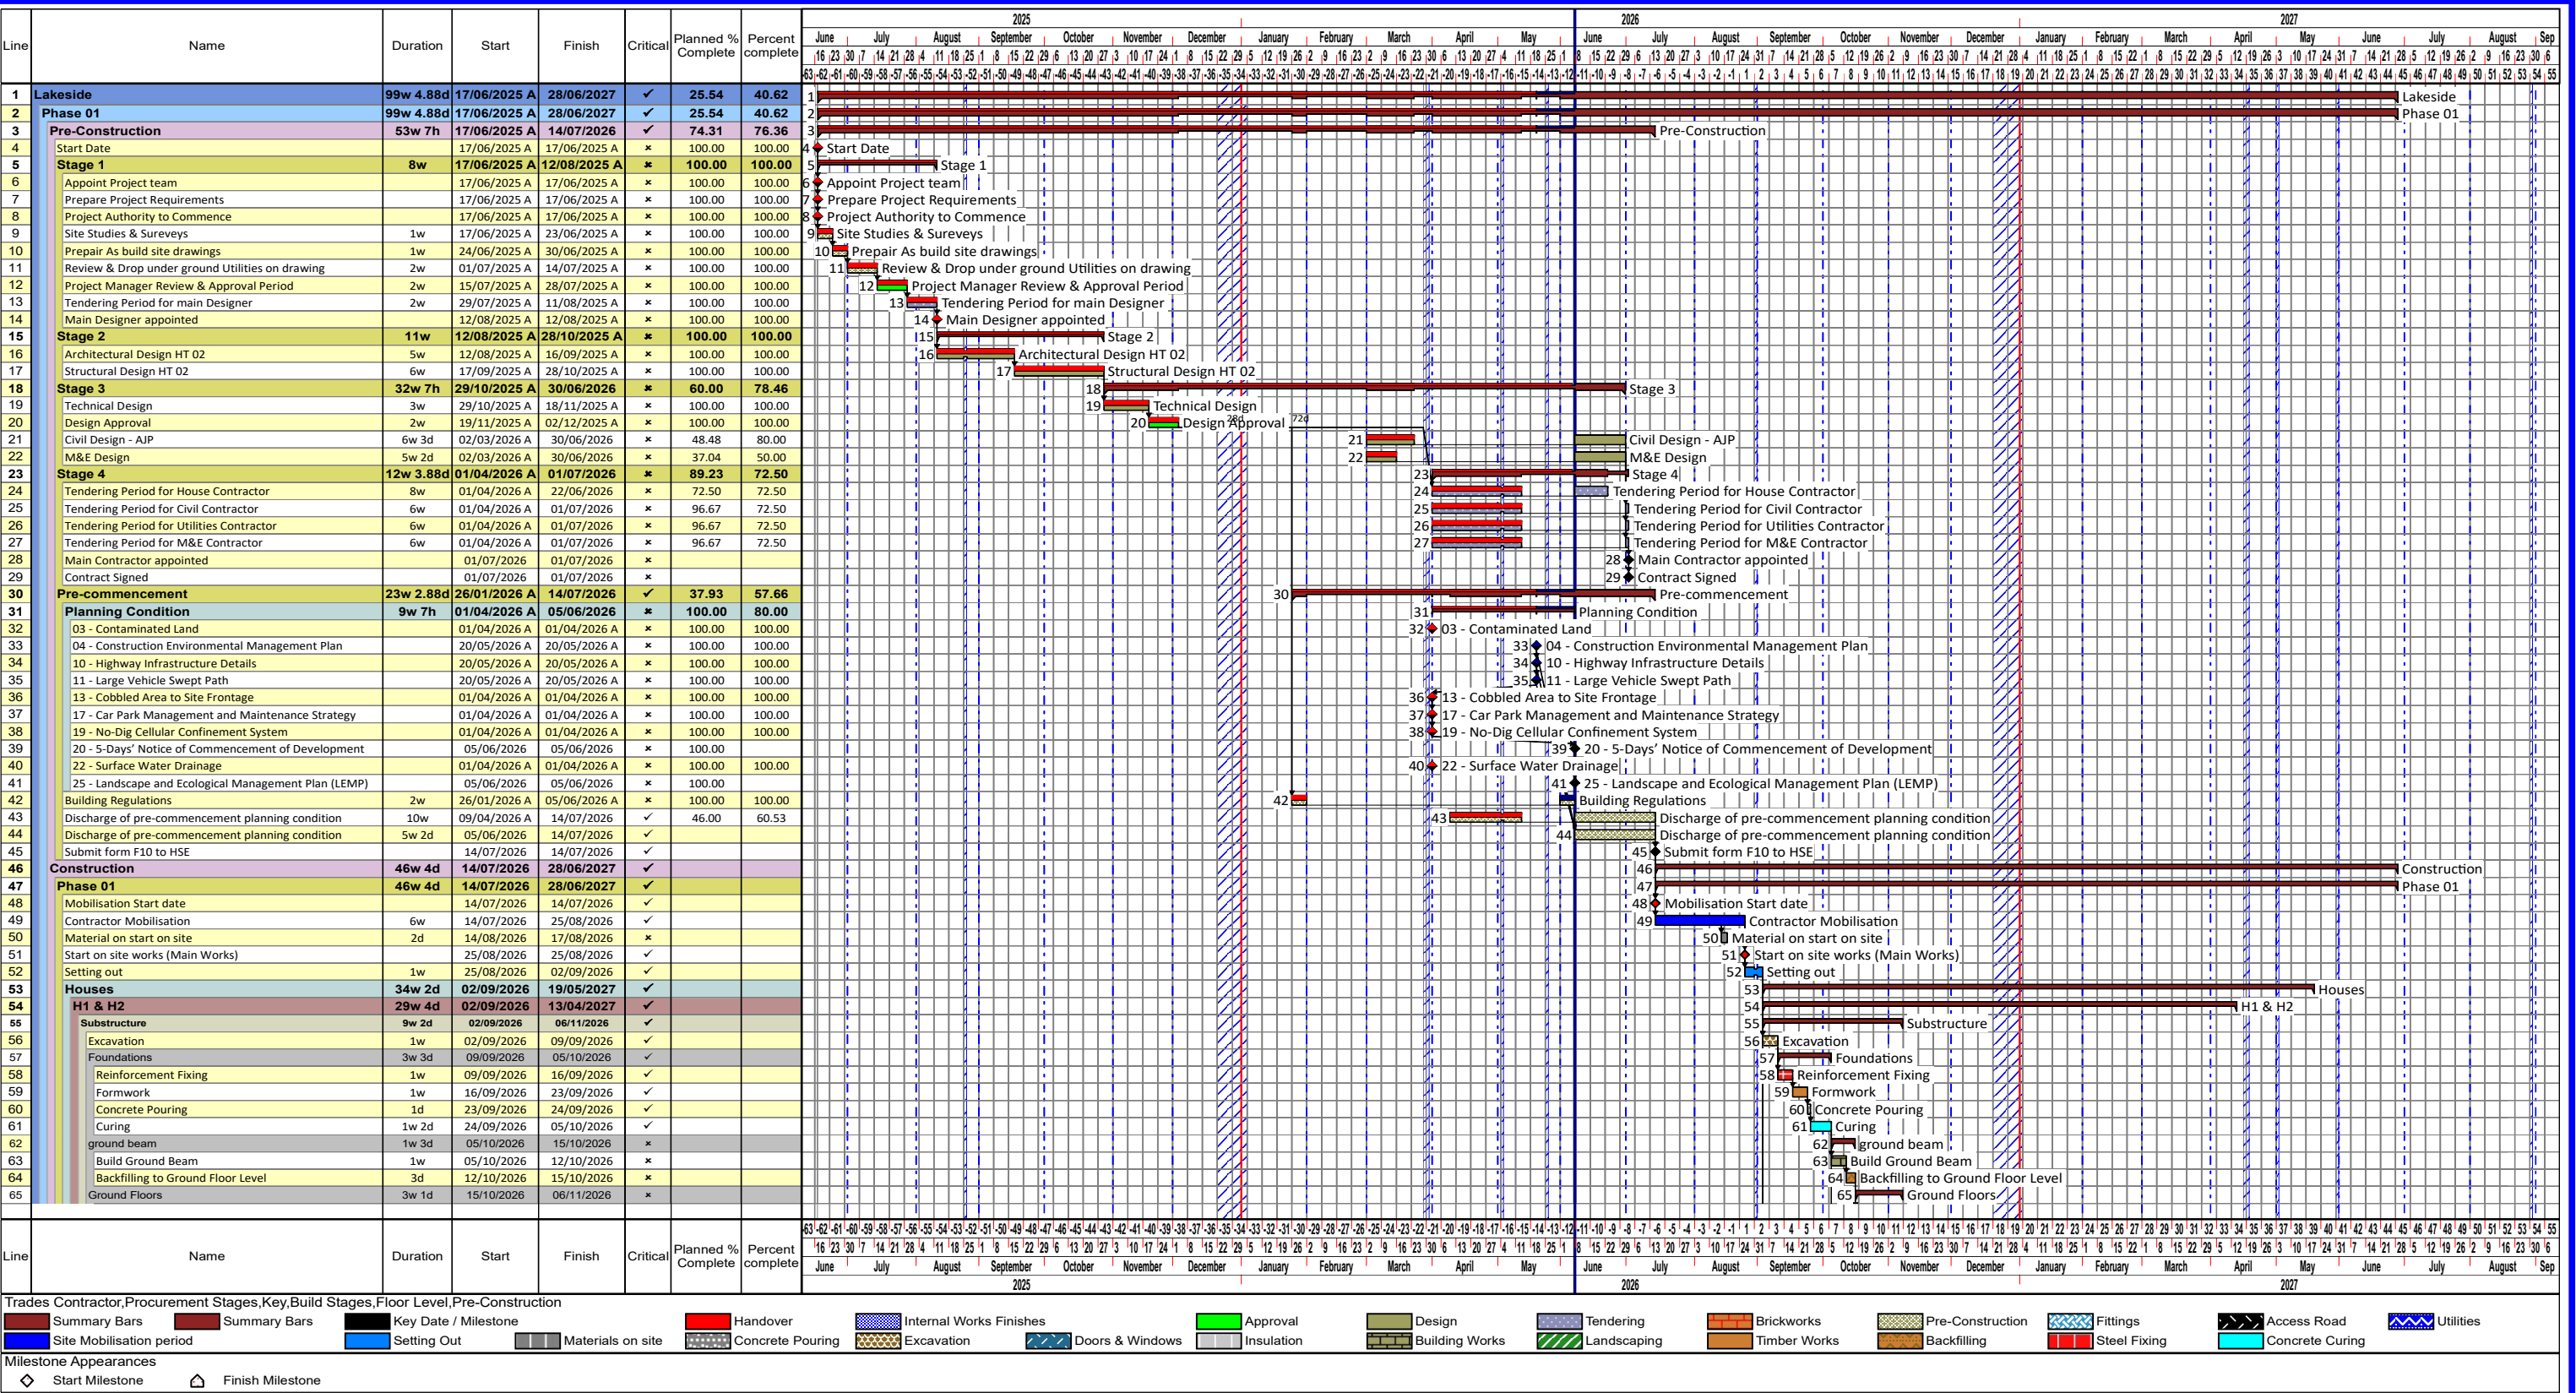

|                                                                                                                                                           |                                                                                      |                        |                                 |                          |                   |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------|------------------------|---------------------------------|--------------------------|-------------------|
| <b>MAC Roofing &amp; Contracting</b><br><br><b>Unit 1 Lumina Buisness Park</b><br><b>Martindale Road</b><br><b>Bromborough</b><br><b>Wirral, CH62 3PT</b> |  | <b>Programme No.</b>   | <b>Lakeside Phase 01 Rev: B</b> | <b>Issued:</b>           | <b>22/06/2026</b> |
|                                                                                                                                                           |                                                                                      | <b>Revision Notes</b>  |                                 | <b>Revised:</b>          | <b>22/06/2026</b> |
|                                                                                                                                                           |                                                                                      | <b>Project Manager</b> |                                 | <b>Planner:</b>          | <b>AM</b>         |
|                                                                                                                                                           |                                                                                      | <b>Page No</b>         | 1 of 3                          | <b>Print Date:</b>       | <b>22/06/2026</b> |
|                                                                                                                                                           |                                                                                      | <b>Filter</b>          | None                            | <b>Percent Complete:</b> | <b>25.54%</b>     |

**Filter: None**



**Filter: None**

|                                                                                                                                                           |                                                                                      |                        |                                 |                          |            |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------|------------------------|---------------------------------|--------------------------|------------|
| <b>MAC Roofing &amp; Contracting</b><br><br><b>Unit 1 Lumina Buisness Park</b><br><b>Martindale Road</b><br><b>Bromborough</b><br><b>Wirral, CH62 3PT</b> |  | <b>Programme No.</b>   | <b>Lakeside Phase 01 Rev: B</b> | <b>Issued:</b>           | 22/06/2026 |
|                                                                                                                                                           |                                                                                      | <b>Revision Notes</b>  |                                 | <b>Revised:</b>          | 22/06/2026 |
|                                                                                                                                                           |                                                                                      | <b>Project Manager</b> |                                 | <b>Planner:</b>          | AM         |
|                                                                                                                                                           |                                                                                      | <b>Page No</b>         | 3 of 3                          | <b>Print Date:</b>       | 22/06/2026 |
|                                                                                                                                                           |                                                                                      | <b>Filter</b>          | None                            | <b>Percent Complete:</b> | 25.54%     |
