



Report No: LTM0207.MS.01

Date: 19/03/2021

Project: 29 Edenhurst Avenue, Liverpool, Merseyside, L16 2LA

BS 5837:2012 Method Statement.

Inspection Record.

Date of Inspection	Surveyor
16/03/2021	Matthew Lally. FdSc MArborA

Lally Tree Management.

36 Goldsworthy Road, Urmston, Manchester, M41 8US

[T] 07305 740120 [E] matt@lallytreemanagement.co.uk [W] <https://www.lallytreemanagement.co.uk/>

This report is the property of Lally Tree management. This report may only be reproduced or disclosed to third parties with express written consent from Lally Tree Management.

Revision	Date	Prepared by	Status
Final	19/03/2021	M. Lally	Final

Contents

1.0	Discussion.....	4
2.0	Method Statement.....	5
2.1	Tree Works	5
2.2	Protective Fencing	5
2.3	Additional Precautions Outside Fenced Areas.....	5
2.4	Summary of Methodology for the Protection of the Trees	6
Appendix One Tree Plan		

1.0 Discussion

- 1.1 The majority of the root system of a tree is in the surface 600mm of the soil extending radially for distances frequently in excess of the trees height. Beyond the main structural roots (close to the base of the trunk), the root system rapidly sub-divides into smaller diameter roots: off this main system, a mass of fine roots develops.
- 1.2 The shape of the main structural roots develops in response to the need for the tree to have physical stability. Beyond these major roots, root growth and development is influenced by the availability of water and nutrients. Unless conditions are uniform around the tree, which would be unusual, the extent of the root system will be very irregular and difficult to predict. It will not generally show the symmetry seen in the branch system.
- 1.3 The parts of the root system, which are active in water and nutrient uptake, are very fine, typically less than 0.5mm diameter. They are short lived, developing in response to the needs of the tree, with the majority dying each winter. It is *essential* that conditions in the soil remain conducive to the healthy growth of these fine roots so that the water and nutrients necessary for healthy tree growth can be absorbed.
- 1.4 All parts of the root system, but especially the fine roots, are vulnerable to damage. Once they are damaged, water and nutrient uptake will be restricted until new roots have regenerated. Vigorous young trees will be capable of rapid regeneration, but over mature trees will respond slowly, *if at all*.
- 1.5 In order to live and grow, roots need oxygen from the soil. Respiration by the roots and other soil organisms depletes this oxygen and increases carbon dioxide levels in the soil; a correct balance of these gases is normally maintained by diffusion between the soil and the atmosphere. Anything, which disturbs this balance, will affect the condition of the root system.
- 1.6 The factors that most commonly affect this diffusion adversely, and therefore damage roots, are the following: -
 - a) Compaction of the ground, which reduces the space between soil particles. This is particularly important on clay soils. A single passage by heavy equipment on clay soils or storage of heavy materials can cause significant damage.
 - b) Changing soil levels, even for a few weeks.
 - c) Covering the root area with impervious surfaces.
 - d) A rise in the level of the water table. Roots can tolerate submersion for short periods. But a permanent rise will deplete the soil of oxygen.
- 1.7 Serious damage is often caused during preliminary site works by stripping the topsoil. For this reason, such works should be avoided until protective fencing has been erected.
- 1.8 Excavations in the rooting area can sever roots. As the majority of roots are in the surface 600mm, even shallow excavations can cause damage.

- 1.9 Excavations for foundations, landscaping or service trenches are usually sufficiently deep to sever most of the roots, and it should therefore be assumed that all parts of the root system beyond the excavation would no longer serve the tree.
- 1.10 Excavation or soil stripping which sever or damage the roots may impair the stability of the tree and make it dangerous.

2.0 Method Statement

Before any form of development commences on the site the following works should be undertaken: -

2.1 Tree Works

Tree No.	Proposed Works
T1	No Works Required
G1	No Works Required
T2	No Works Required
G3	No Works Required
T4	No Works Required
T5	No Works Required
G6	No Works Required

2.2 Protective Fencing

- 2.2.1 Due to all trees being off site and behind an existing boundary fence with no RPAs present within the confines of the site, it is felt that protective fencing is not required on this occasion.

2.3 Additional Precautions Outside Fenced Areas

- 2.3.1 Oil, bitumen, cement or other material likely to cause damage to the tree will not be stacked or discharged within 10m of the trees stem or within the protective area. Also, materials in general will not be stacked or discharged within the exclusion zone.
- 2.3.2 Concrete mixing and washing will not be carried out within 10m of any retained trees.
- 2.3.3 Fires will not be lit beneath the foliage or in a position where the flames could extend to within 5m of the foliage, branches or trunk. If the fire is large, then this may necessitate a distance of at least 20m.
- 2.3.4 Trees that are to be retained will not be used as anchorage for equipment.
- 2.3.5 Notice boards, telephone cables, or other services will not be attached to any part of the retained tree.

- 2.3.6 Care should be taken when using cranes or other equipment near the canopy of the retained trees. Also, any trees to be felled in proximity to the retained trees should be done so with particular care.


2.4 Summary of Methodology for the Protection of the Trees

1: Implementation of Development

Appendix One

Tree Plan



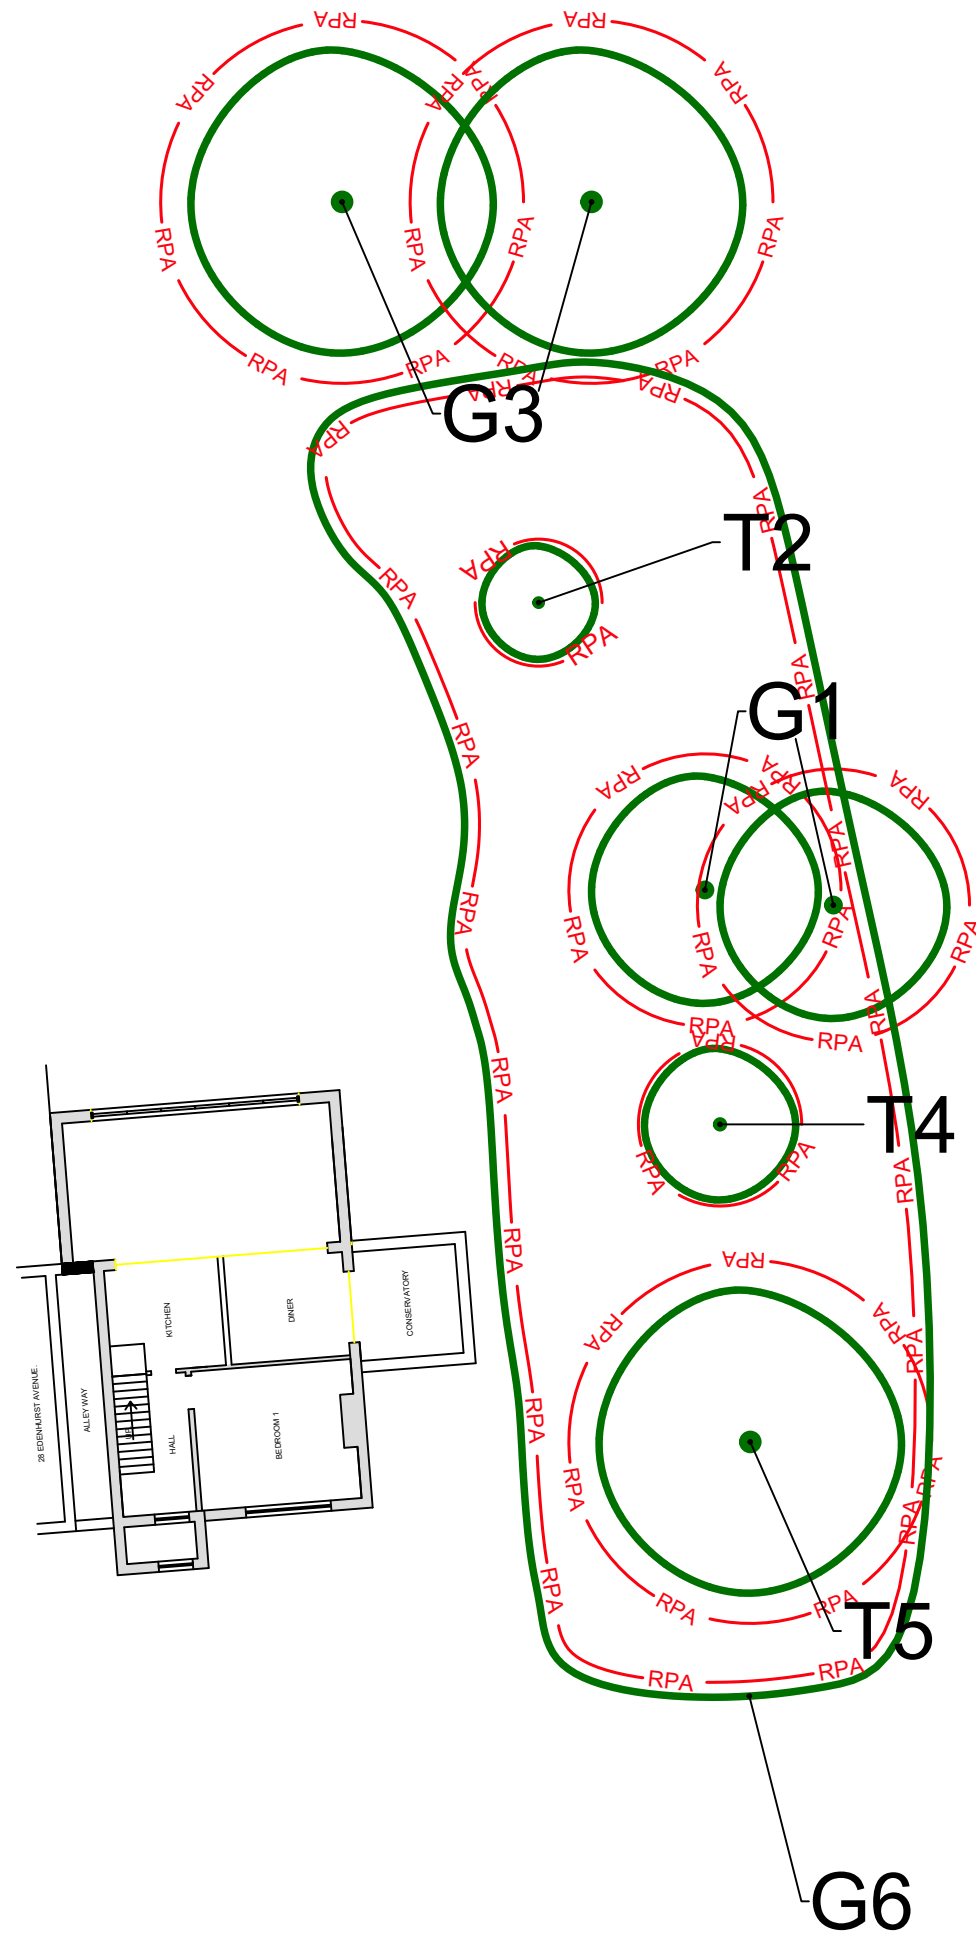

Do not scale this drawing (printed or electronic version).

Contractors must check all dimensions from site

This drawing is for use on this site only and should be used in conjunction with all relevant consultants drawings..

LEGEND

 Retained Trees

 Removed Trees

 Root Protection Areas





Scale:	1:200@A3	Date:	19/03/2021
Job:	LTM0207.Edenhurst		
Address	29 Edenhurst Avenue, Liverpool, L16 2LA		
Client:	Karen Worthington		
Drawing Number:	LTM0207.TPP.01		
Drawn by:	Matthew Lally		
TREE PROTECTION PLAN			
