



Project

Project Name: DJL CONSTRUCTION - 35 WILSON ROAD HUYTON

Project Date: 11/08/2026

Inspection Standard: MSCC5 Sewers & Drainage GB (SRM5 Scoring)

Table of Contents

Project Name	Project Number	Project Date
DJL CONSTRUCTION - 35 WILSON ROAD HUYTON		11/08/2026

Project Information	P-1
Section Item 1: F3 > F4 (F3X)	1
Section Item 2: F4 > F5 (F4X)	3
Section Item 3: SW MH > DOWNSTREAM (SW MHX)	4
Section Item 4: UNBURIEDMH > DOWNSTREAM (UNBURIEDMHX)	5

Project Information

Project Name	Project Number	Project Date
DJL CONSTRUCTION - 35 WILSON ROAD HUYTON		11/08/2026

Client

Company: DJL CONSTRUCTION LTD
Street: UNIT 5A CHAPEL HILL INDUSTRIAL ESTATE
Town or City: LONGRIDGE
Post Code: PR3 3BU

Site

Company: DJL CONSTRUCTION
Street: 35 WILSON ROAD
Town or City: HUYTON

Contractor

Company: C.J LYON & SONS LTD
Contact: NICOLA CREAMER
Street: BENTLEY NURSERIES
Town or City: BENTLEY LANE
County: MAWDESLEY
Post Code: L40 3SN
Phone: 01257 462986

Section Inspection - 11/08/2026 - F3X

Item No. 1	Insp. No. 1	Date 11/08/26	Time 9:21	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F3X
Operator M. Glover		Vehicle Not Specified		Camera Crawler Unit	Preset Length Not Specified	Legal Status Public Sewer	Alternative ID Not Specified

Town or Village:	Huyton	Inspection Direction:	Downstream	Upstream Node:	F3
Road:	35 Wilson Road	Inspected Length:	22.00 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	22.00 m	Downstream Node:	F4
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul		Pipe Shape:	Circular	
Type of Pipe:	Gravity drain/sewer		Dia/Height:	150 mm	
Flow Control:	No flow control		Material:	Vitrified clay	
Year Constructed:	Not Specified		Lining Type:	No Lining	
Inspection Purpose:	Routine inspection		Lining Material:	No Lining	
Comments:	Blistered at 3.50m & fractured at 13.40m				
Recommendations:					

Scale: 1:191 Position [m] Code Observation MPEG Photo Grade

The diagram shows a vertical pipe section with two manholes at the ends. The top manhole is labeled 'F3' and the bottom manhole is labeled 'F4'. The pipe is represented by a vertical grey bar. Depth markers are indicated by horizontal lines extending from the pipe to the right, with corresponding depth values in meters. Observations are listed in a table to the right of the pipe, with color-coded text matching the observation details. A blue arrow points downwards on the left side of the pipe, indicating the direction of flow.

Depth: m	Code	Observation	MPEG	Photo	Grade
0.00	MH	Start node, manhole, reference: F3	00:00:00		
0.00	WL	Water level, 5% of the vertical dimension			
3.50	GP	General photograph taken at this point: Blisters in pipe	00:00:22	1	
13.40	FC	Fracture, circumferential from 7 o'clock to 8 o'clock	00:01:07	2	3 / 2
21.80	LR	Line deviates right	00:02:21		
22.00	MHF	Finish node, manhole, reference: F4	00:02:23		

Depth: m

F4

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	40.0	1.8	40.0	3.0	1	1.0	0.0	1.0	2.0

Section Pictures - 11/08/2026 - F3X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
1	Downstream	F3X		



1, 00:00:22, 3.50 m
General photograph taken at this point, Blisters in pipe



2, 00:01:07, 13.40 m
Fracture, circumferential from 7 o'clock to 8 o'clock

Section Inspection - 11/08/2026 - F4X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
2	1	11/08/26	9:22	Not Specified	No Rain Or Snow	Yes	F4X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
M. Glover		Not Specified		Crawler Unit	Not Specified	Public Sewer	Not Specified

Town or Village:	Huyton	Inspection Direction:	Downstream	Upstream Node:	F4
Road:	35 Wilson Road	Inspected Length:	30.90 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	30.90 m	Downstream Node:	F5
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul		Pipe Shape:	Circular	
Type of Pipe:	Gravity drain/sewer		Dia/Height:	225 mm	
Flow Control:	No flow control		Material:	Vitrified clay	
Year Constructed:	Not Specified		Lining Type:	No Lining	
Inspection Purpose:	Routine inspection		Lining Material:	No Lining	
Comments:	None				
Recommendations:					


Scale:	1:268	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m F4 0.00 MH Start node, manhole, reference: F4 00:00:00 0.00 WL Water level, 5% of the vertical dimension 30.90 MHF Finish node, manhole, reference: F5 00:05:12 F5 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Section Inspection - 11/08/2026 - SW MHX

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
3	1	11/08/26	9:23	Not Specified	No Rain Or Snow	Yes	SW MHX
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
M. Glover		Not Specified		Crawler Unit	Not Specified	Public Sewer	Not Specified

Town or Village:	Huyton	Inspection Direction:	Downstream	Upstream Node:	SW MH
Road:	35 Wilson Road	Inspected Length:	82.90 m	Upstream Pipe Depth:	5.500 m
Location:	Road	Total Length:	82.90 m	Downstream Node:	DOWNSTREAM
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water		Pipe Shape:	Circular	
Type of Pipe:	Gravity drain/sewer		Dia/Height:	750 mm	
Flow Control:	No flow control		Material:	Concrete	
Year Constructed:	Not Specified		Lining Type:	No Lining	
Inspection Purpose:	Routine inspection		Lining Material:	No Lining	
Comments:	None				
Recommendations:					

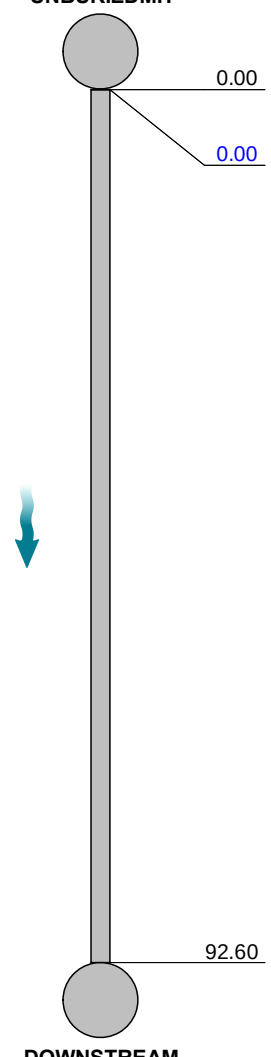
Scale:	1:718	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 5.50 m SW MH 							
		0.00	MH	Start node, manhole, reference: SW MH	00:00:00		
		0.00	WL	Water level, 5% of the vertical dimension			
		82.90	MHF	Finish node, manhole, reference: DOWNSTREAM	00:11:35		
DOWNSTREAM Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Section Inspection - 11/08/2026 - UNBURIEDMHX

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
4	1	11/08/26	9:26	Not Specified	No Rain Or Snow	Yes	UNBURIEDMHX
Operator M. Glover		Vehicle Not Specified		Camera Crawler Unit	Preset Length Not Specified	Legal Status Public Sewer	Alternative ID Not Specified

Town or Village:	Huyton	Inspection Direction:	Downstream	Upstream Node:	UNBURIEDMH
Road:	35 Wilson Road	Inspected Length:	92.60 m	Upstream Pipe Depth:	4.850 m
Location:	Road	Total Length:	92.60 m	Downstream Node:	DOWNSTREAM
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water		Pipe Shape:	Circular	
Type of Pipe:	Gravity drain/sewer		Dia/Height:	750 mm	
Flow Control:	No flow control		Material:	Concrete	
Year Constructed:	Not Specified		Lining Type:	No Lining	
Inspection Purpose:	Routine inspection		Lining Material:	No Lining	
Comments:	None				
Recommendations:					

Scale:	1:802	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 4.85 m UNBURIEDMH 							
		0.00	MH	Start node, manhole, reference: UNBURIED MH	00:00:00		
		0.00	WL	Water level, 5% of the vertical dimension			
		92.60	MHF	Finish node, manhole, reference: DOWNSTREAM	00:08:50		
DOWNSTREAM Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0
